


ID	Task Name	Duration	Start	Baseline Finish	Finish	% Complete	Predecessors	Resource Names	18 Mar '13							25 Mar '13			
									M	T	W	T	F	S	S	M	T	W	T
1	Overall Performance Assurance Plan	727 days	Wed 20/03/13	Wed 31/12/14	Thu 31/12/15	29%													
2	Independent Study of Performance Risk	530 days	Wed 20/03/13	Wed 31/12/14	Tue 31/03/15	65%													
3	✓ Create scope for an independent study of the settlement process (incl consultation with Workgroup)	89 days	Wed 20/03/13	Mon 22/07/13	Mon 22/07/13	100%		PAW											
4	✓ Determine possible level of funding for the independent study	29 days	Wed 12/06/13	Mon 22/07/13	Mon 22/07/13	100%		PAW											
5	✓ Determine how the independent study will be funded	36 days	Mon 16/09/13	Mon 04/11/13	Mon 04/11/13	100%		Ofgem											
6	✓ Ofgem to write to EUK, ICOSS and ENA	56 days	Fri 04/10/13	Fri 04/10/13	Fri 20/12/13	100%		Ofgem											
7	✓ Responses from EUK, ICOSS and ENA	55 days	Mon 11/11/13	Mon 04/11/13	Fri 24/01/14	100%		EUK/ICOSS/ENA											
8	✓ Agree mechanism for paying for independent study	5 days	Mon 11/11/13	Mon 04/11/13	Fri 15/11/13	100%		Ofgem											
9	✓ Identify possible service providers for independent study	76 days	Mon 22/07/13	Mon 04/11/13	Mon 04/11/13	100%		Ofgem											
10	✓ Tender for independent study	201 days	Fri 29/11/13	Fri 29/11/13	Fri 05/09/14	100%		Ofgem											
11	✓ Undertake tender evaluation (including mtgs with tenderers)	205 days	Mon 02/12/13	Mon 09/12/13	Tue 30/09/14	100%		Ofgem											
12	✓ Agree party for independent study	3 days	Wed 24/09/14	Mon 09/12/13	Fri 26/09/14	100%		Ofgem											
13	✓ Contract with independent study party	214 days	Tue 24/12/13	Tue 24/12/13	Fri 17/10/14	100%		Ofgem											
14	✓ Commence independent study	207 days	Thu 02/01/14	Wed 01/01/14	Fri 17/10/14	100%		Ofgem											
15	✓ Conclude independent study (including risk register of "theoretical process")	176 days	Fri 16/05/14	Fri 13/06/14	Fri 16/01/15	100%		Ofgem											
16	PAF Group to consider independent study and any reporting required from Xoserve/SPAA	217 days	Thu 01/05/14	Fri 20/06/14	Fri 27/02/15	0%		Ofgem											
17	✓ Xoserve to provide reporting and conclude	253 days	Thu 16/01/14	Fri 27/06/14	Mon 05/01/15	100%		Xoserve/SPAA											
18	PAF Group to consider reporting and agree materiality	176 days	Fri 27/06/14	Fri 27/06/14	Fri 27/02/15	0%		PAW											
19	PAF Group to consider ongoing data elements for PAF	293 days	Fri 14/02/14	Fri 14/02/14	Tue 31/03/15	0%		PAW											
20	1st cut of data elements for PAF and performance monitoring to be reviewed by the PAF Group	197 days	Mon 30/06/14	Mon 30/06/14	Tue 31/03/15	0%		PAW											
21	Performance Assurance Framework Development	407 days	Wed 25/09/13	Wed 01/10/14	Thu 16/04/15	35%													
22	Reporting	395 days	Wed 25/09/13	Mon 31/03/14	Tue 31/03/15	55%													
23	✓ Consider reporting that Xoserve currently does	1 day	Wed 25/09/13	Wed 25/09/13	Wed 25/09/13	100%		PAW											
24	✓ Determine appropriateness of existing reporting	1 day	Wed 25/09/13	Wed 25/09/13	Wed 25/09/13	100%		PAW											
25	✓ Consider any additional reporting/controls necessary for post Nexus functionality/market model	105 days	Wed 25/09/13	Fri 29/11/13	Tue 18/02/14	100%		PAW											
26	✓ Agree future reporting required, in line with Project Nexus Workgroup	148 days	Wed 25/09/13	Fri 29/11/13	Fri 18/04/14	100%		PAW/PNUNC											
27	PAF Group to determine individual elements and timings of reporting	336 days	Tue 17/12/13	Tue 31/12/13	Tue 31/03/15	10%		PAW											
28	✓ Determine individual elements and timings of performance monitoring	75 days	Tue 17/12/13	Mon 31/03/14	Mon 31/03/14	100%		PAW											
29	Overall Governance Arrangements	363 days	Mon 11/11/13	Fri 13/06/14	Wed 01/04/15	23%													
30	✓ Agree main parties to the PAF - e.g. Transporters, Shippers, Xoserve	1 day	Mon 11/11/13	Fri 31/01/14	Mon 11/11/13	100%		PAW											
31	PAF Group to agree what current governance arrangements will be impacted by the PAF and if anything new will be required	314 days	Tue 17/12/13	Thu 15/05/14	Fri 27/02/15	0%		PAW											
32	PAF Group to commence discussions with other governance bodies (if required)	336 days	Tue 17/12/13	Fri 28/02/14	Tue 31/03/15	0%		PAW											
33	✓ Agree the funding parties for PAF	75 days	Tue 17/12/13	Mon 31/03/14	Mon 31/03/14	100%		PAW											
34	✓ Agree if an annual budget is required	119 days	Tue 17/12/13	Mon 31/03/14	Fri 30/05/14	100%		PAW											
35	✓ Consider Ofgem's involvement/oversight	1 day	Fri 30/05/14	Wed 30/04/14	Fri 30/05/14	100%		PAW											
36	✓ Agree governance around reporting - how to request new reports	1 day	Fri 30/05/14	Wed 14/05/14	Fri 30/05/14	100%	26	PAW											
37	PAF Group to decide if there is any consultation needed with Parties/Ofgem following the determination of a settlement risk penalty	1 day	Tue 31/03/15	Wed 14/05/14	Tue 31/03/15	0%	87	PAW/Ofgem											
38	PAF Group to determine individual elements and timings of incentive regime and invoicing (if deemed required under action 1)	1 day	Wed 01/04/15	Fri 13/06/14	Wed 01/04/15	0%	37	PAW											
39	PAF Group to determine individual elements and timings of assurance (if deemed required under action 1)	1 day	Fri 27/02/15	Fri 13/06/14	Fri 27/02/15	0%	28	PAW											
40	Day to Day Governance Arrangements	108 days	Mon 02/12/13	Wed 30/04/14	Wed 30/04/14	100%													
41	✓ Determine the need for an "oversight" workgroup/committee and, if necessary, its remit, frequency of meetings and if it could make decisions	108 days	Mon 02/12/13	Wed 30/04/14	Wed 30/04/14	100%		PAW											
42	✓ Determine role of Joint Office, Xoserve, Ofgem and SPAA and involvement in PAF	108 days	Mon 02/12/13	Wed 30/04/14	Wed 30/04/14	100%		PAW											
43	✓ Consider inclusion in UNC directly or via ancillary document	108 days	Mon 02/12/13	Wed 30/04/14	Wed 30/04/14	100%		PAW											
44	Introducing the PAF	374 days	Mon 11/11/13	Wed 01/10/14	Thu 16/04/15	11%													
45	PAF Group to develop business rules for PAF MOD	362 days	Mon 11/11/13	Fri 29/08/14	Tue 31/03/15	20%		PAW											
46	✓ Mod raised by BGT on independent study	1 day	Fri 07/02/14	Fri 07/02/14	Fri 07/02/14	100%		PAW											
47	PAF Group to consider two Mods for PAF and Policing / Administration	233 days	Wed 09/04/14	Wed 09/04/14	Fri 27/02/15	10%		PAW											
48	PAF Group to raise two Mods for PAF and Policing / Administration	240 days	Wed 30/04/14	Wed 30/04/14	Tue 31/03/15	9%		PAW											
49	PAF Group to hold mod panel meeting to discuss two Mods	241 days	Thu 15/05/14	Thu 15/05/14	Thu 16/04/15	0%		PAW											
50	Development of Mod 483	171 days	Tue 05/08/14	NA	Tue 31/03/15	80%													
51	PAF Group to agree, in principle, the basis for the settlement risk premium	1 day	Tue 31/03/15	Wed 30/04/14	Tue 31/03/15	0%	16	PAW											
52	PAF Group to agree frequency (at least initial frequency) of the analysis of settlement risk and how often methodology needs to be updated (if at all)	1 day	Tue 31/03/15	Wed 30/04/14	Tue 31/03/15	0%	16	PAW											
53	✓ Discuss at PAW Meeting	1 day	Tue 05/08/14	Tue 05/08/14	Tue 05/08/14	100%		PAW											



Project: Performance Assurance Plan
Date: Mon 02/02/15


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

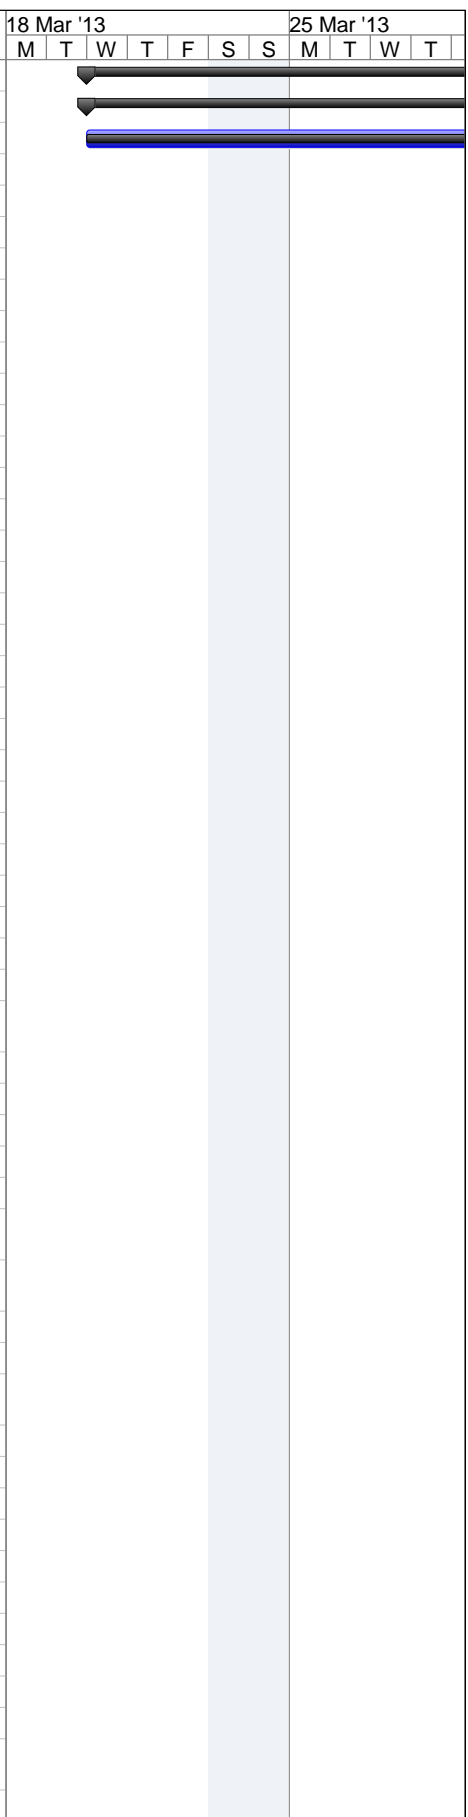

Project: Performance Assurance Plan
Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

10 Jun '13	17 Jun '13	24 Jun '13	01 Jul '13	08 Jul '13	15 Jul '13	22 Jul '13	29 Jul '13	05 Aug '13	12 Aug '13	19 Aug '13
M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S

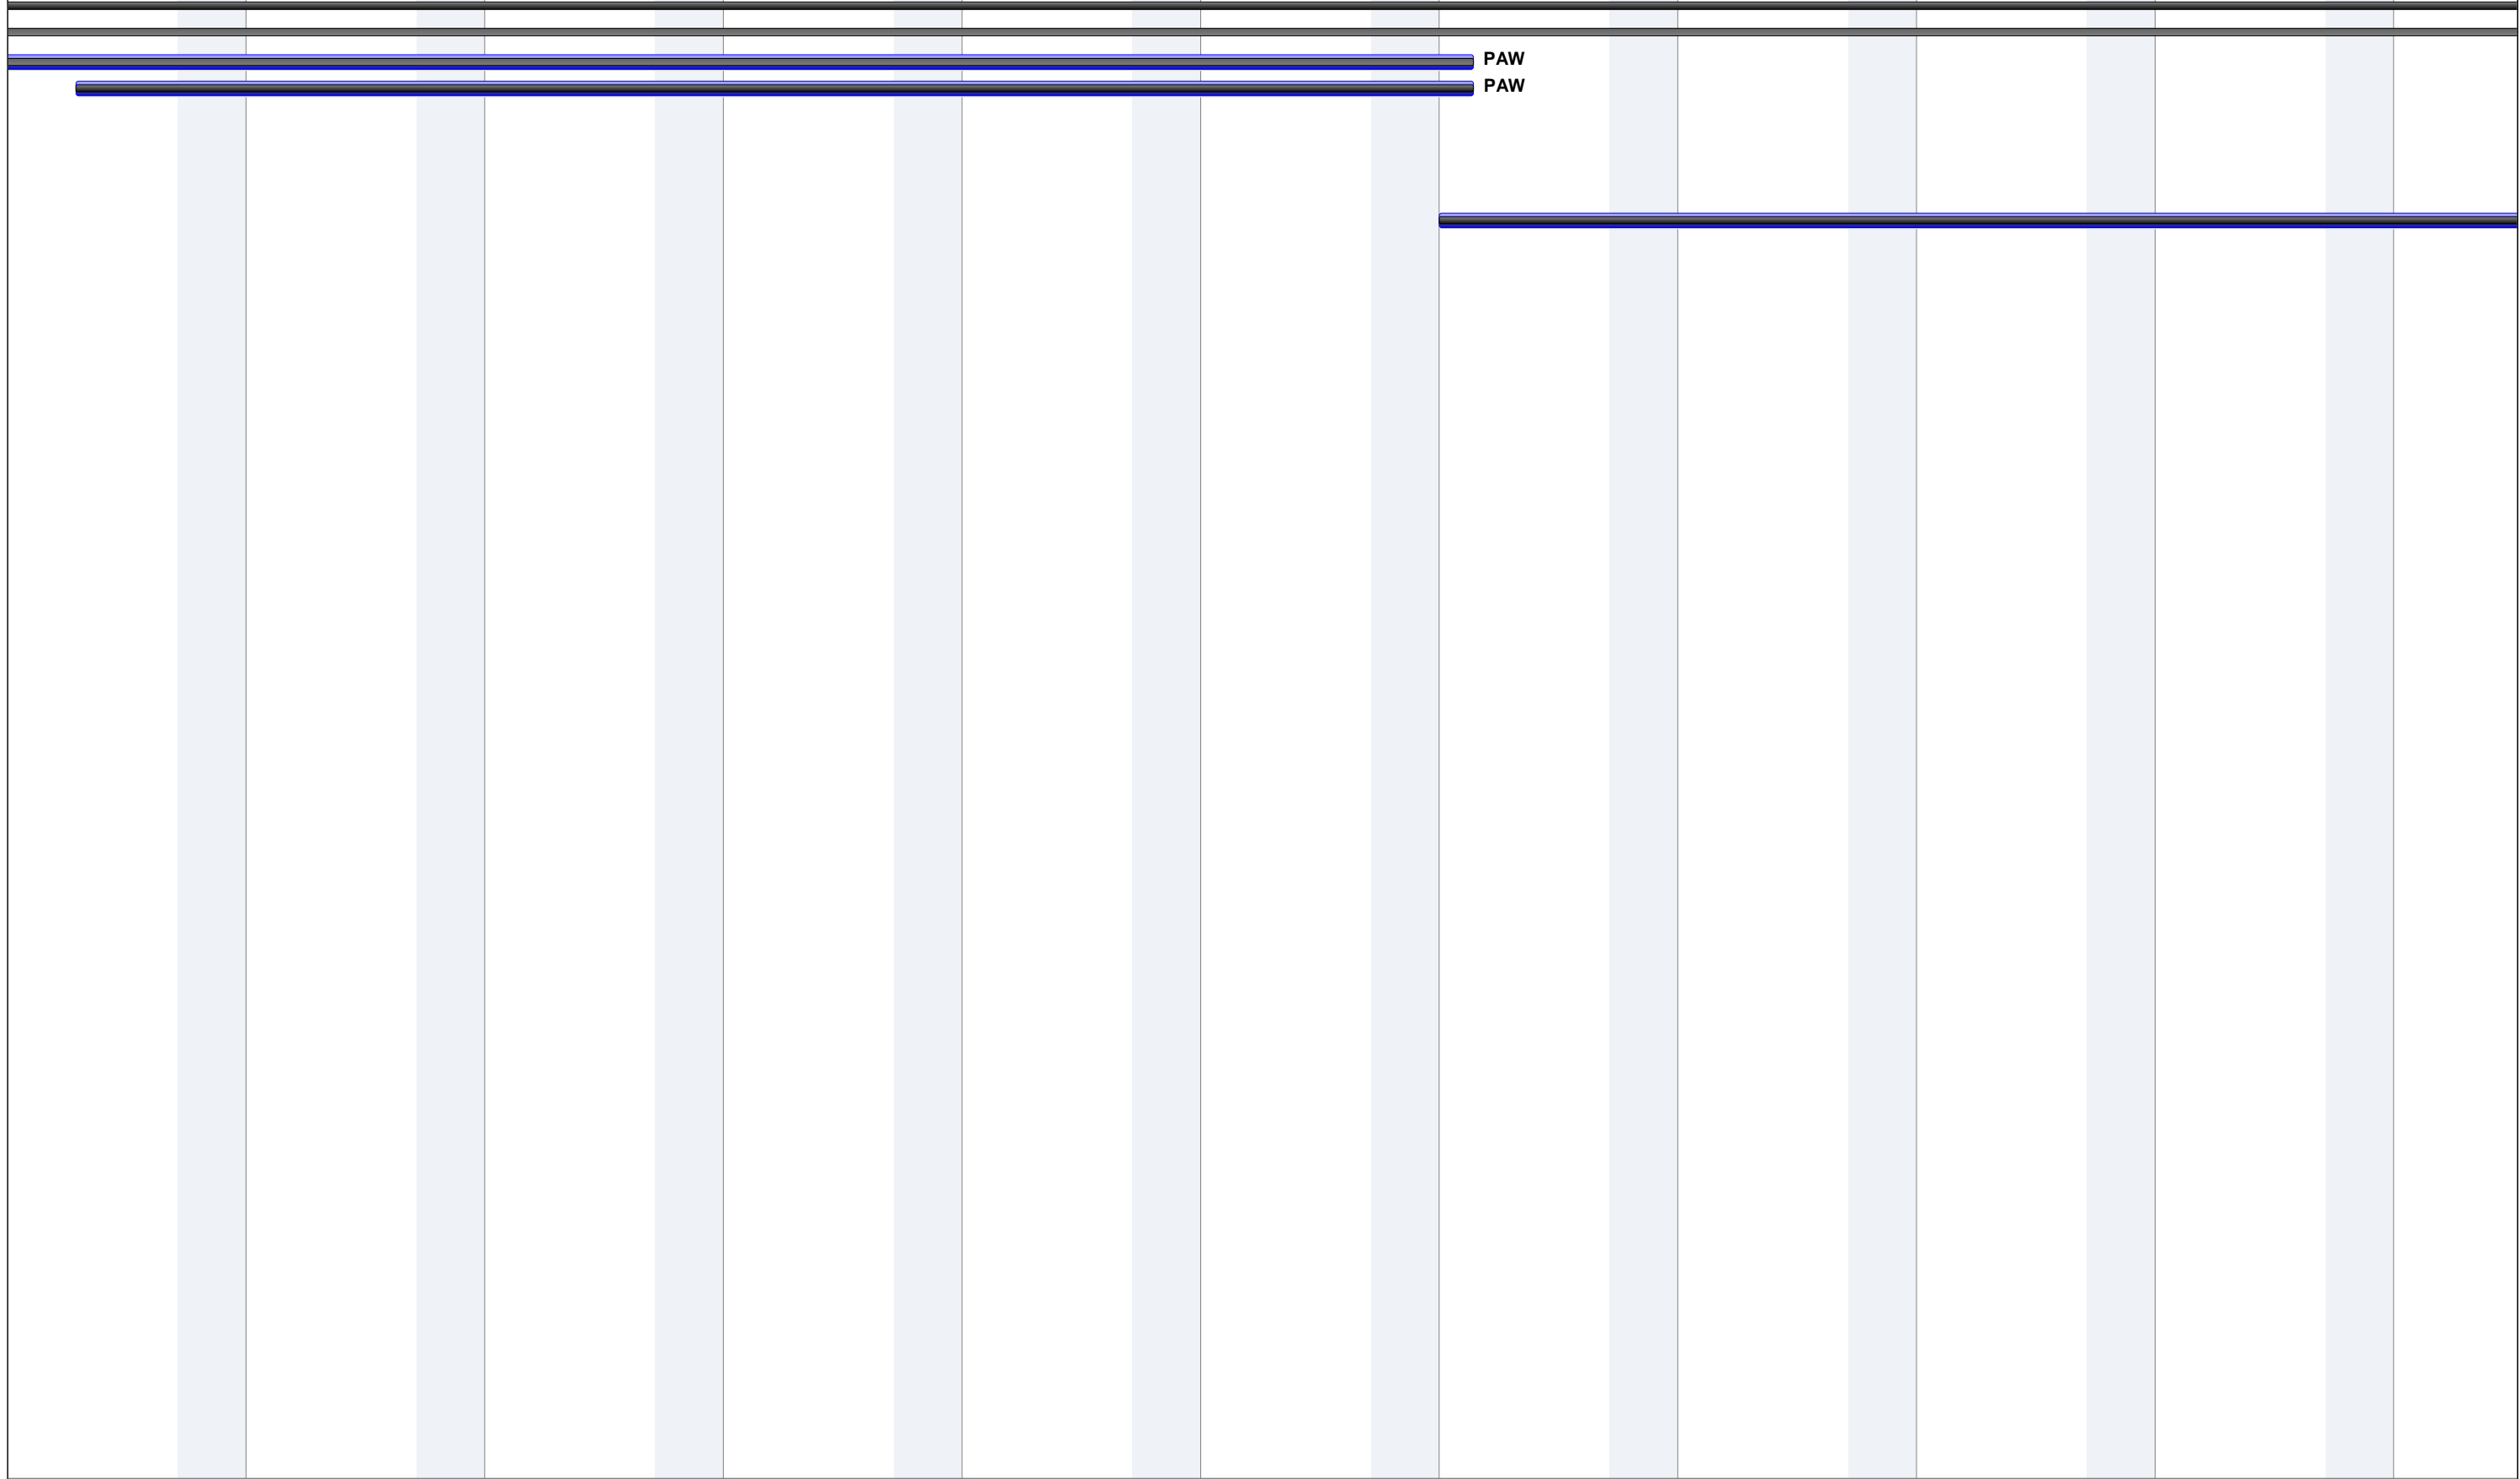


Project: Performance Assurance Plan Date: Mon 02/02/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			



Project: Performance Assurance Plan
Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

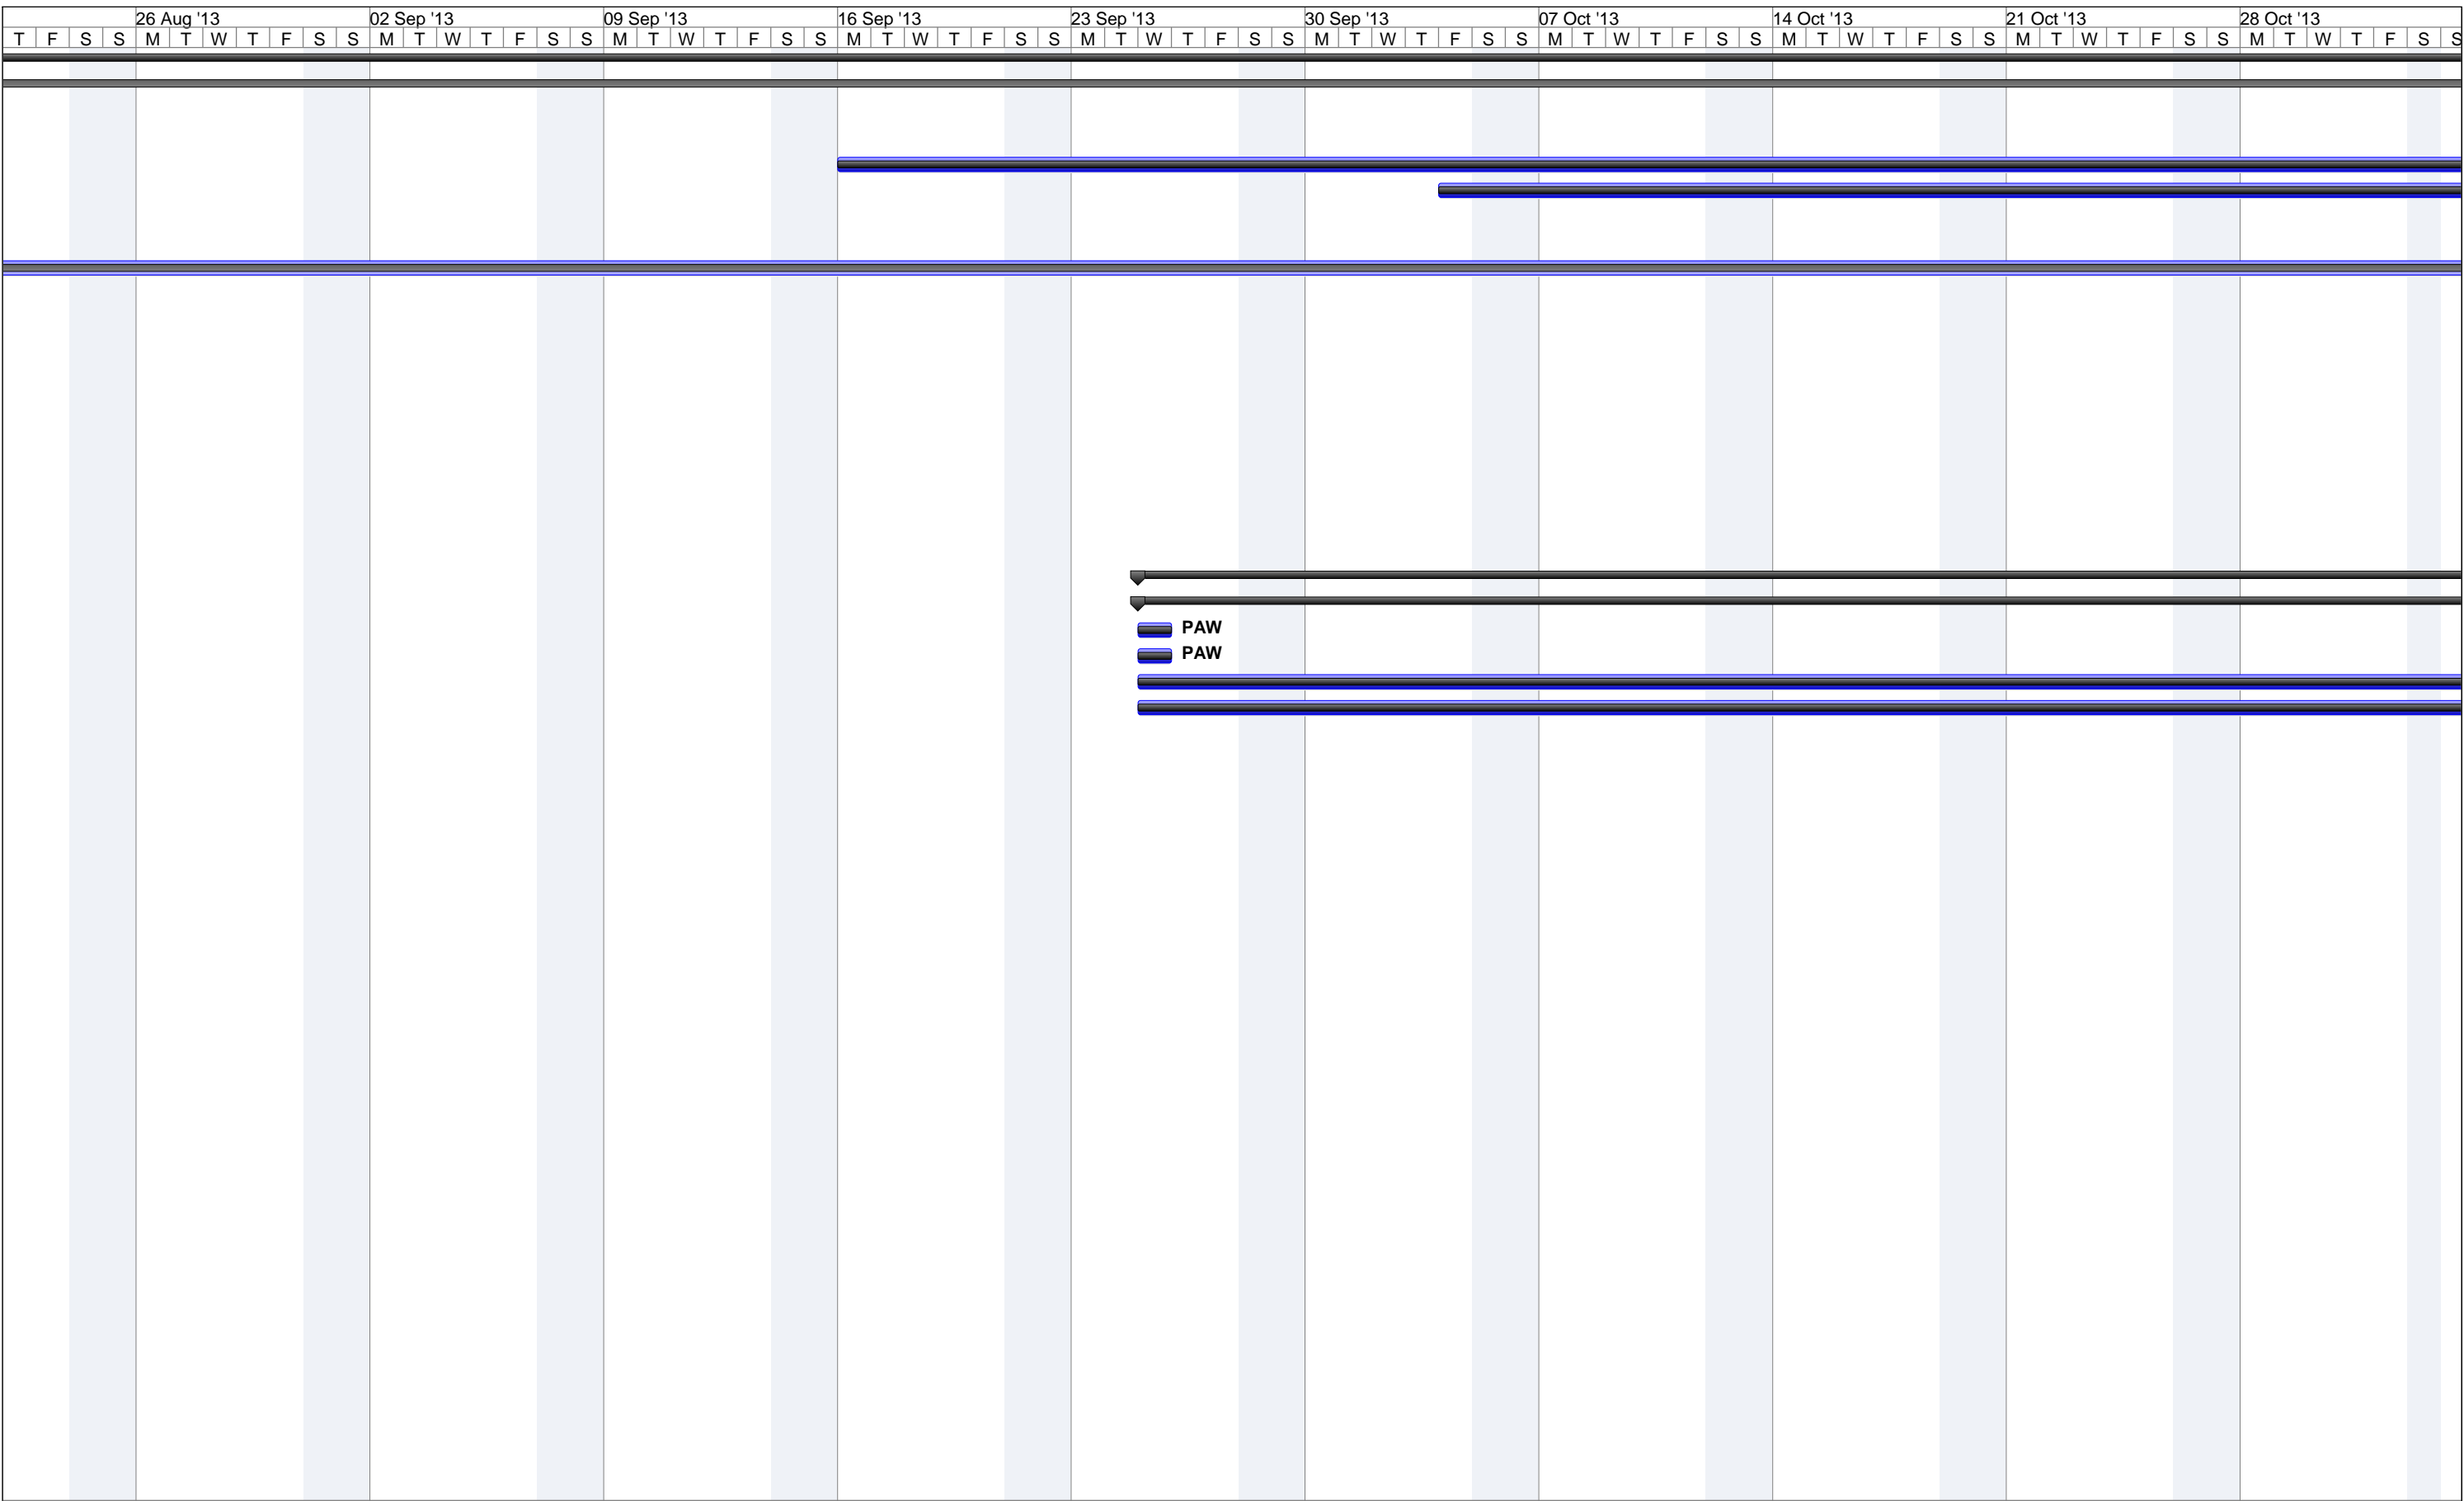

Project: Performance Assurance Plan
 Date: Mon 02/02/15


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			



Project: Performance Assurance Plan
Date: Mon 02/02/15


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

04 Nov '13 11 Nov '13 18 Nov '13 25 Nov '13 02 Dec '13 09 Dec '13 16 Dec '13 23 Dec '13 30 Dec '13 06 Jan '14 13 Jan '14
 S M T W T F S S S M T W T F S S S M T W T F S S S M T W T F S S S M T W T F S S S M T W T F S S S M T W

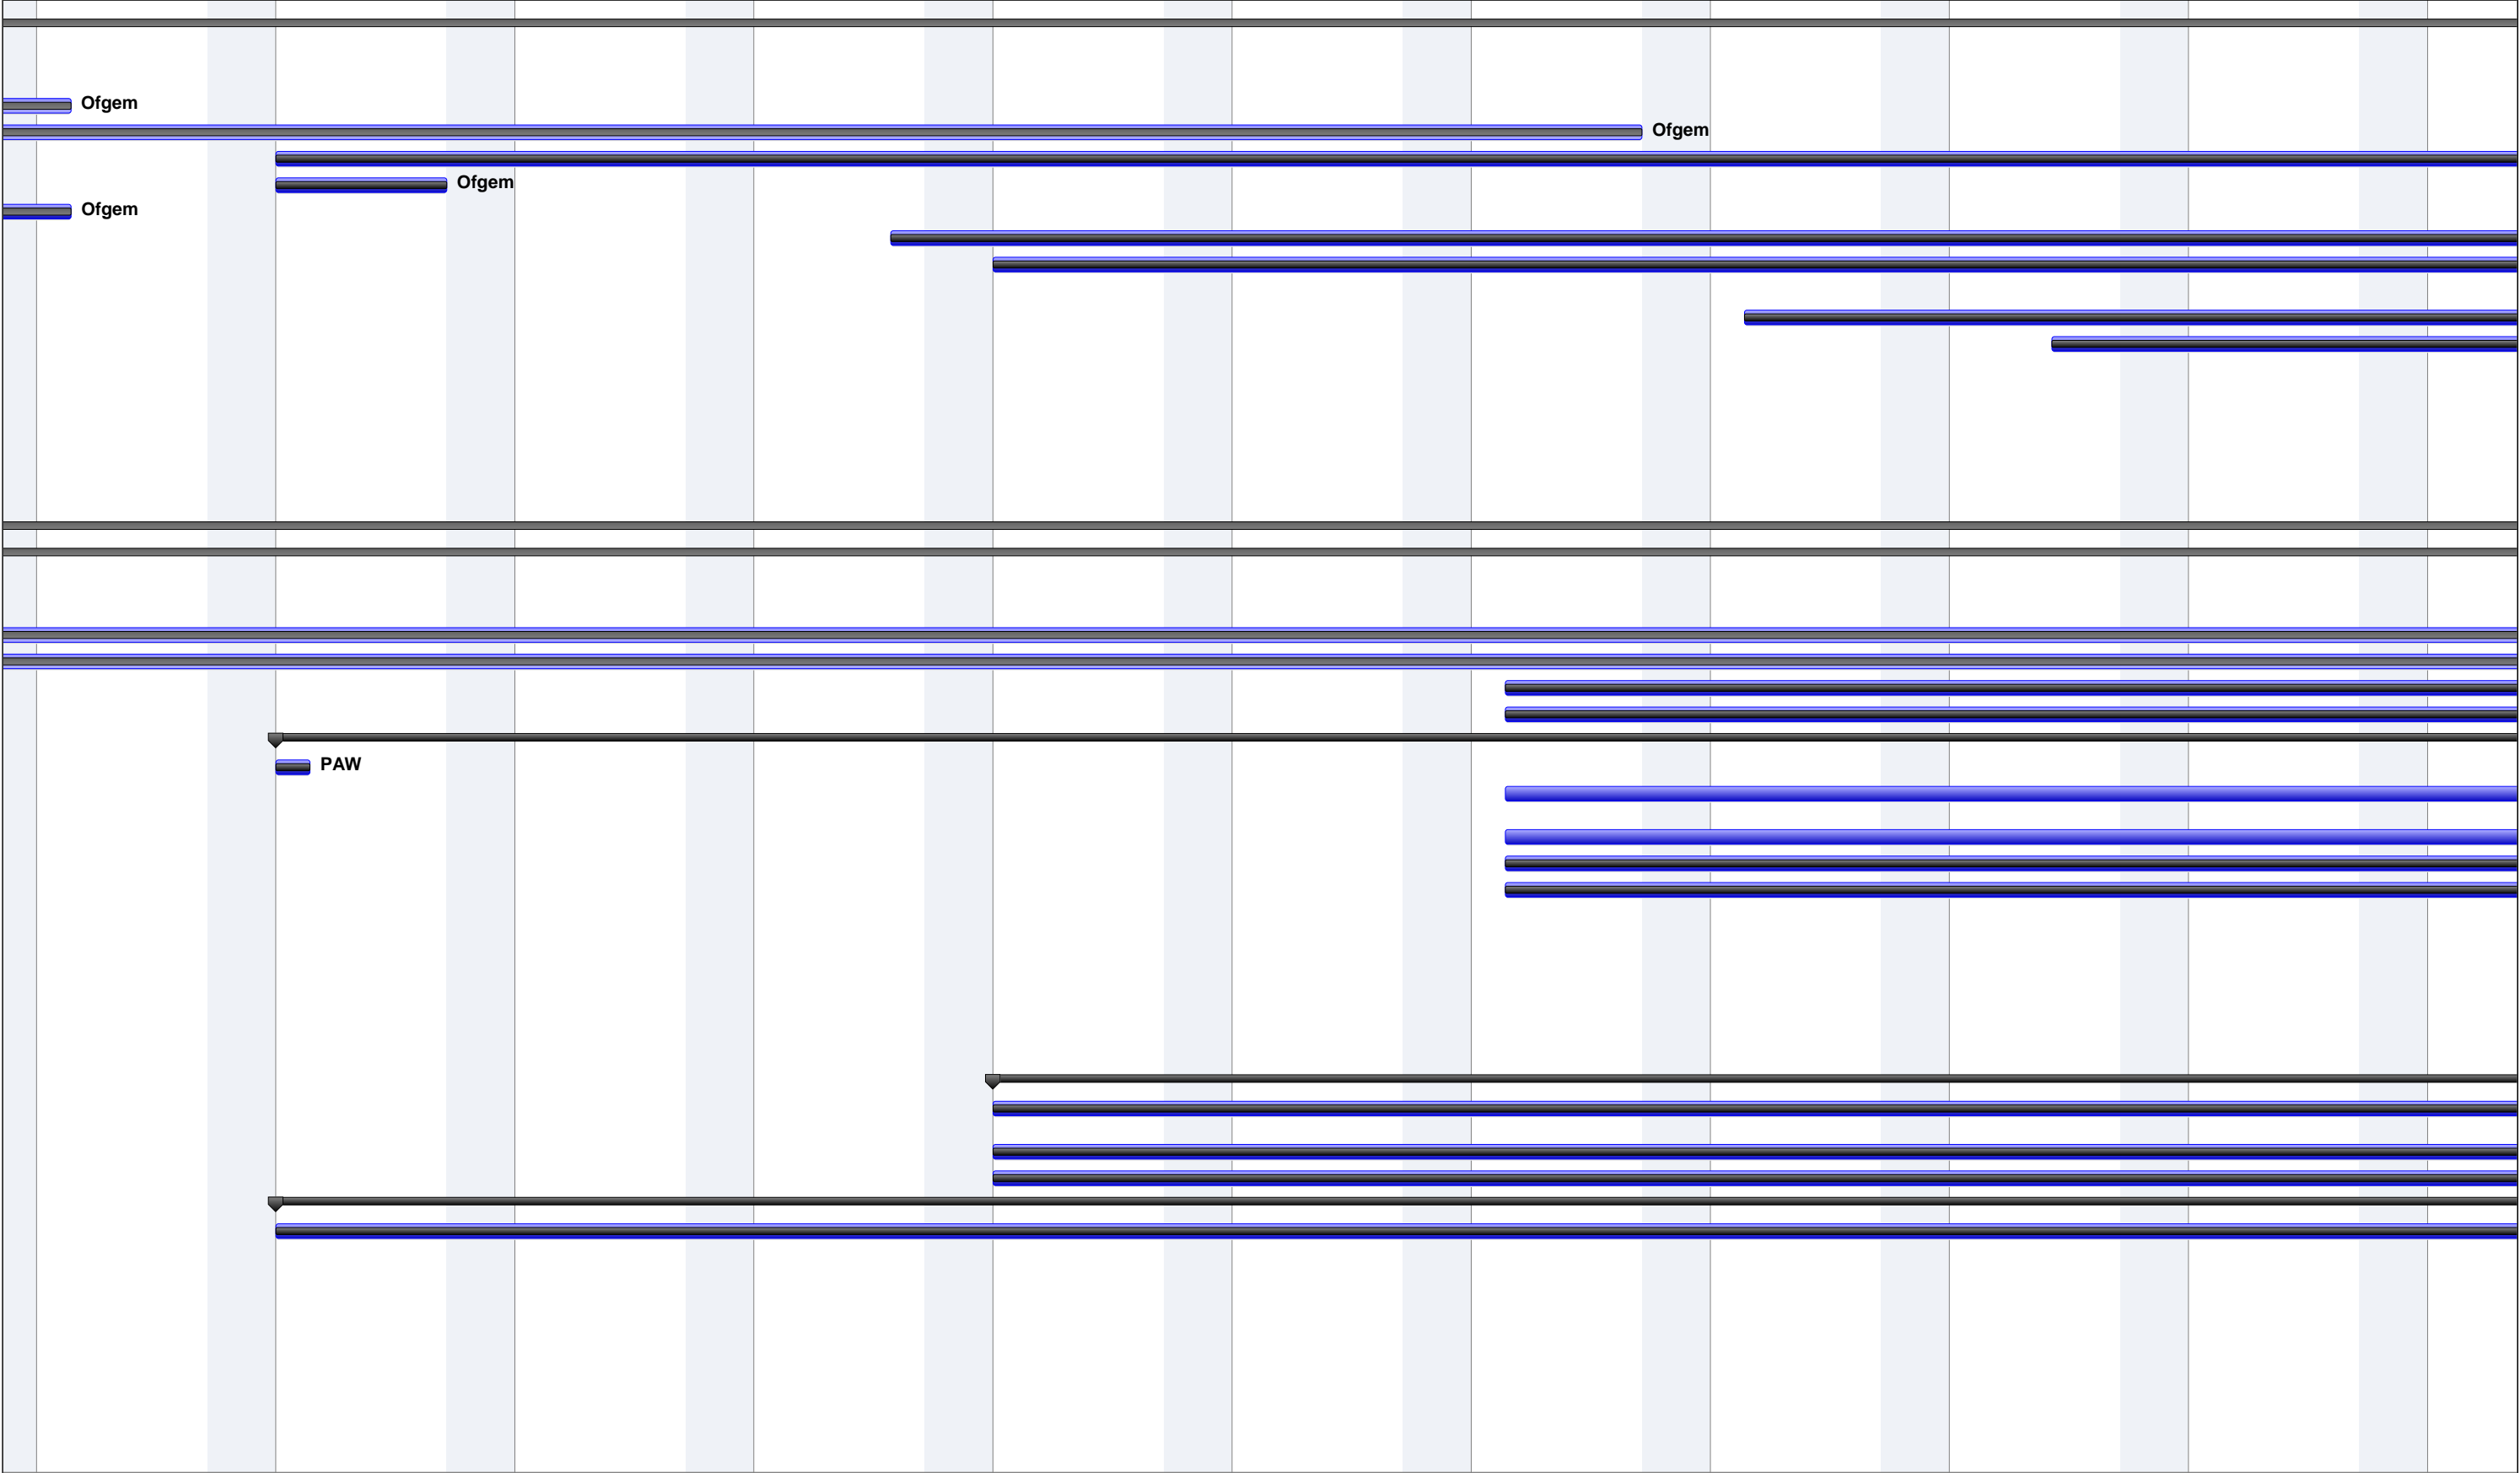


Project: Performance Assurance Plan
 Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

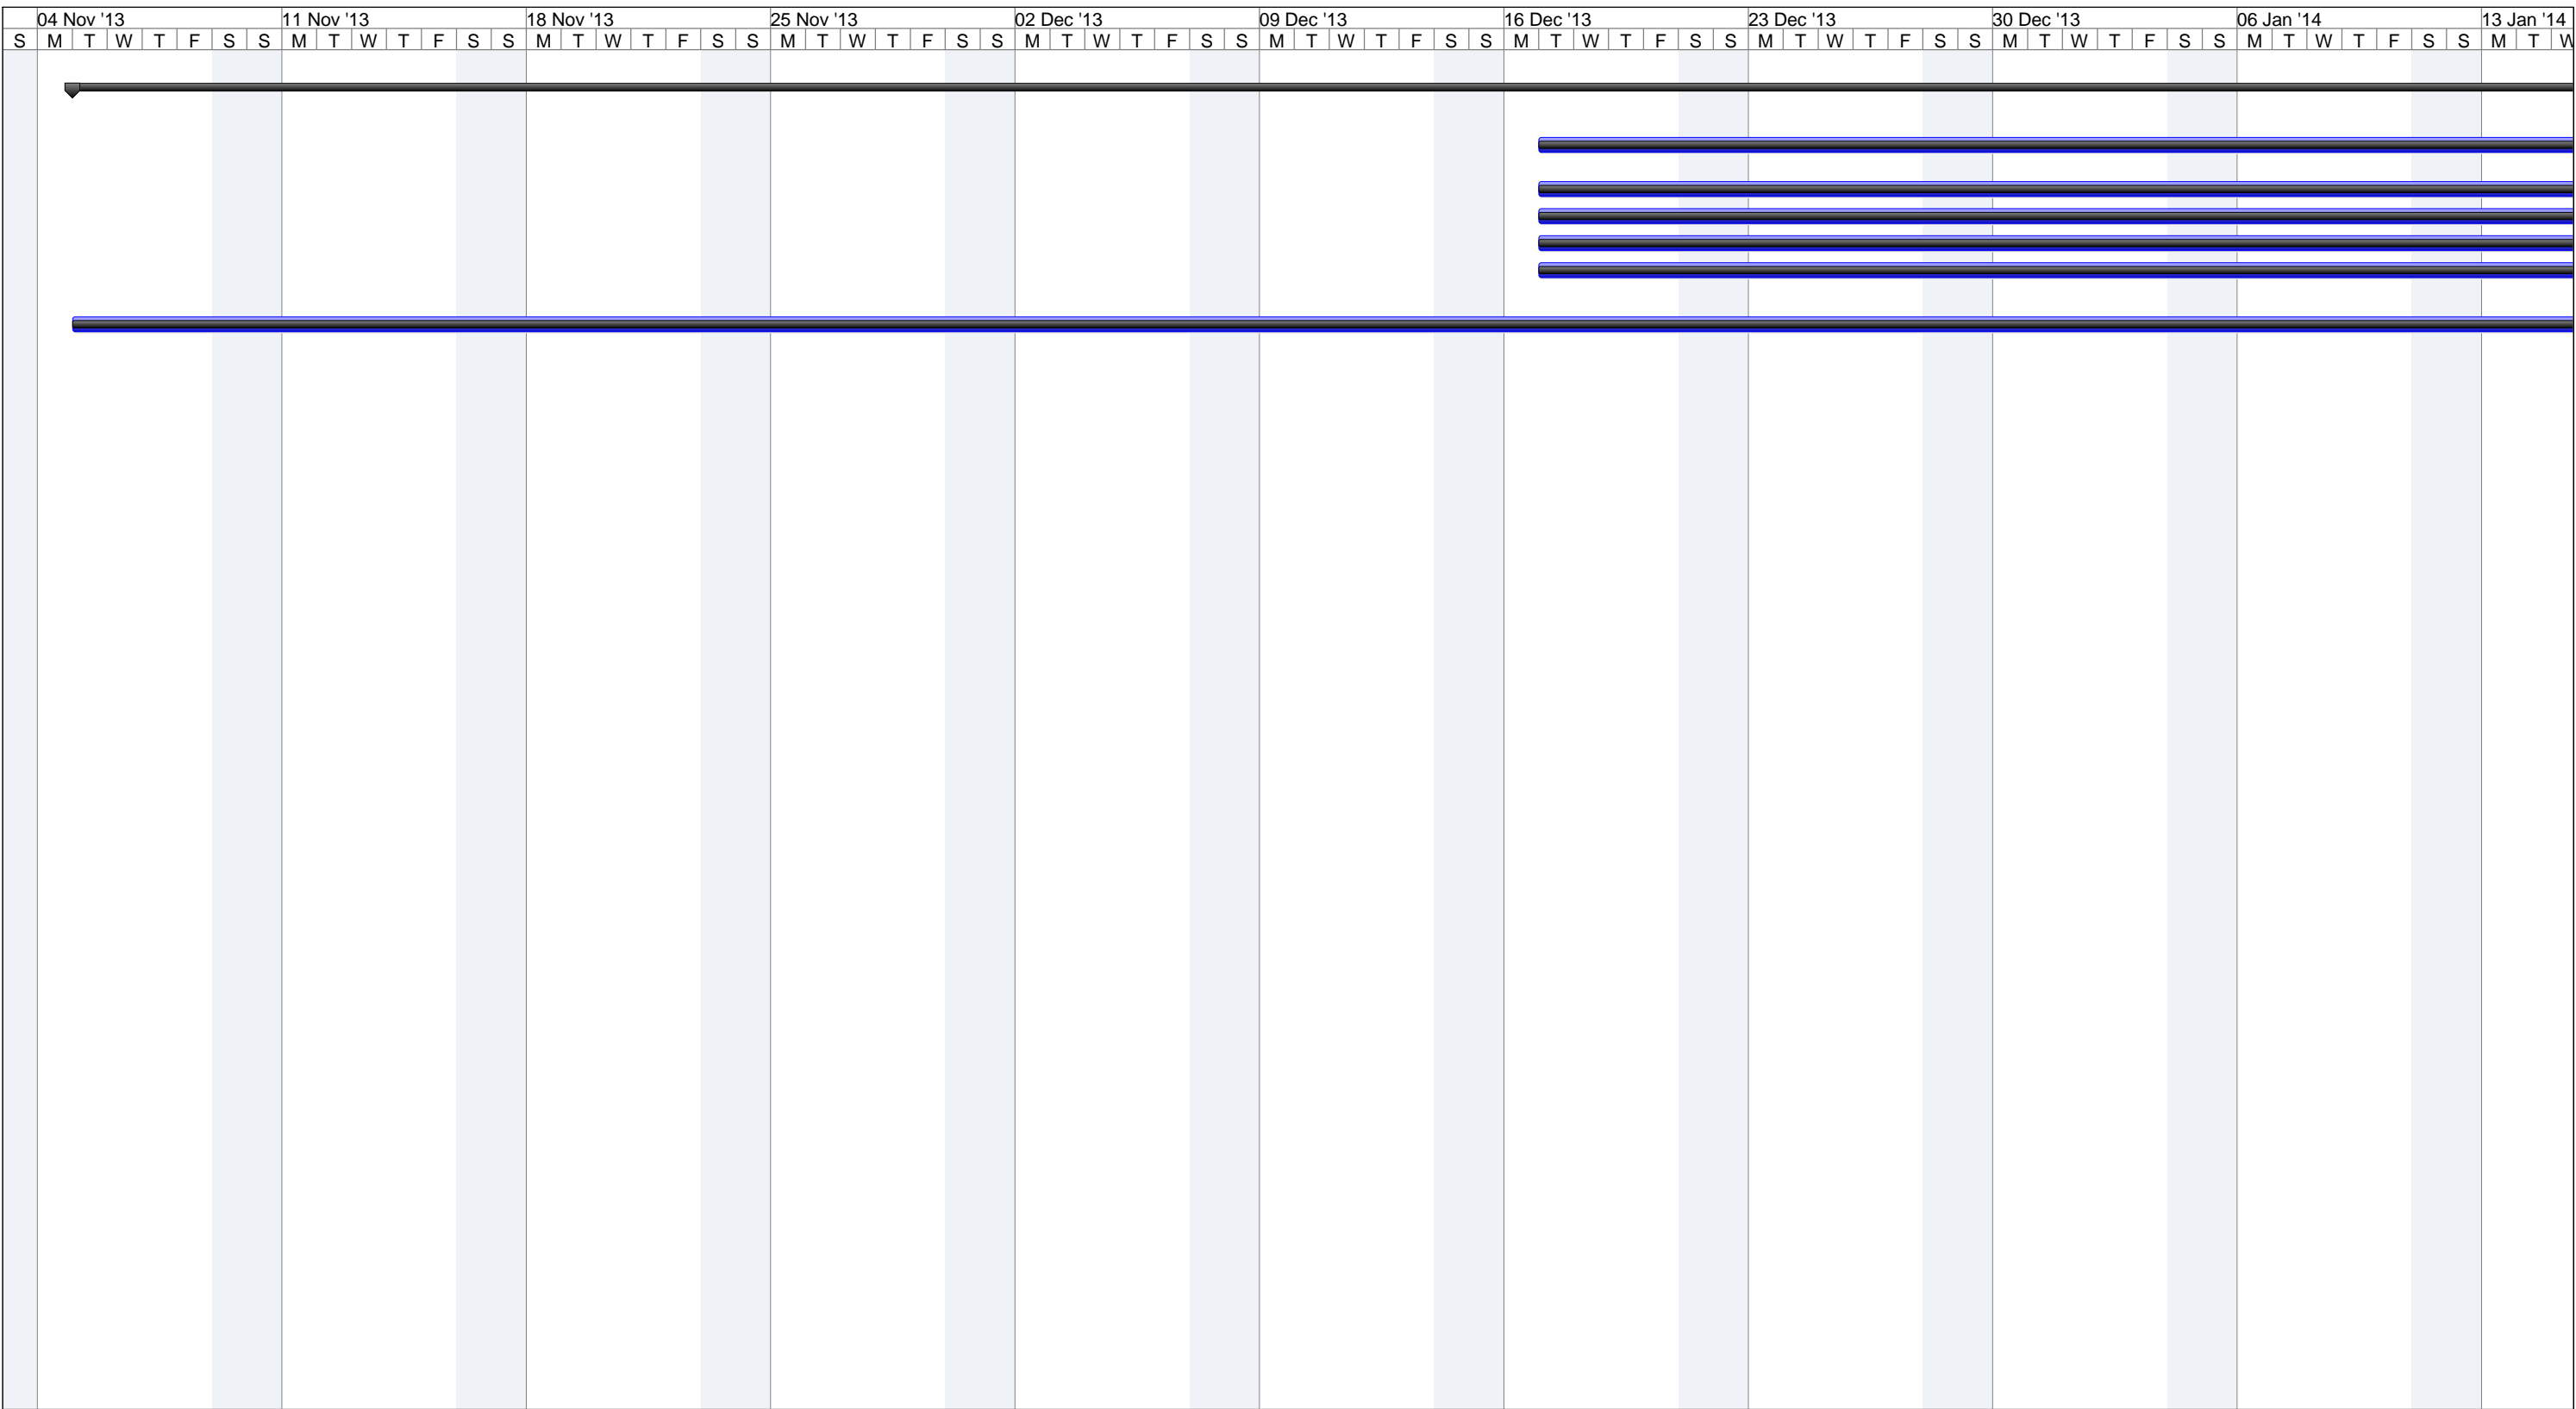

Project: Performance Assurance Plan
Date: Mon 02/02/15


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

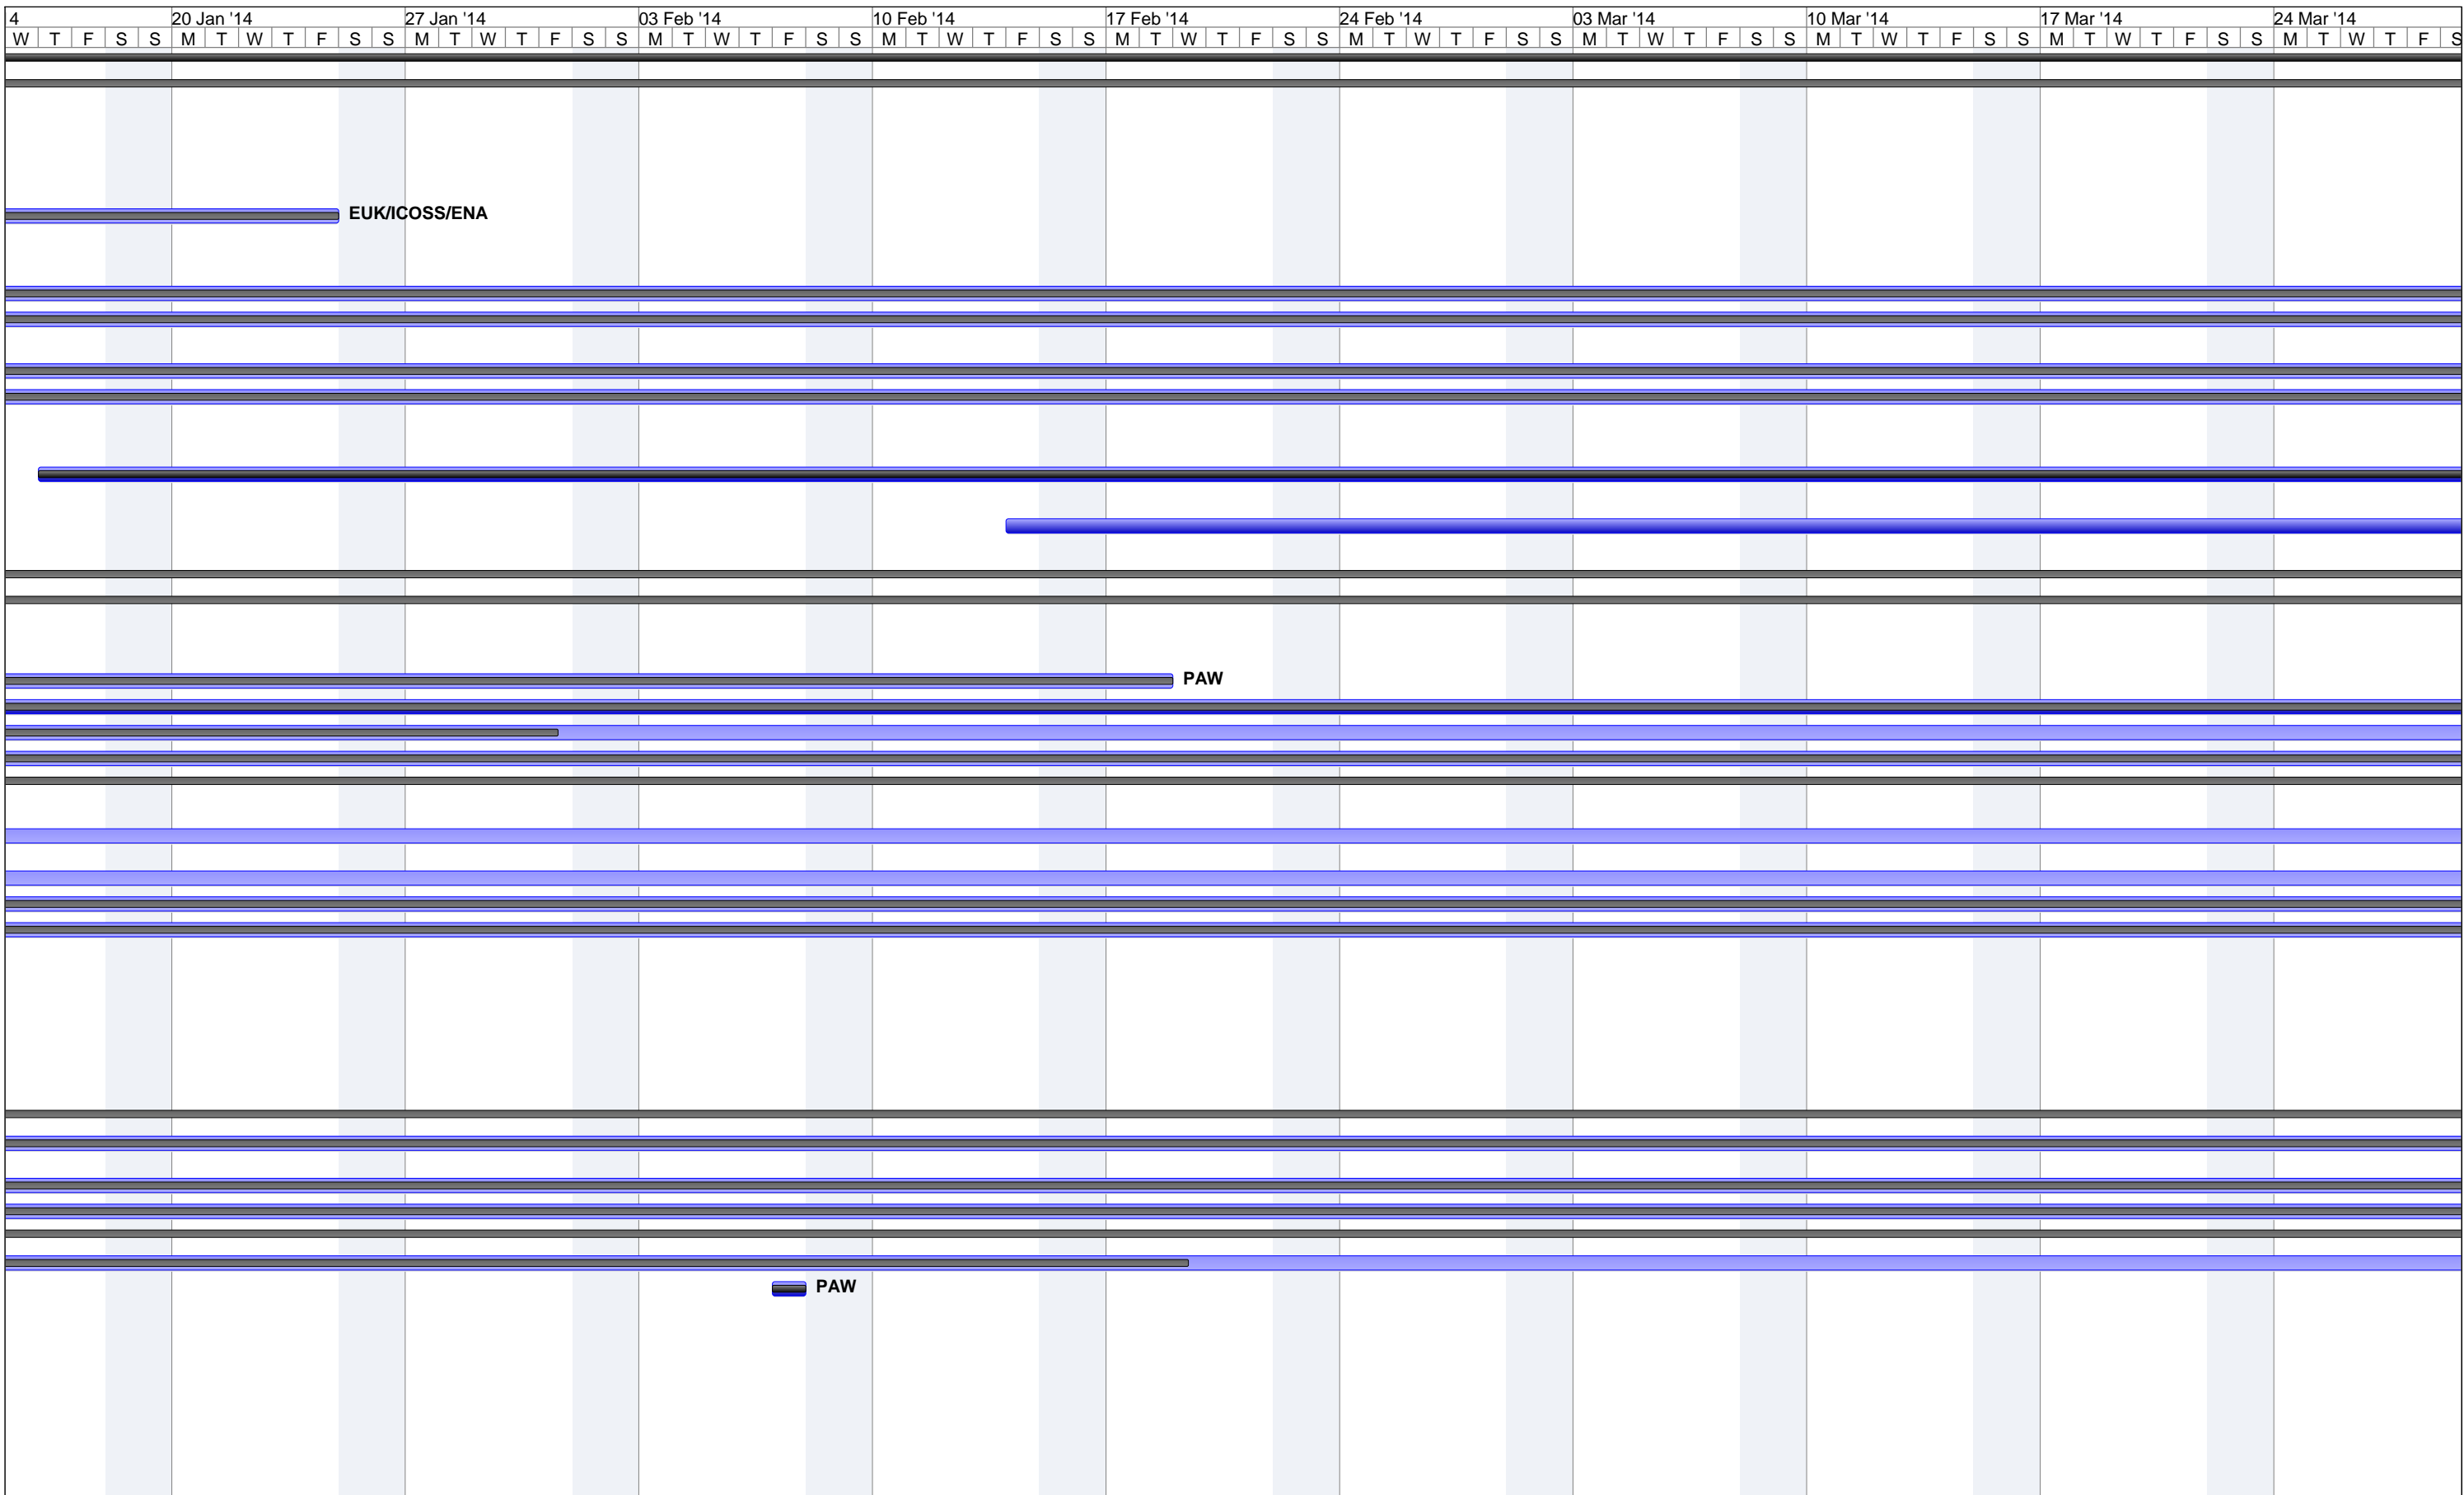

Project: Performance Assurance Plan
 Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			


4 20 Jan '14 27 Jan '14 03 Feb '14 10 Feb '14 17 Feb '14 24 Feb '14 03 Mar '14 10 Mar '14 17 Mar '14 24 Mar '14
W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S

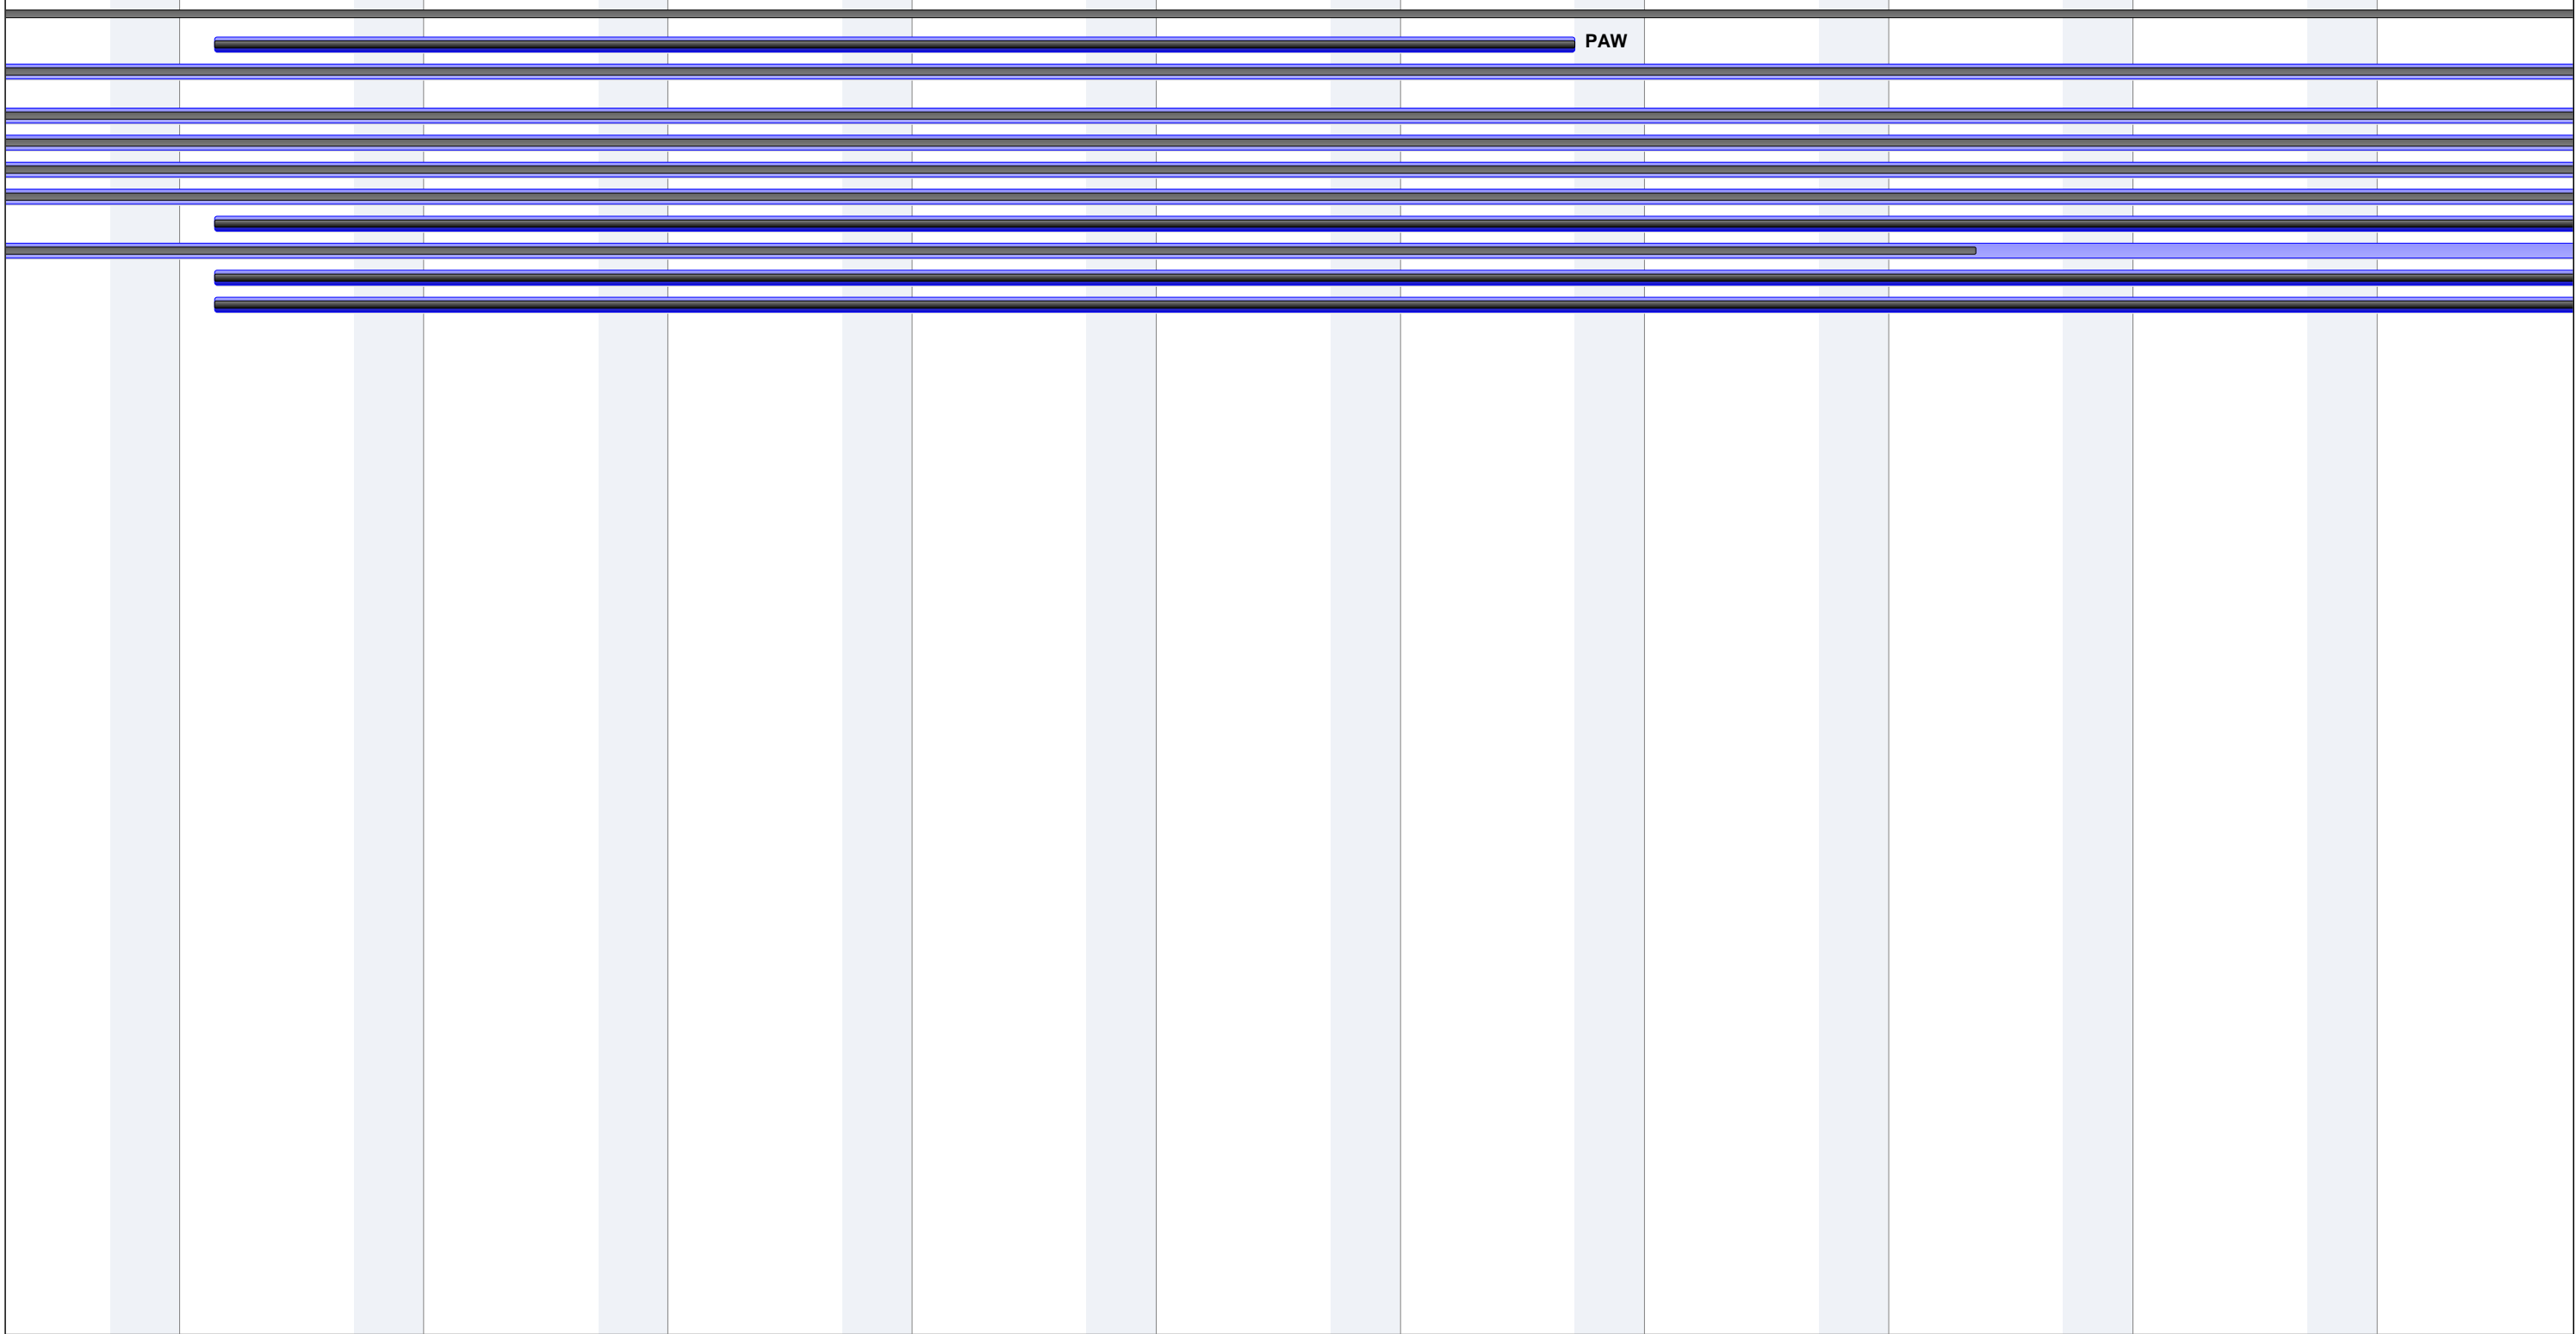

Project: Performance Assurance Plan
Date: Mon 02/02/15


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

31 Mar '14 07 Apr '14 14 Apr '14 21 Apr '14 28 Apr '14 05 May '14 12 May '14 19 May '14 26 May '14 02 Jun '14 09 Jun

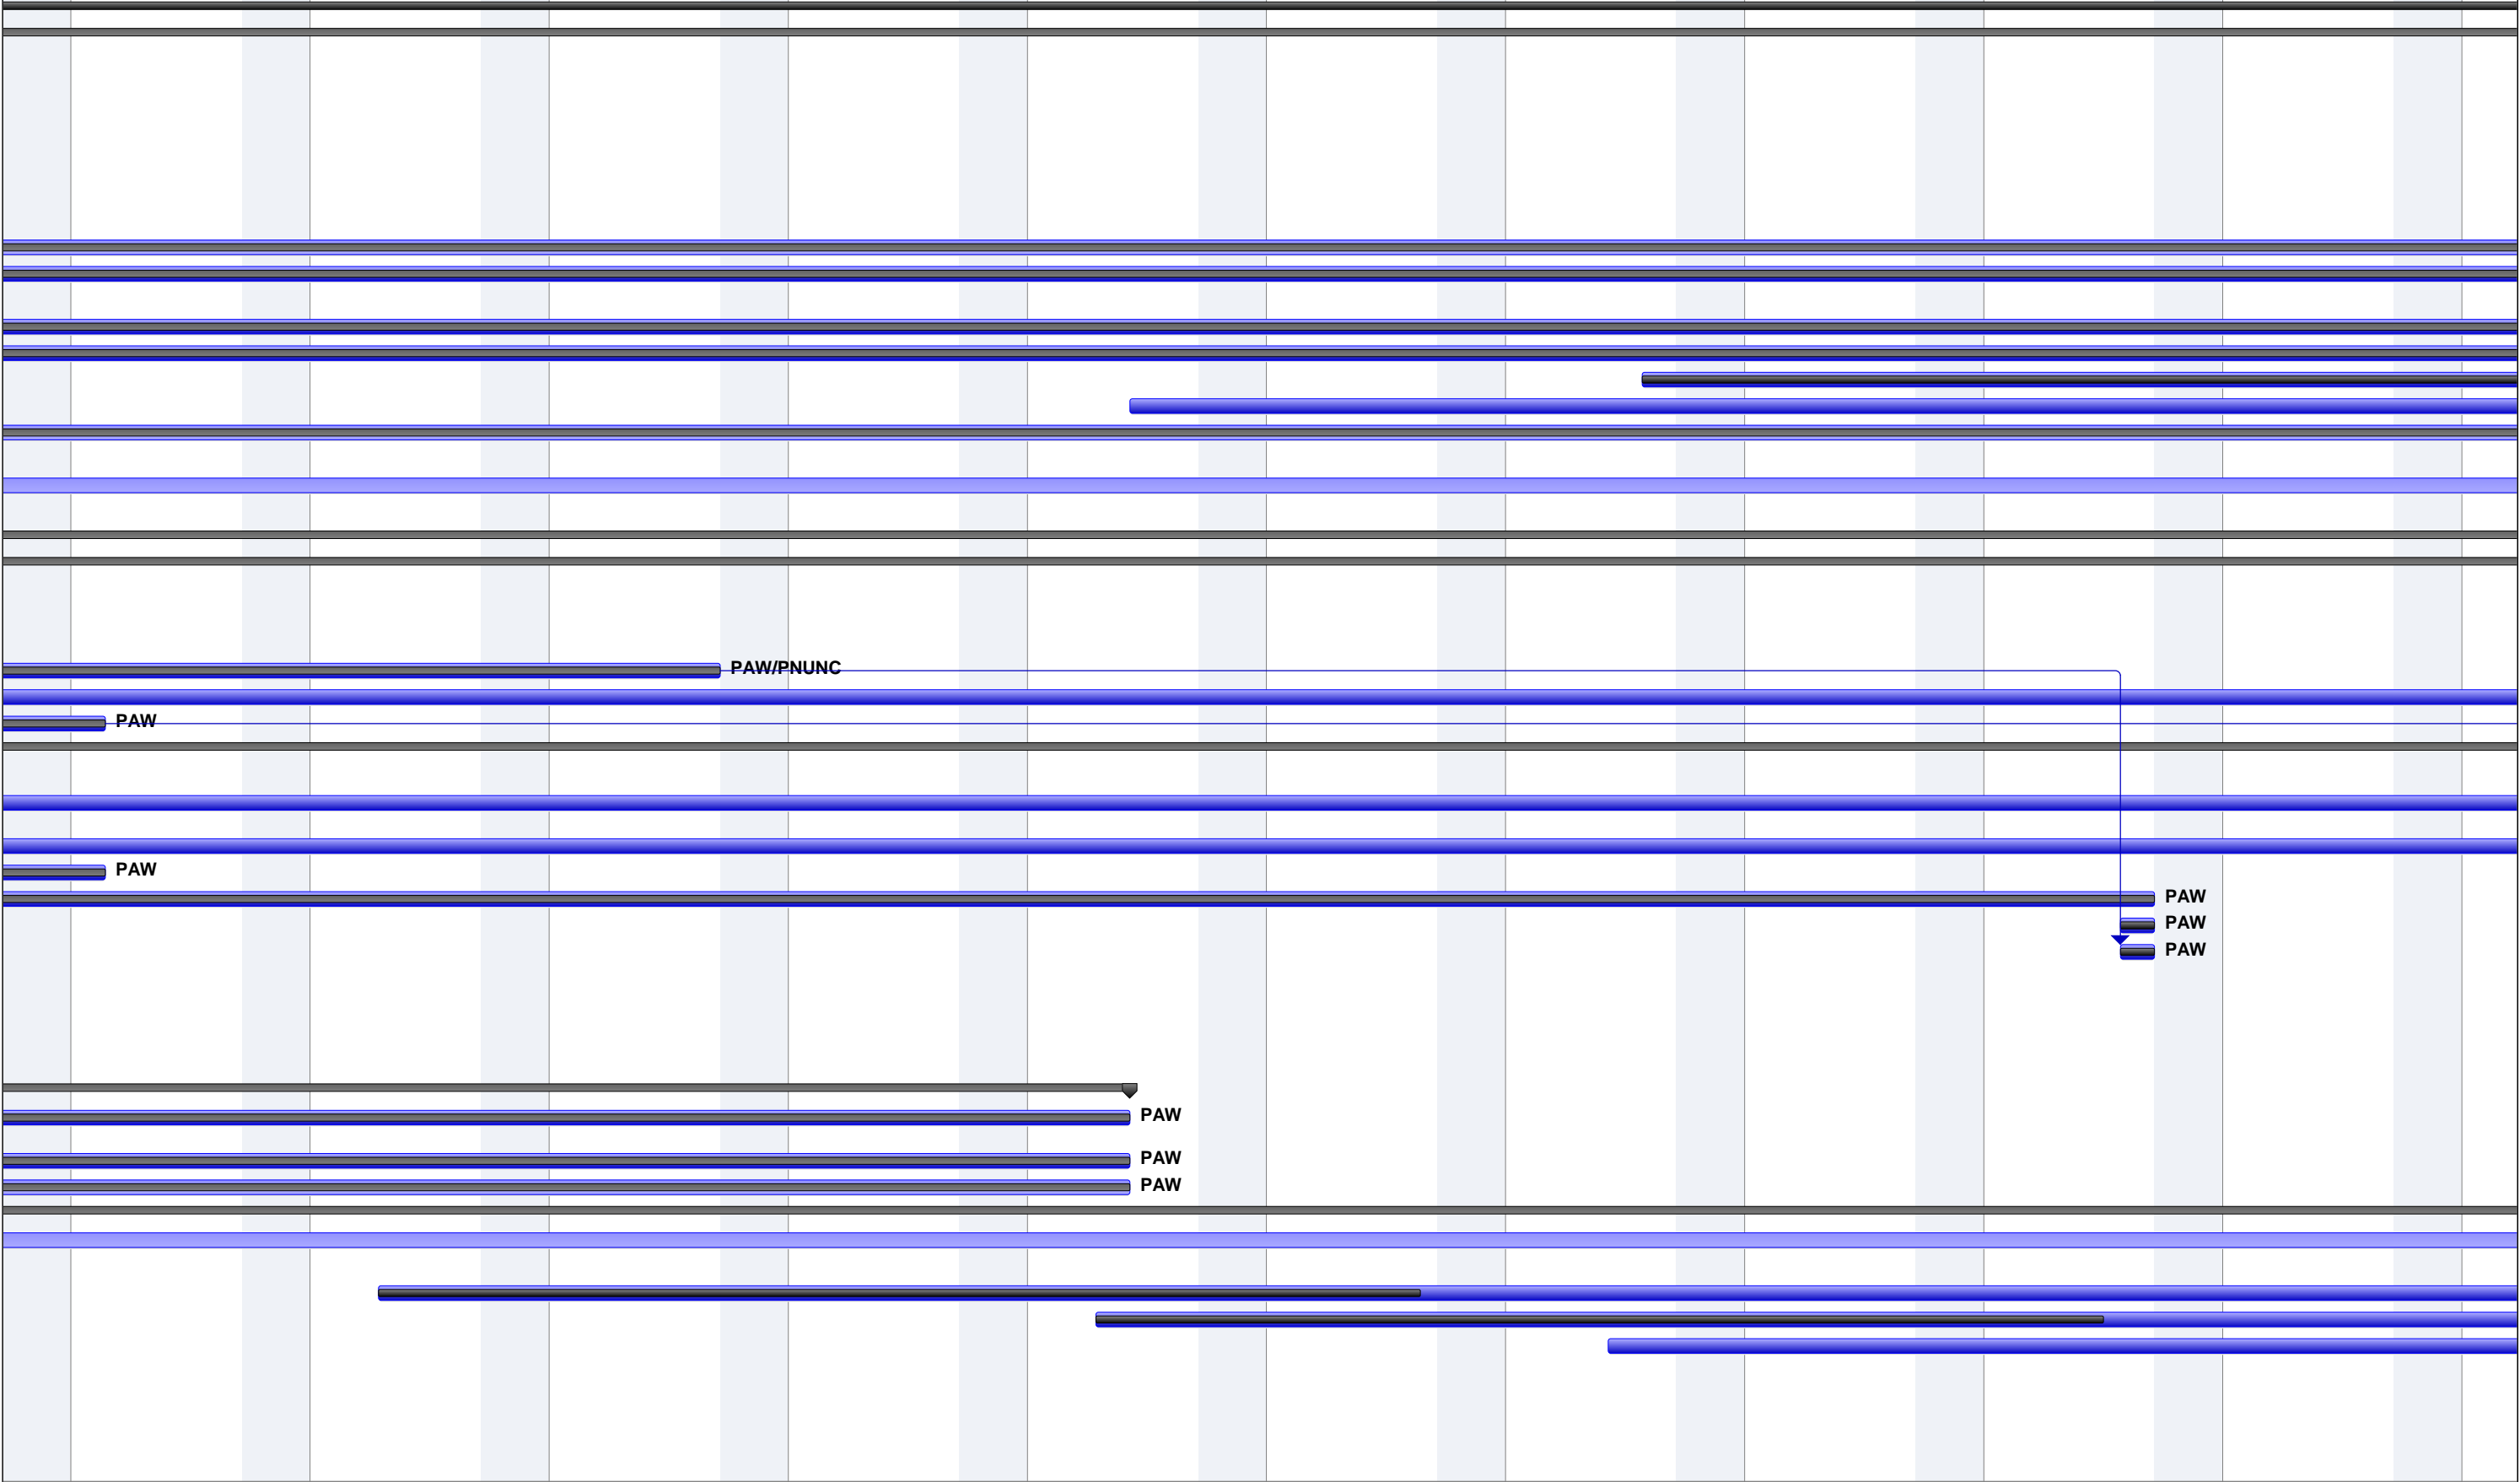


Project: Performance Assurance Plan
Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

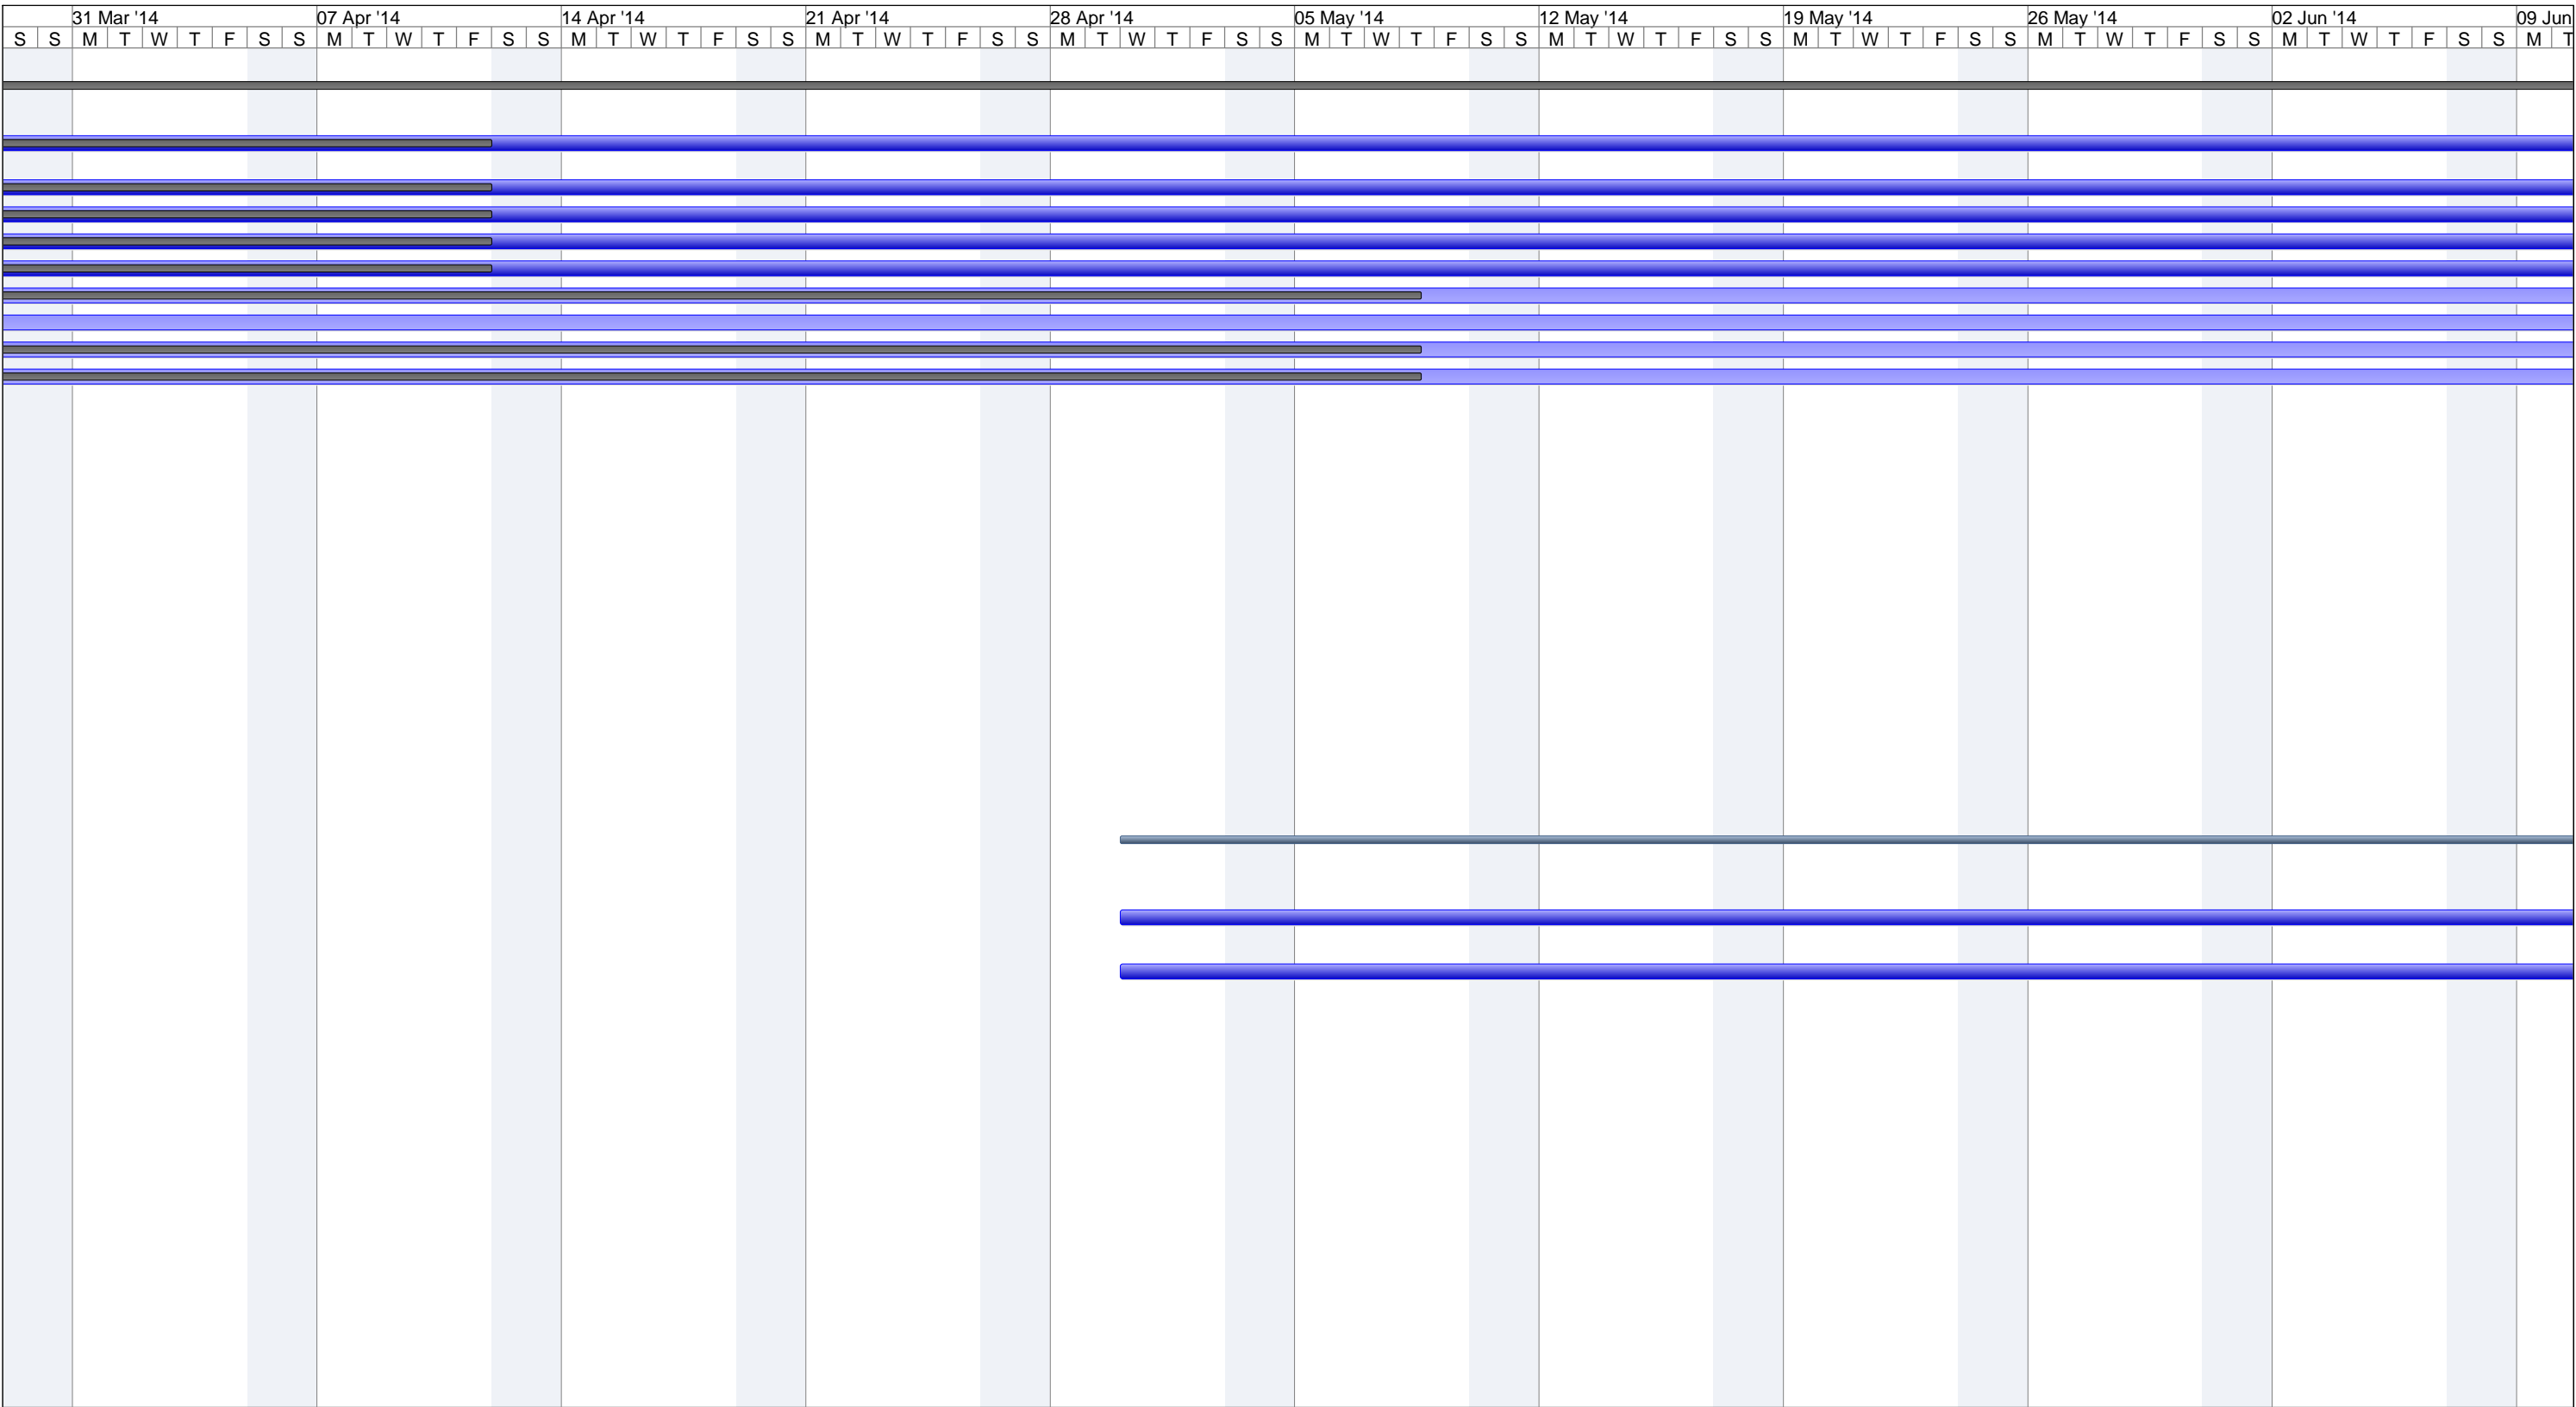


Project: Performance Assurance Plan
 Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

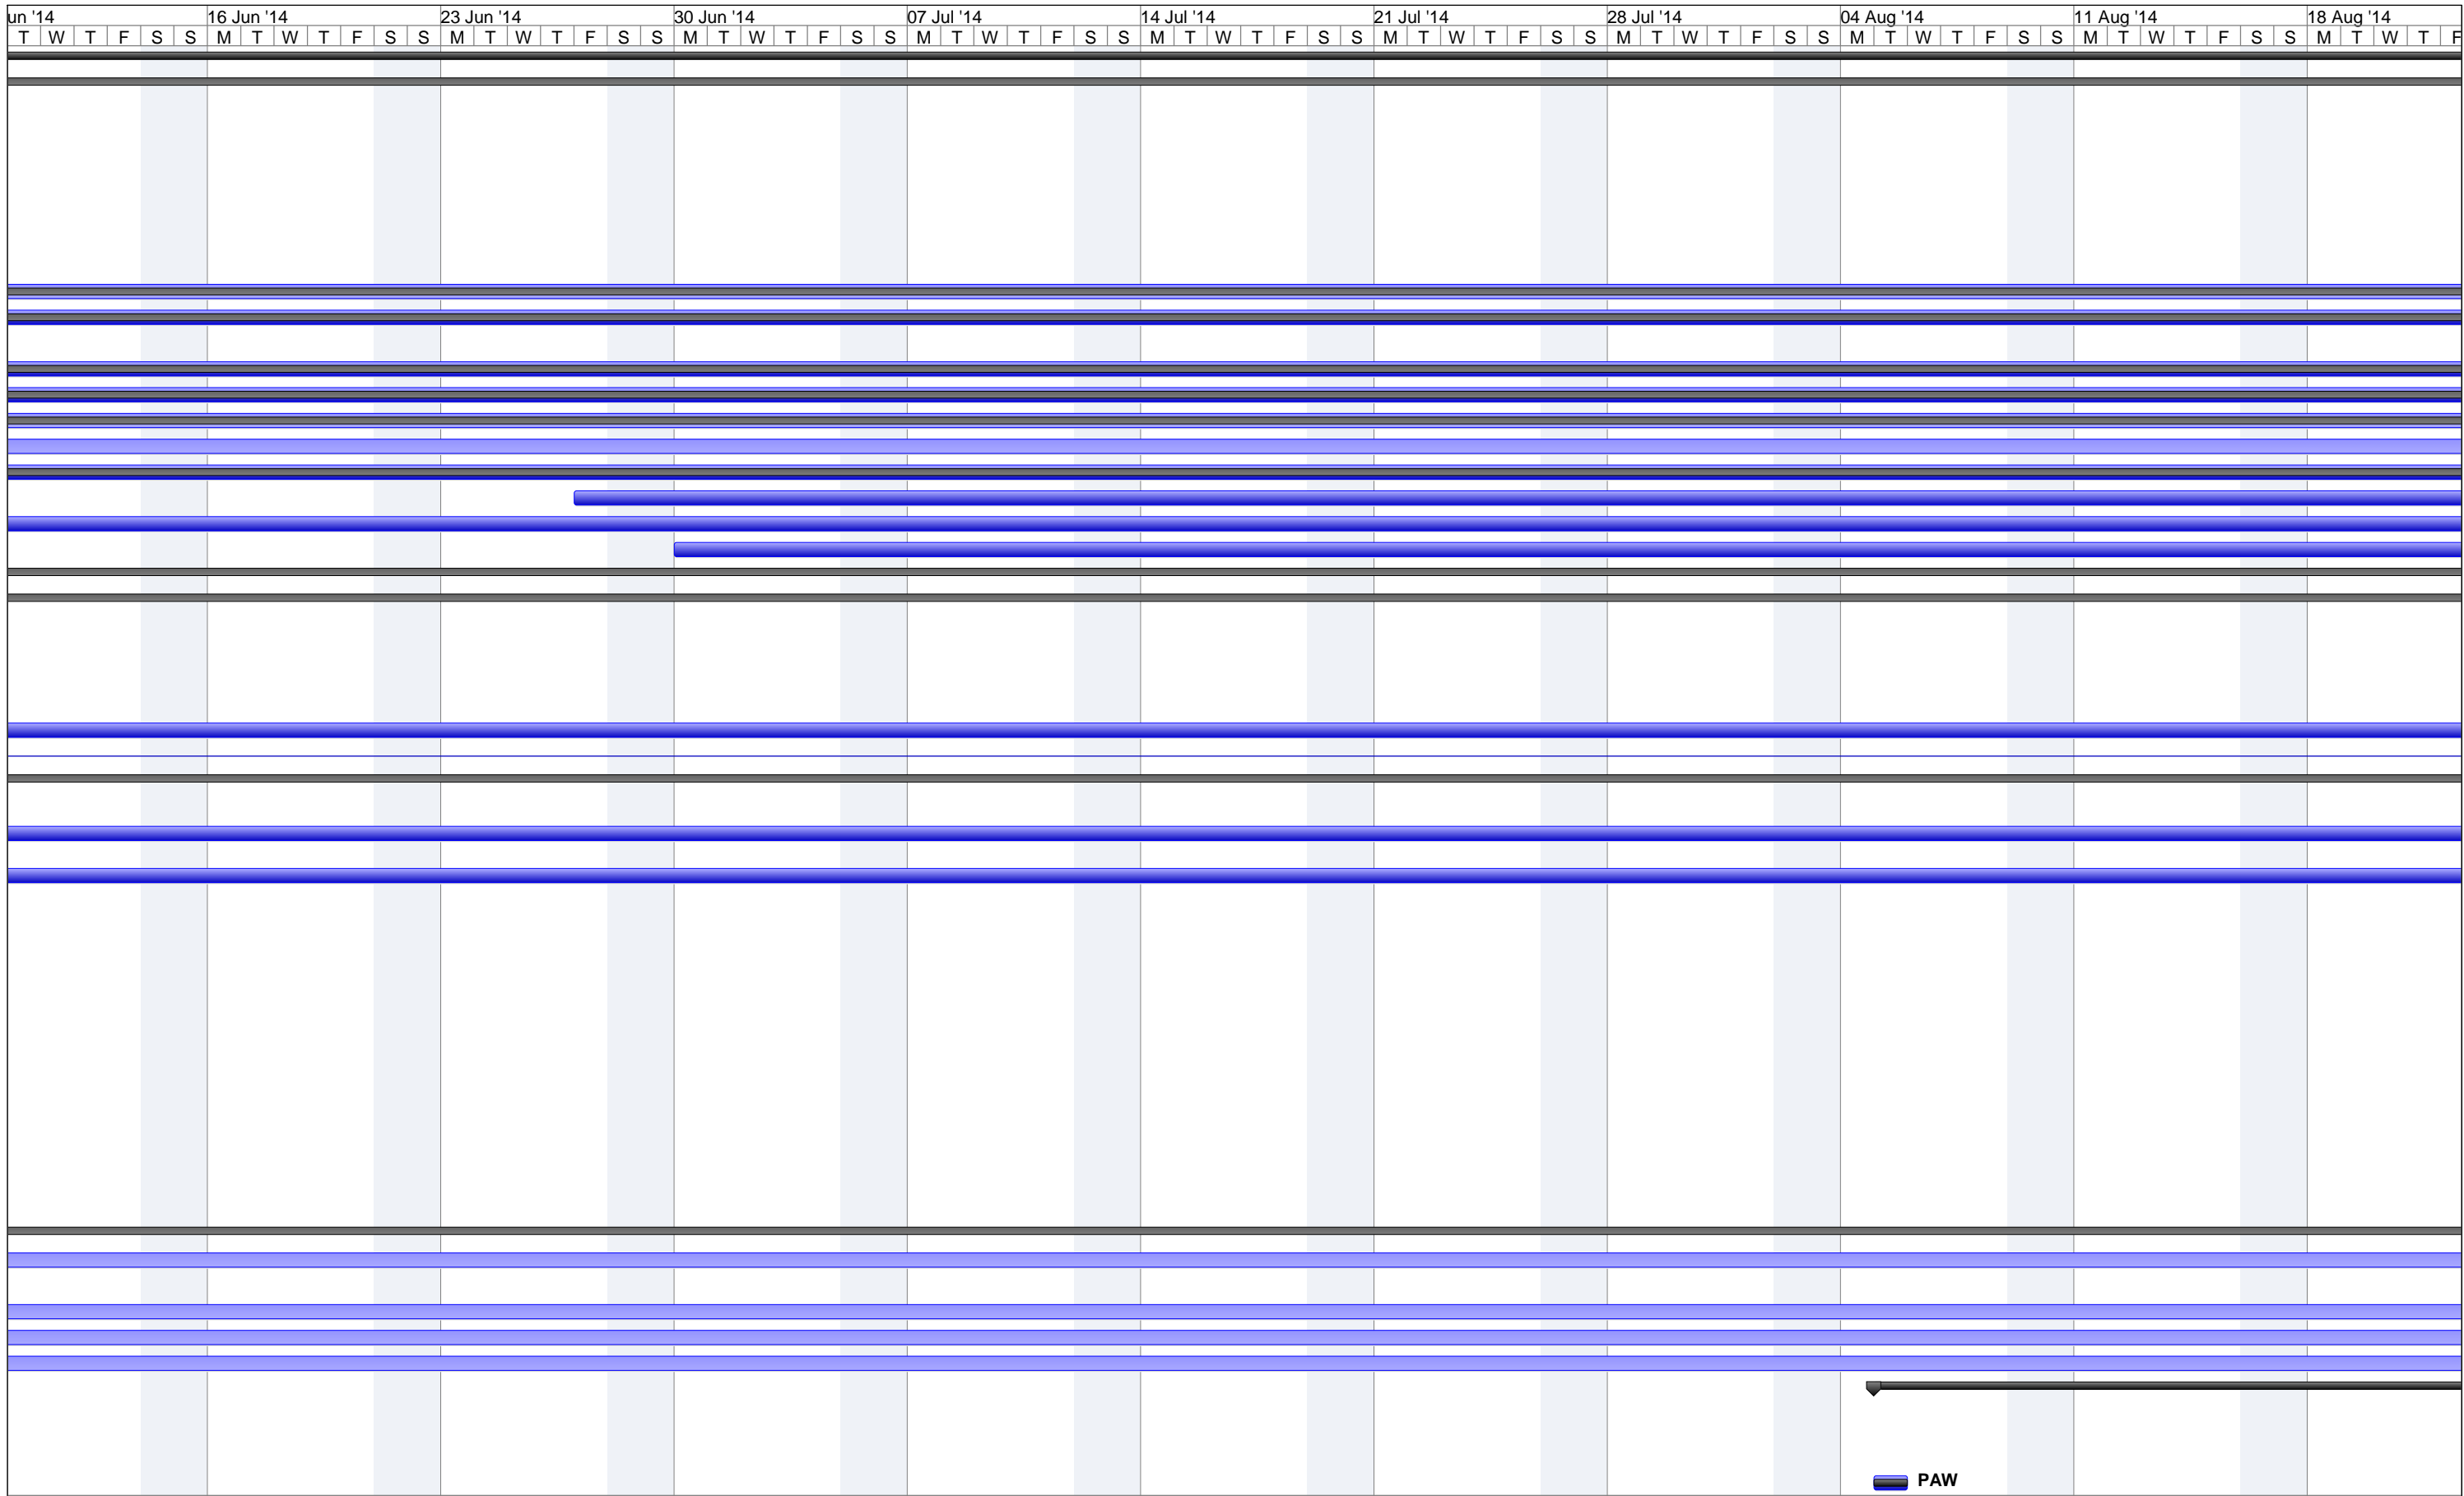


Project: Performance Assurance Plan
Date: Mon 02/02/15


Task
Split
Milestone
Summary




Project Summary
External Tasks
External Milestone
Inactive Task



Inactive Milestone
Inactive Summary
Manual Task
Duration-only




Manual Summary Rollup
Manual Summary
Start-only
Finish-only




Progress
Deadline



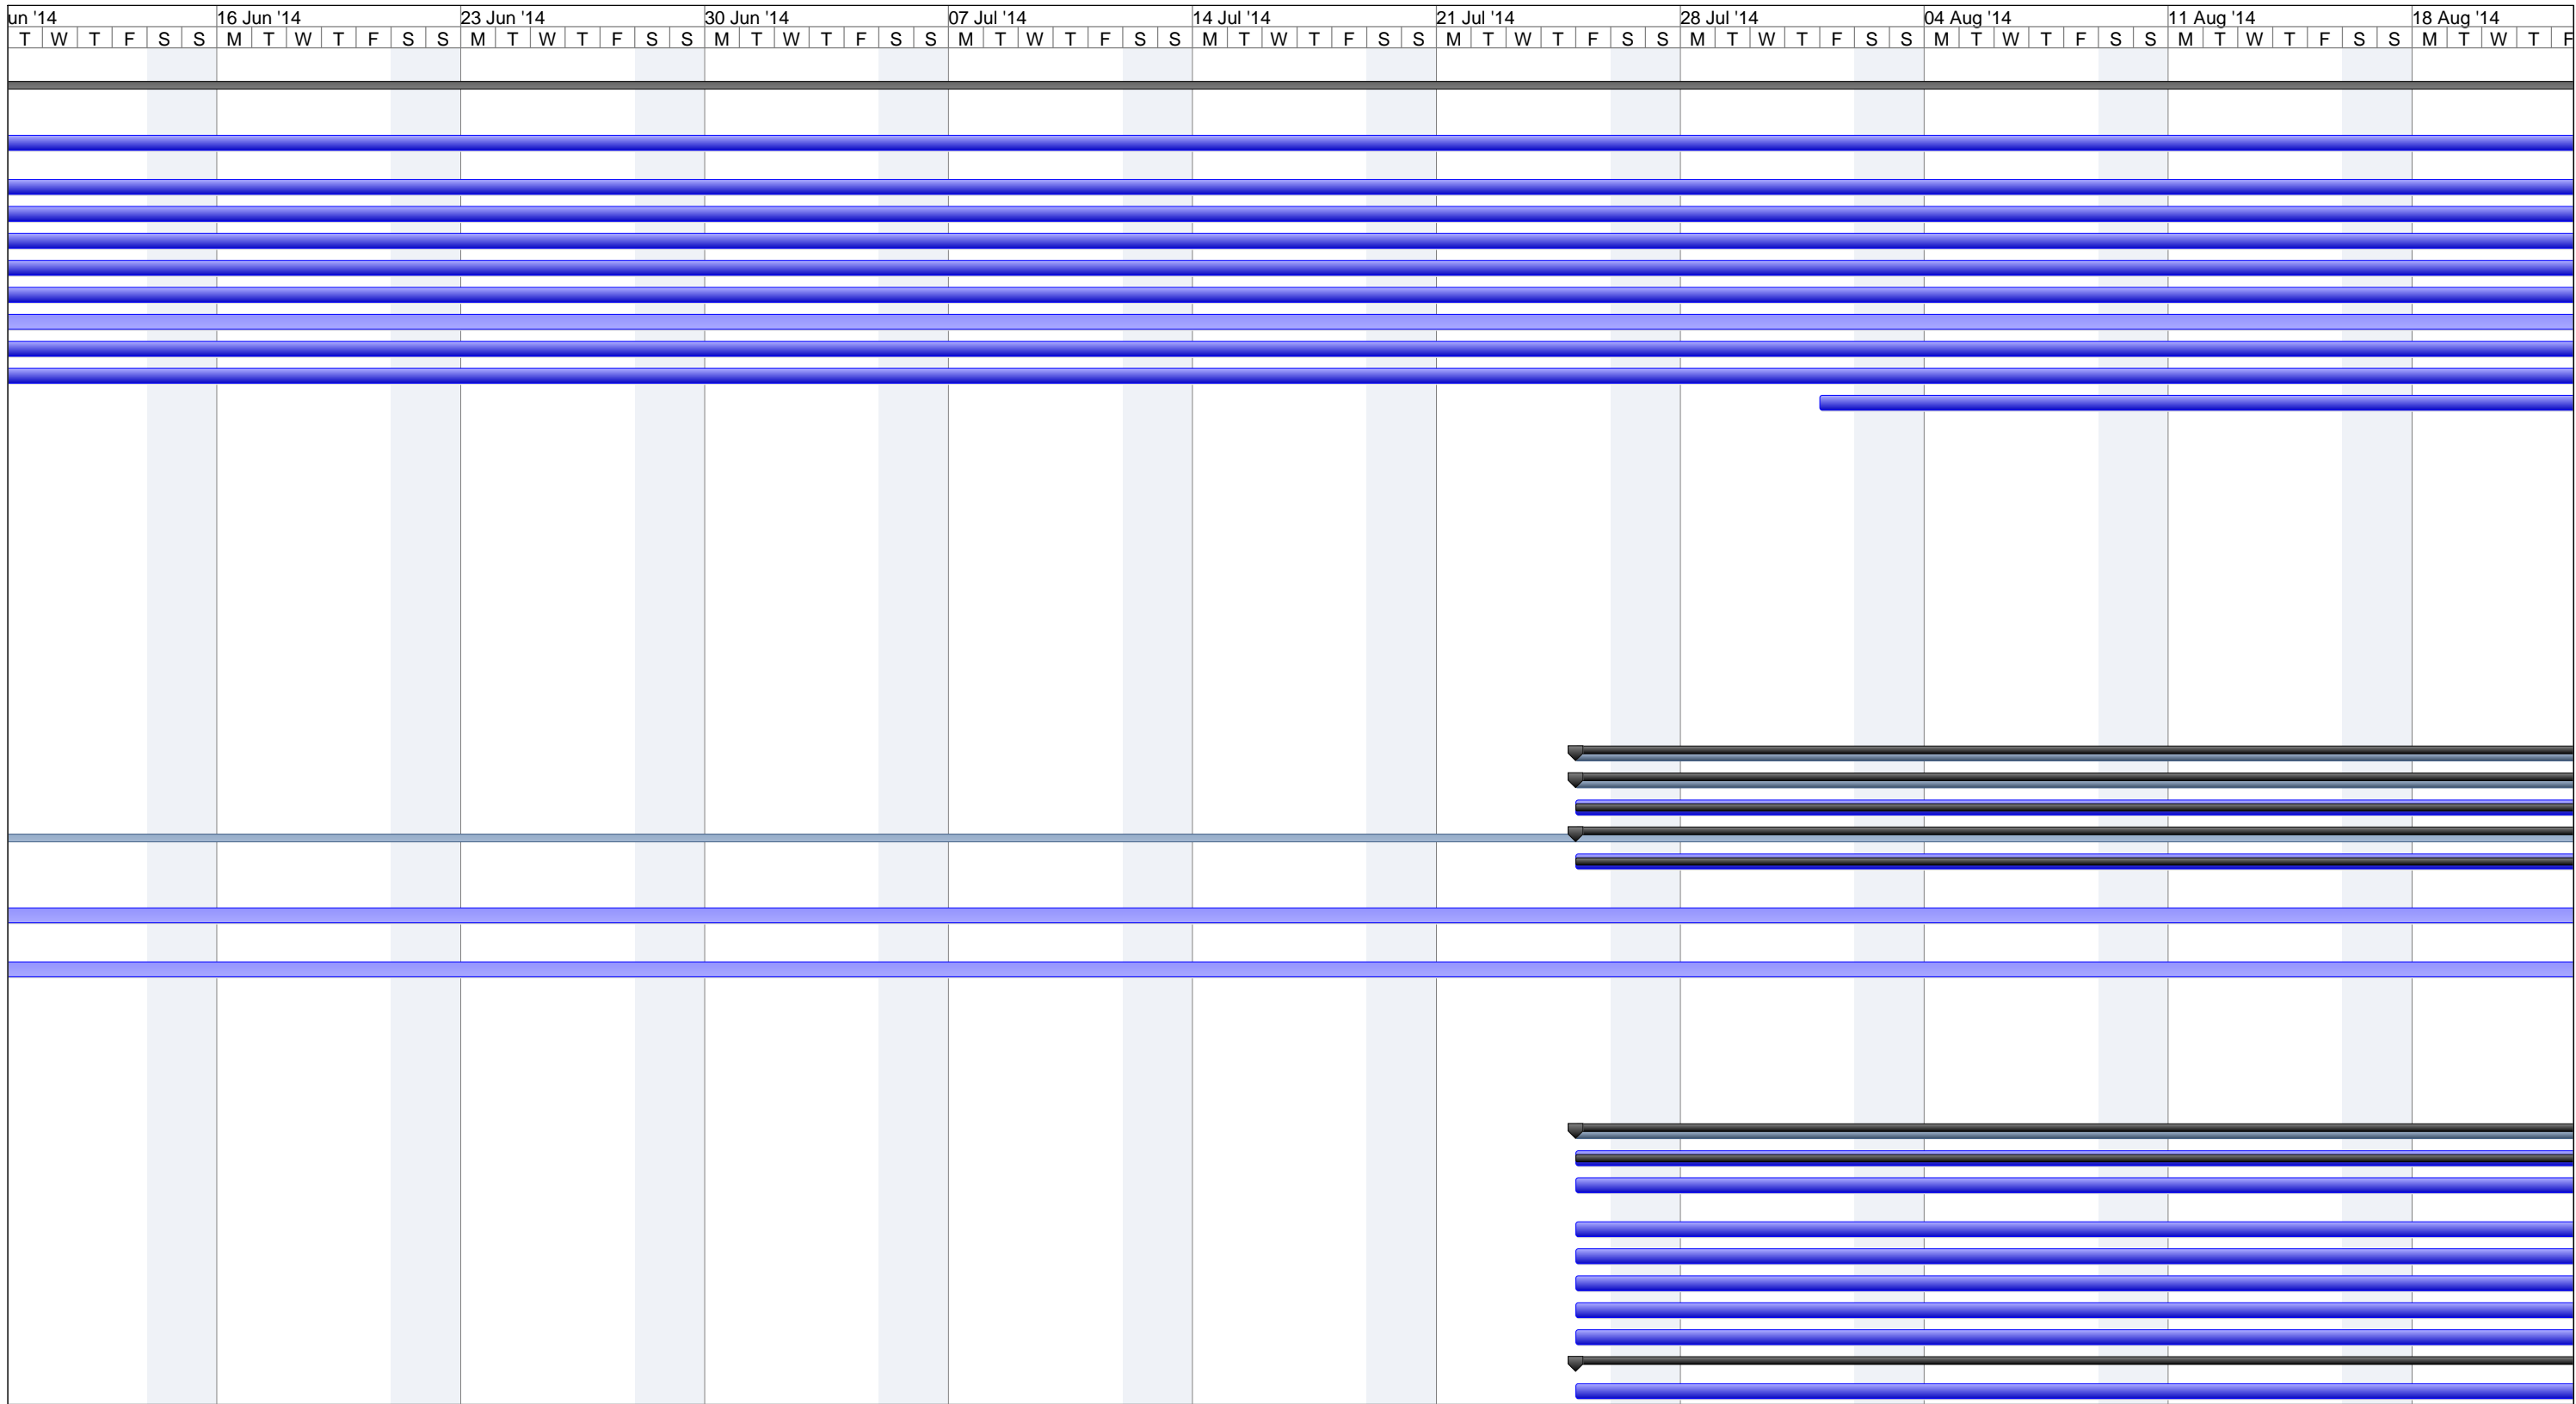



Project: Performance Assurance Plan
Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

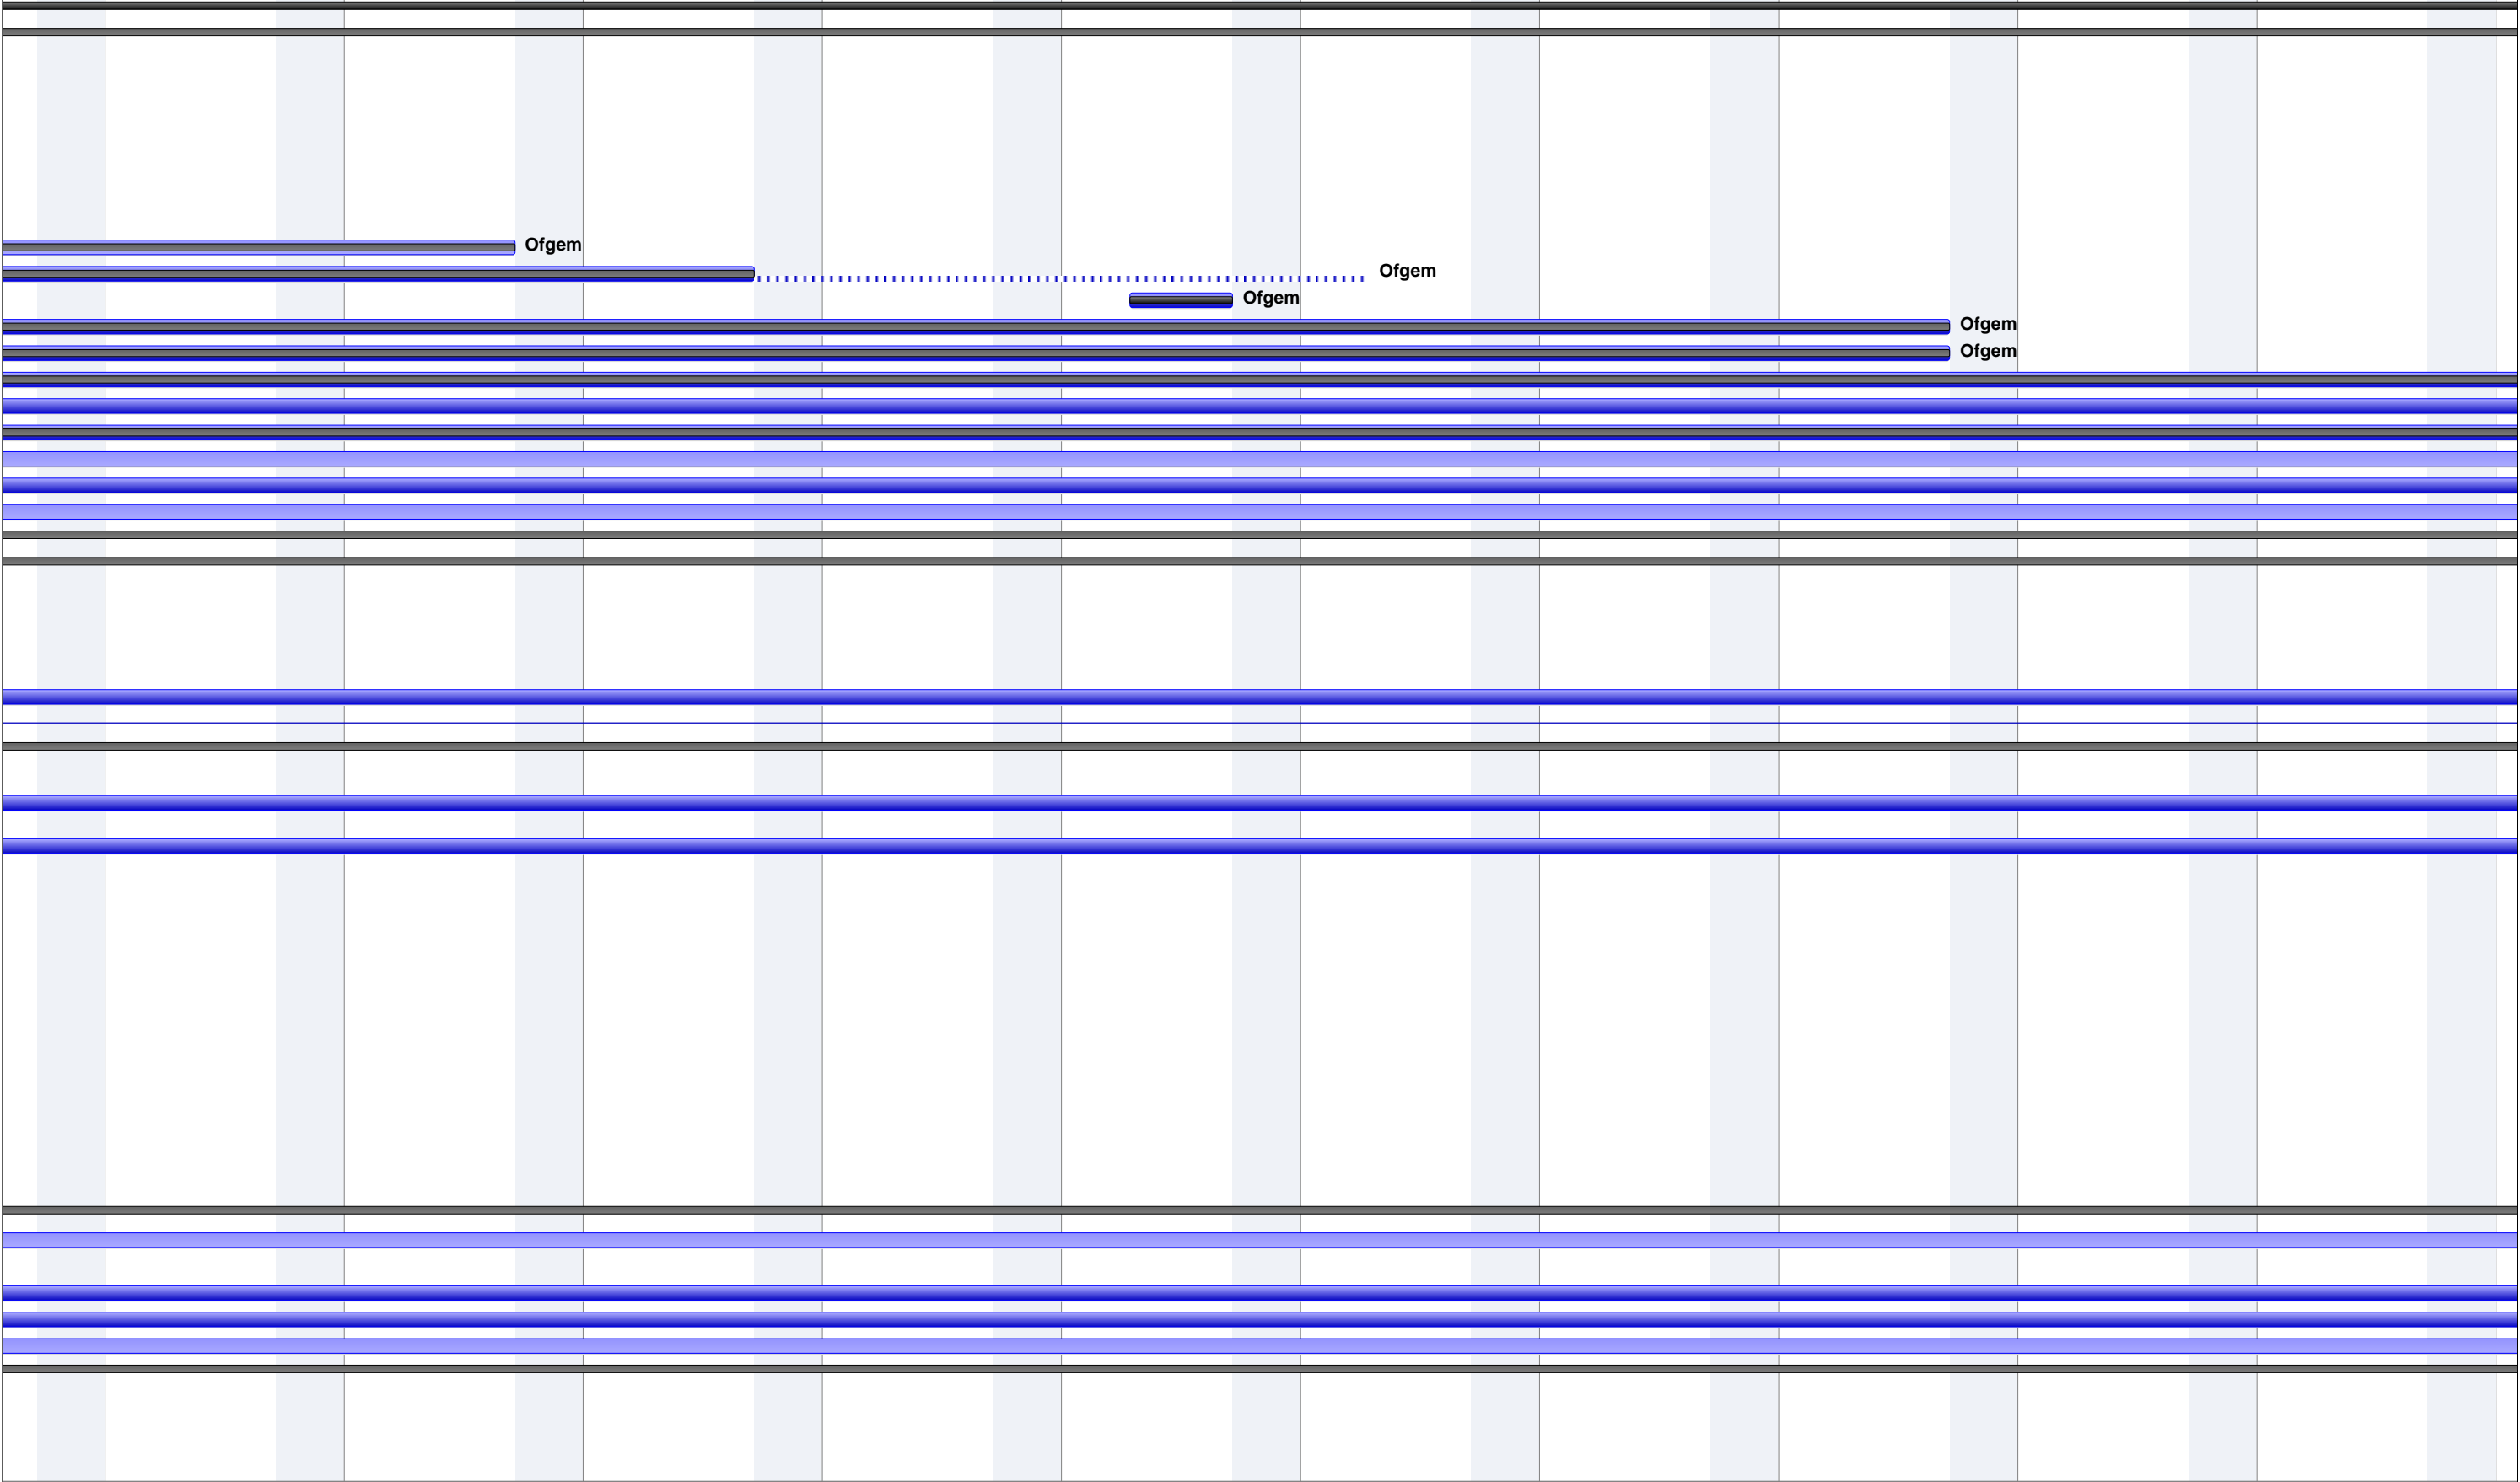


Project: Performance Assurance Plan
Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

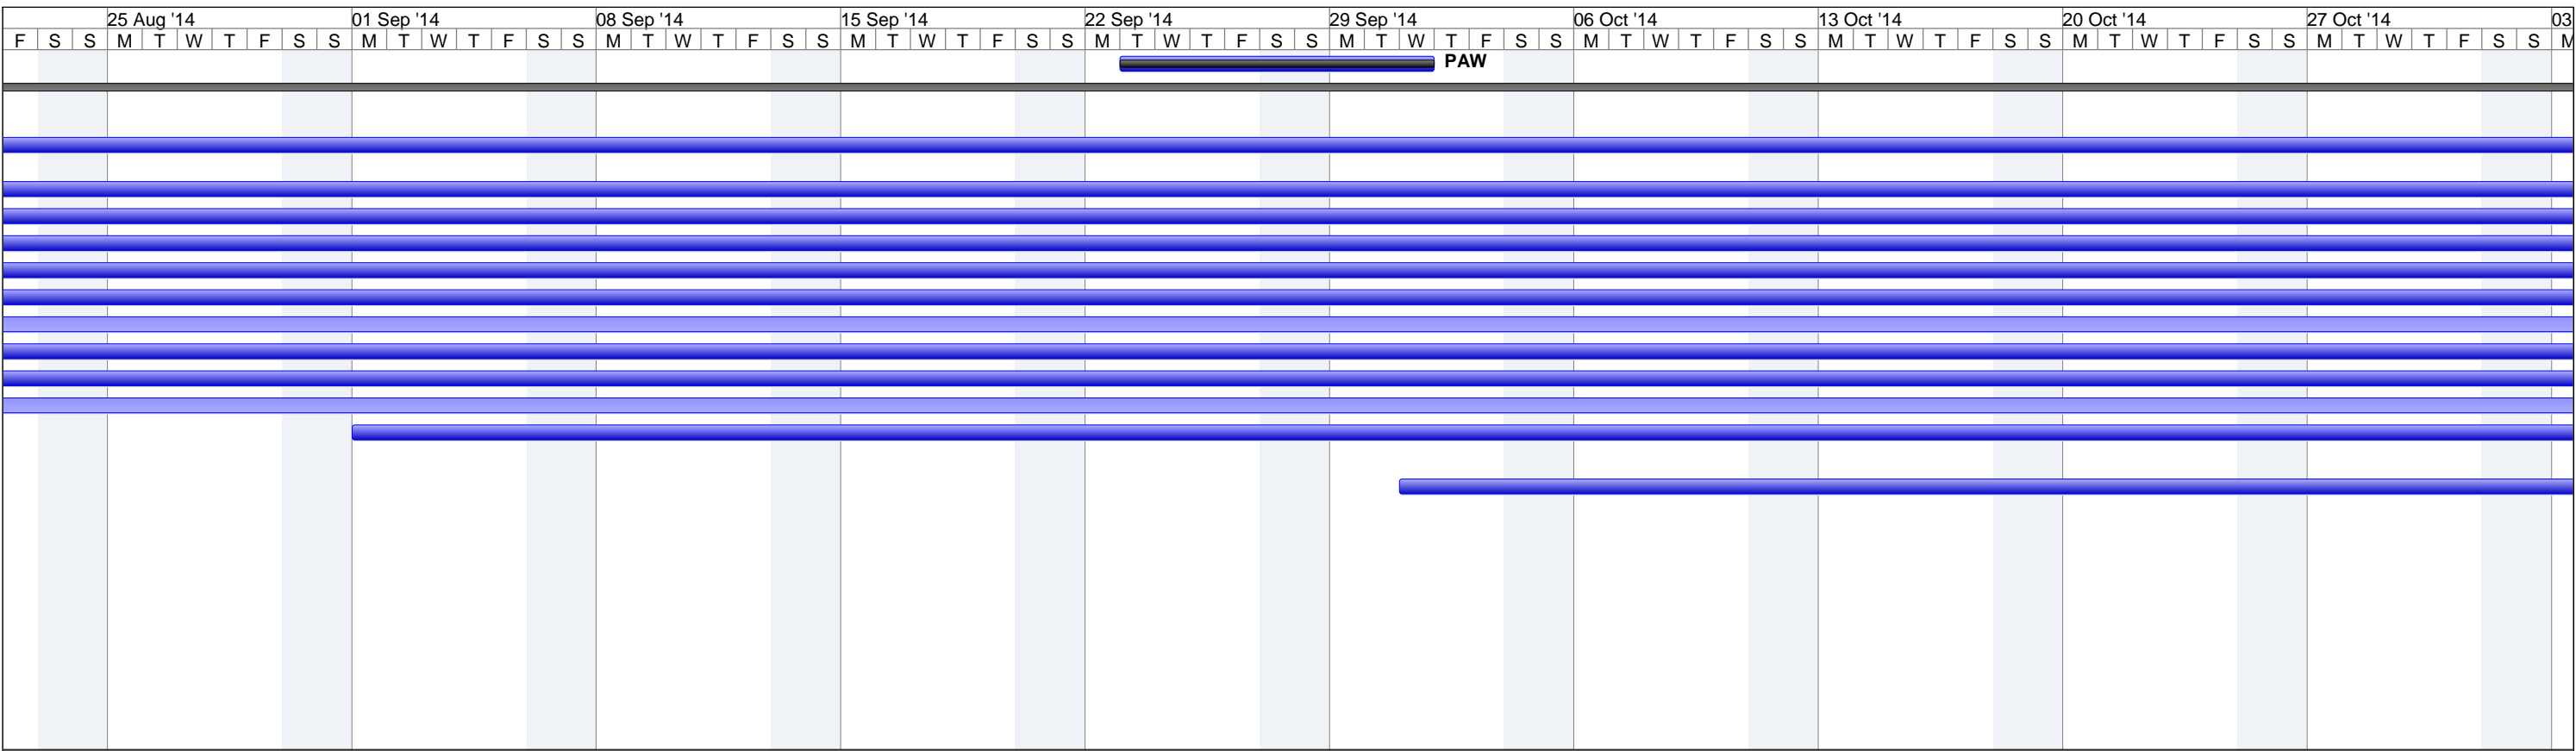

Project: Performance Assurance Plan Date: Mon 02/02/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			


03 Nov '14 10 Nov '14 17 Nov '14 24 Nov '14 01 Dec '14 08 Dec '14 15 Dec '14 22 Dec '14 29 Dec '14 05 Jan '15 12 Jan '15
M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S

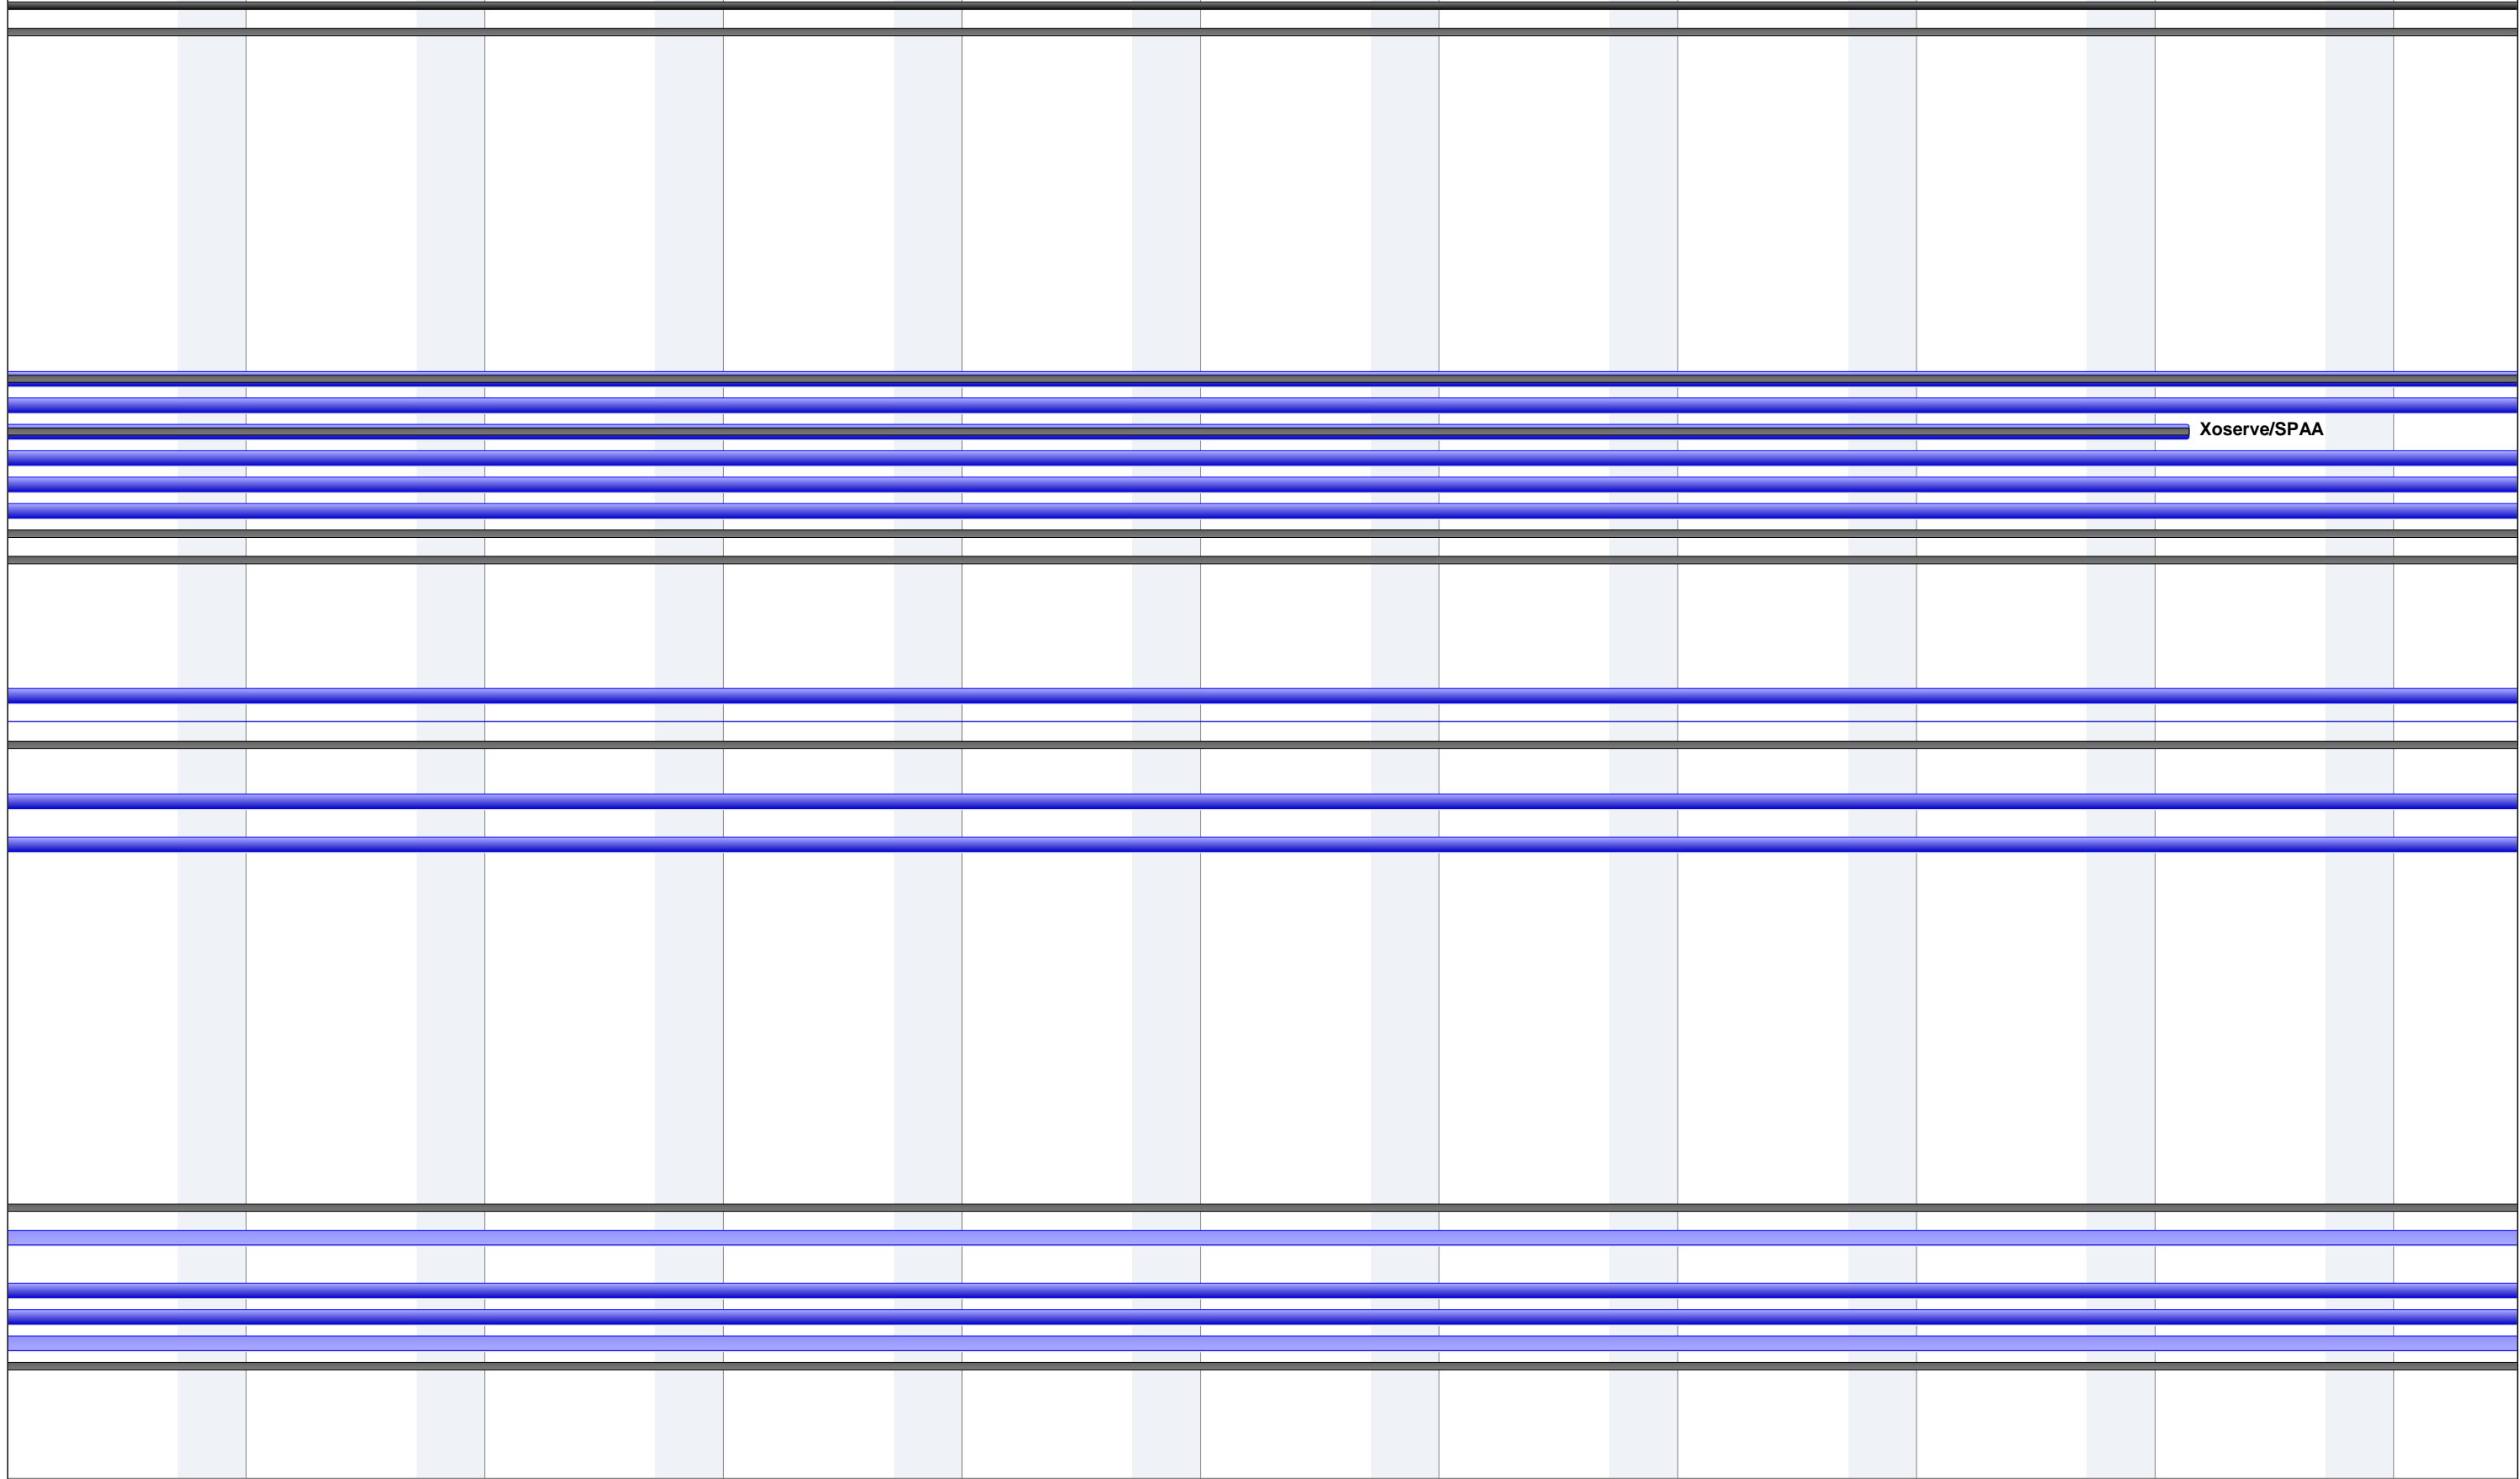

Xoserve/SPAA


Project: Performance Assurance Plan Date: Mon 02/02/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

03 Nov '14 10 Nov '14 17 Nov '14 24 Nov '14 01 Dec '14 08 Dec '14 15 Dec '14 22 Dec '14 29 Dec '14 05 Jan '15 12 Jan '15
M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T

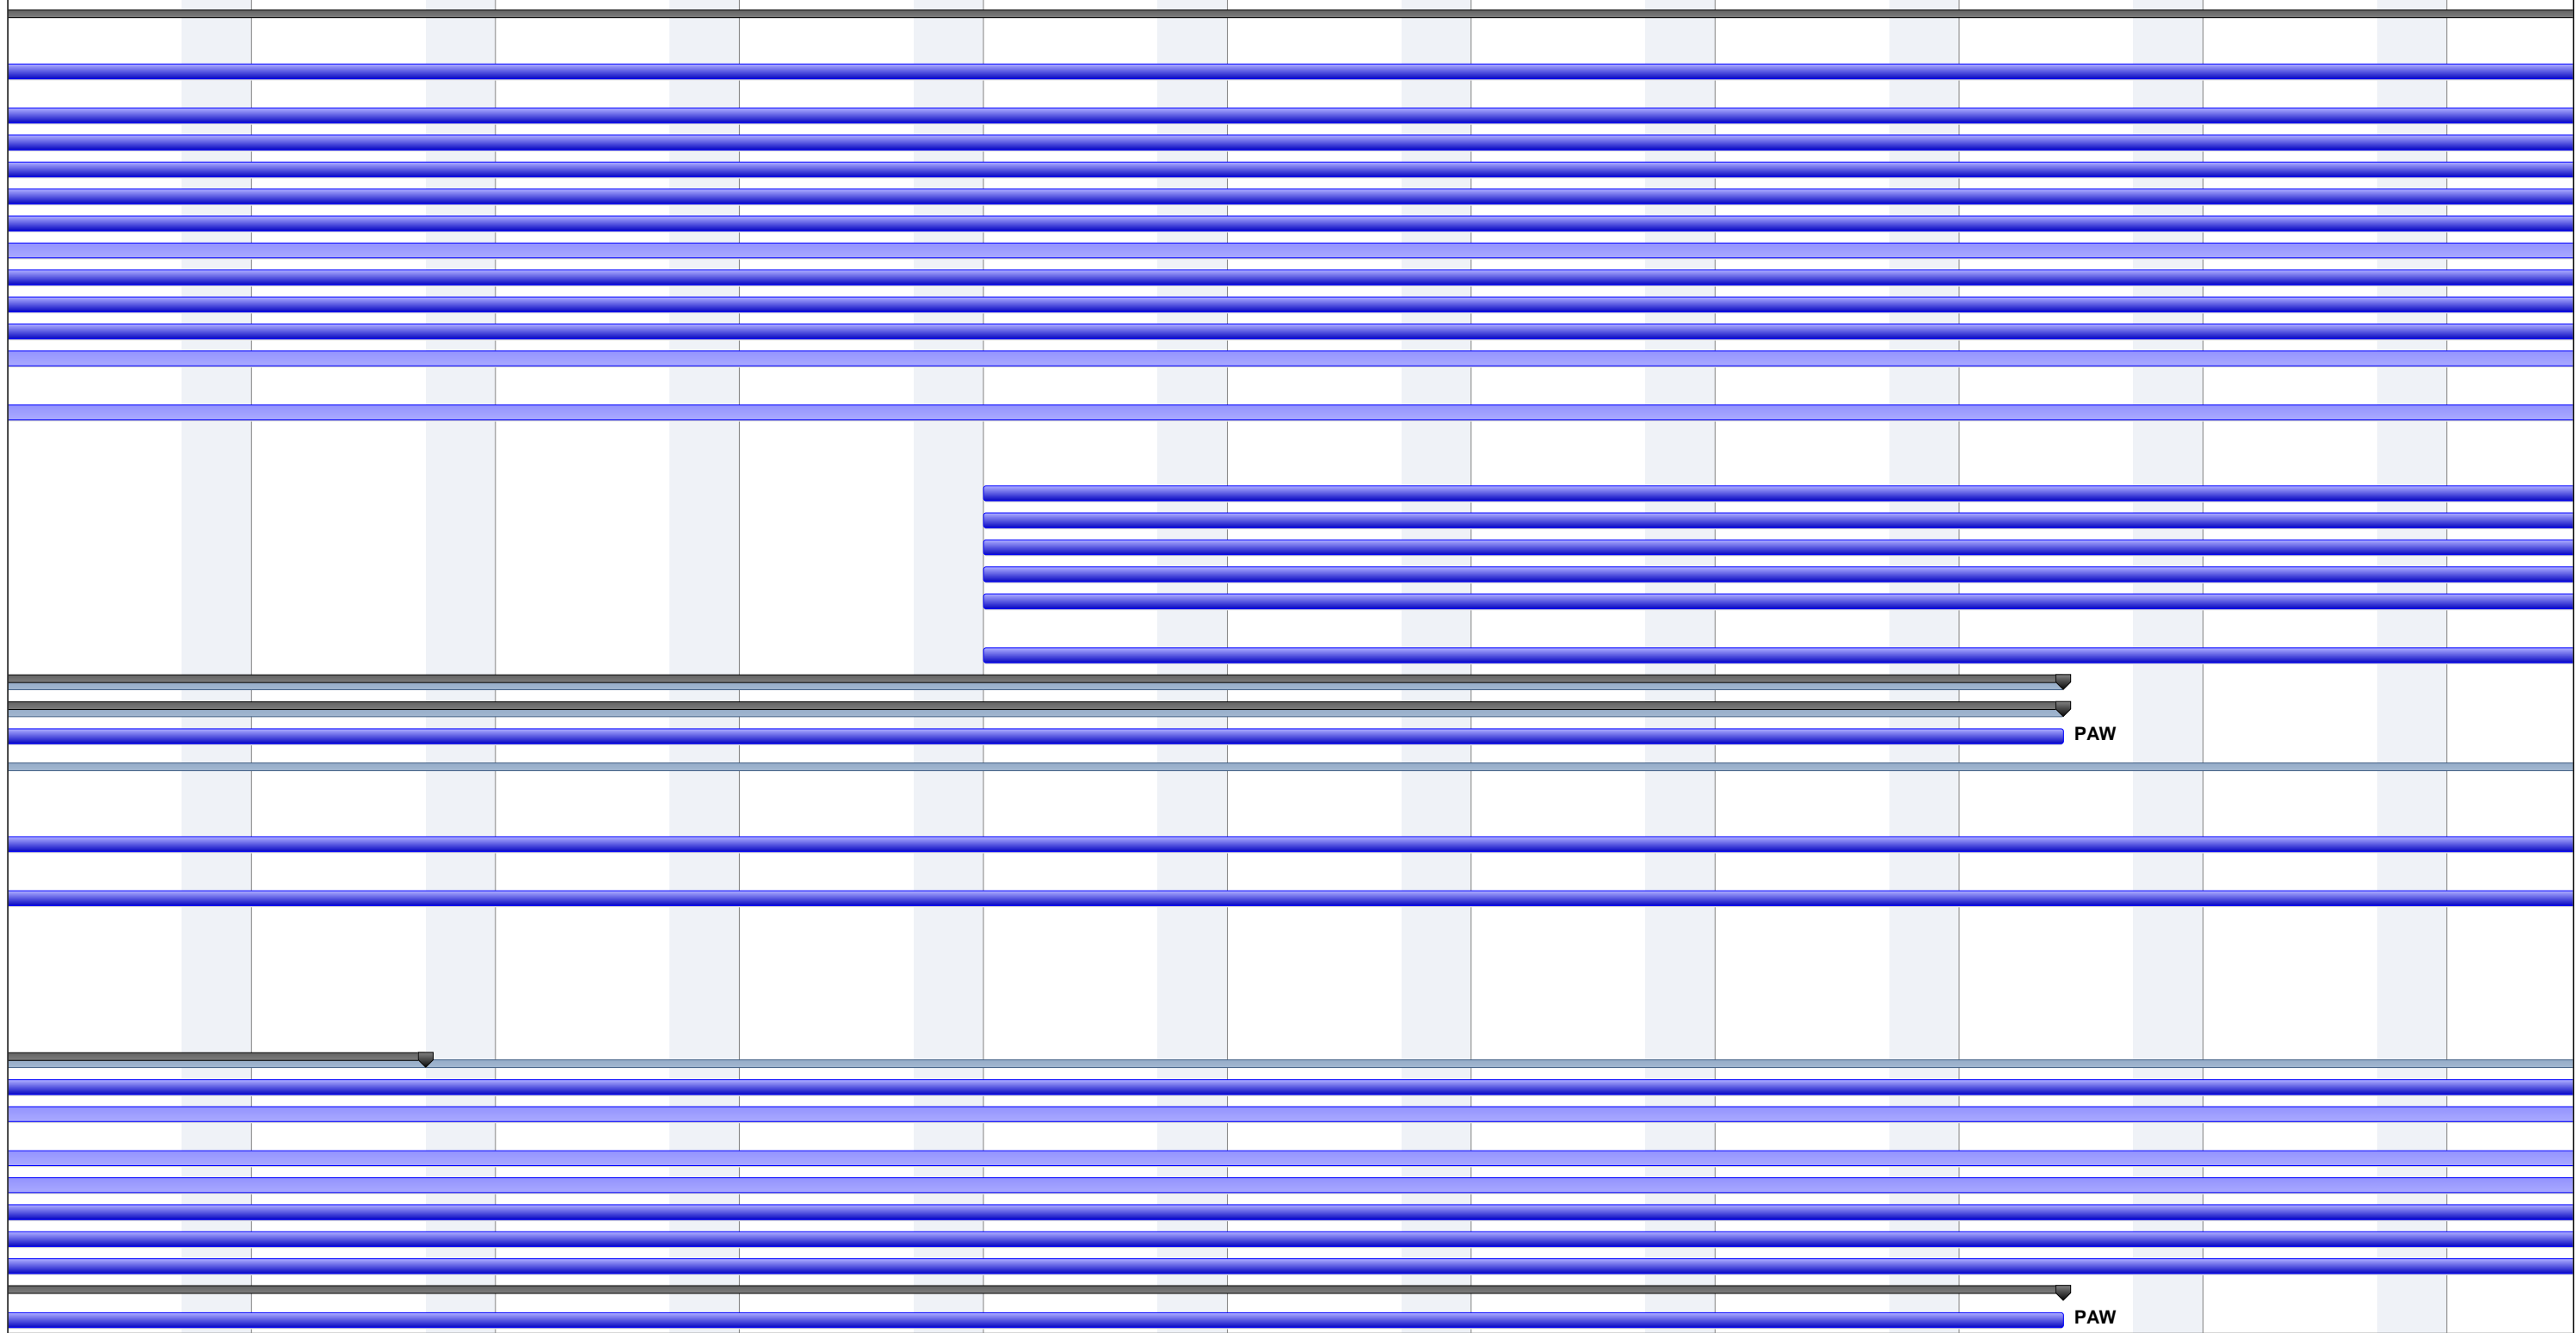

Project: Performance Assurance Plan
Date: Mon 02/02/15


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

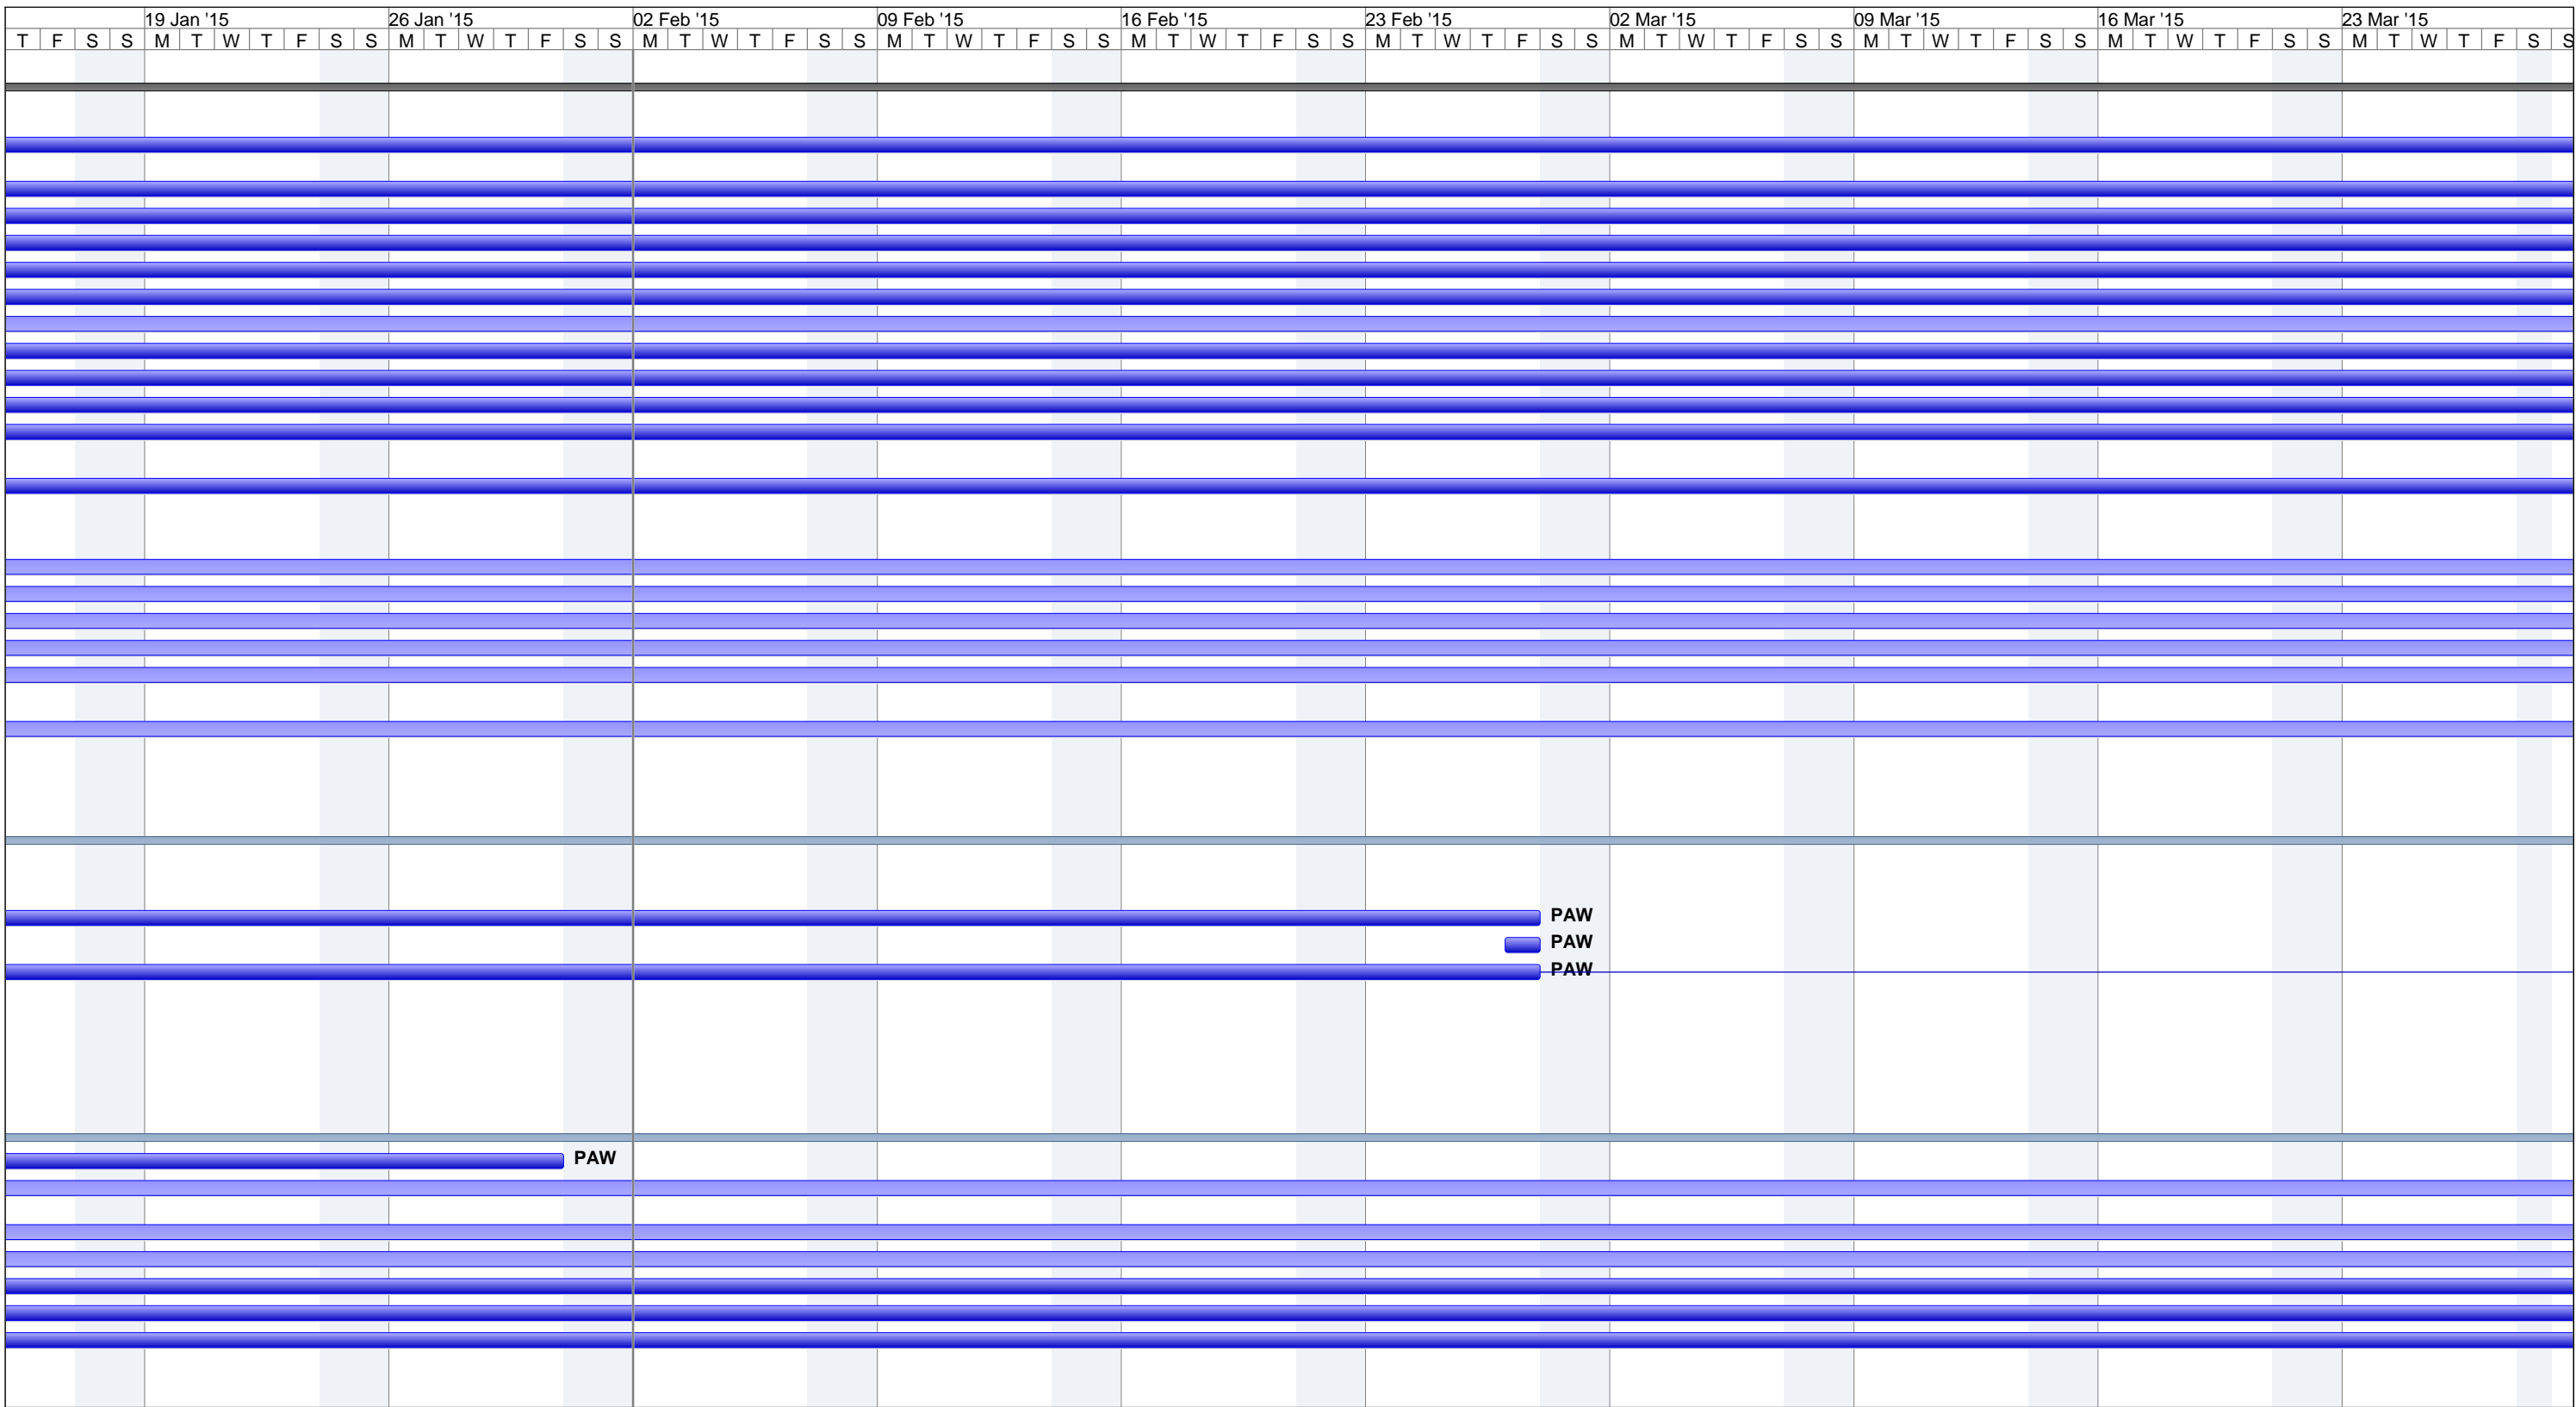

Project: Performance Assurance Plan
Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			


30 Mar '15 06 Apr '15 13 Apr '15 20 Apr '15 27 Apr '15 04 May '15 11 May '15 18 May '15 25 May '15 01 Jun '15 08 Jun '15

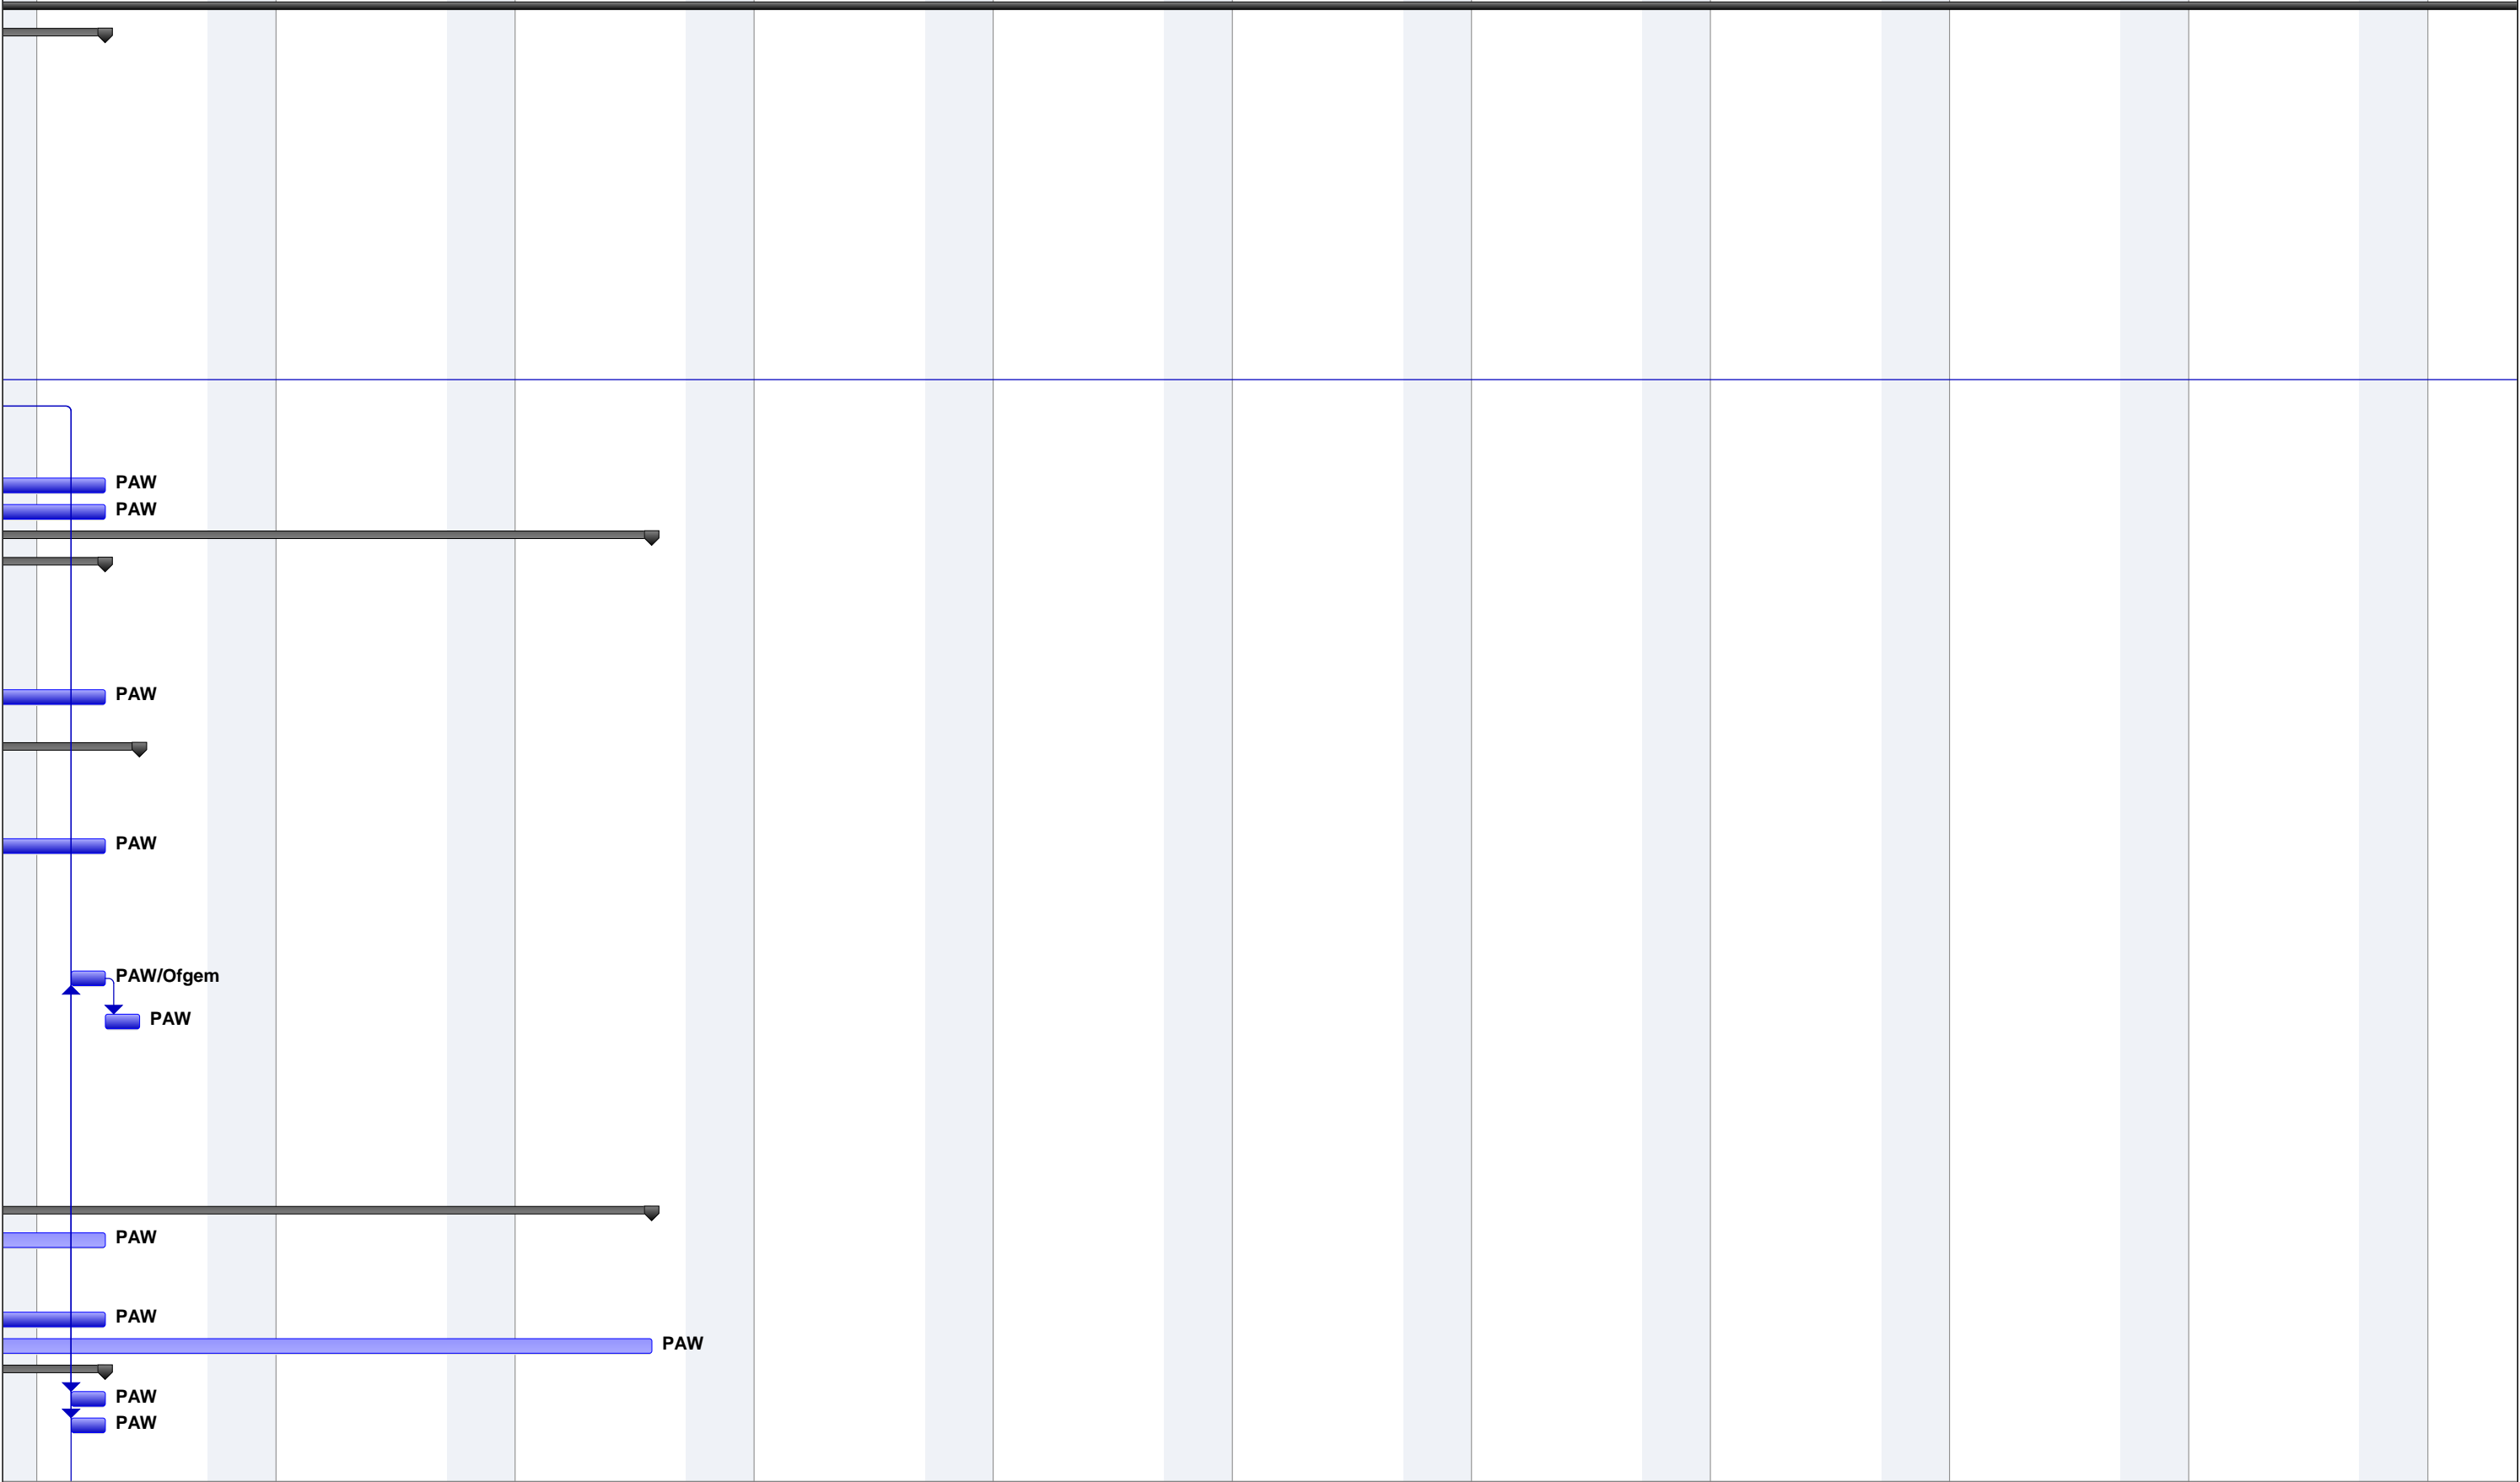

Project: Performance Assurance Plan
Date: Mon 02/02/15


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

30 Mar '15 06 Apr '15 13 Apr '15 20 Apr '15 27 Apr '15 04 May '15 11 May '15 18 May '15 25 May '15 01 Jun '15 08 Jun '15

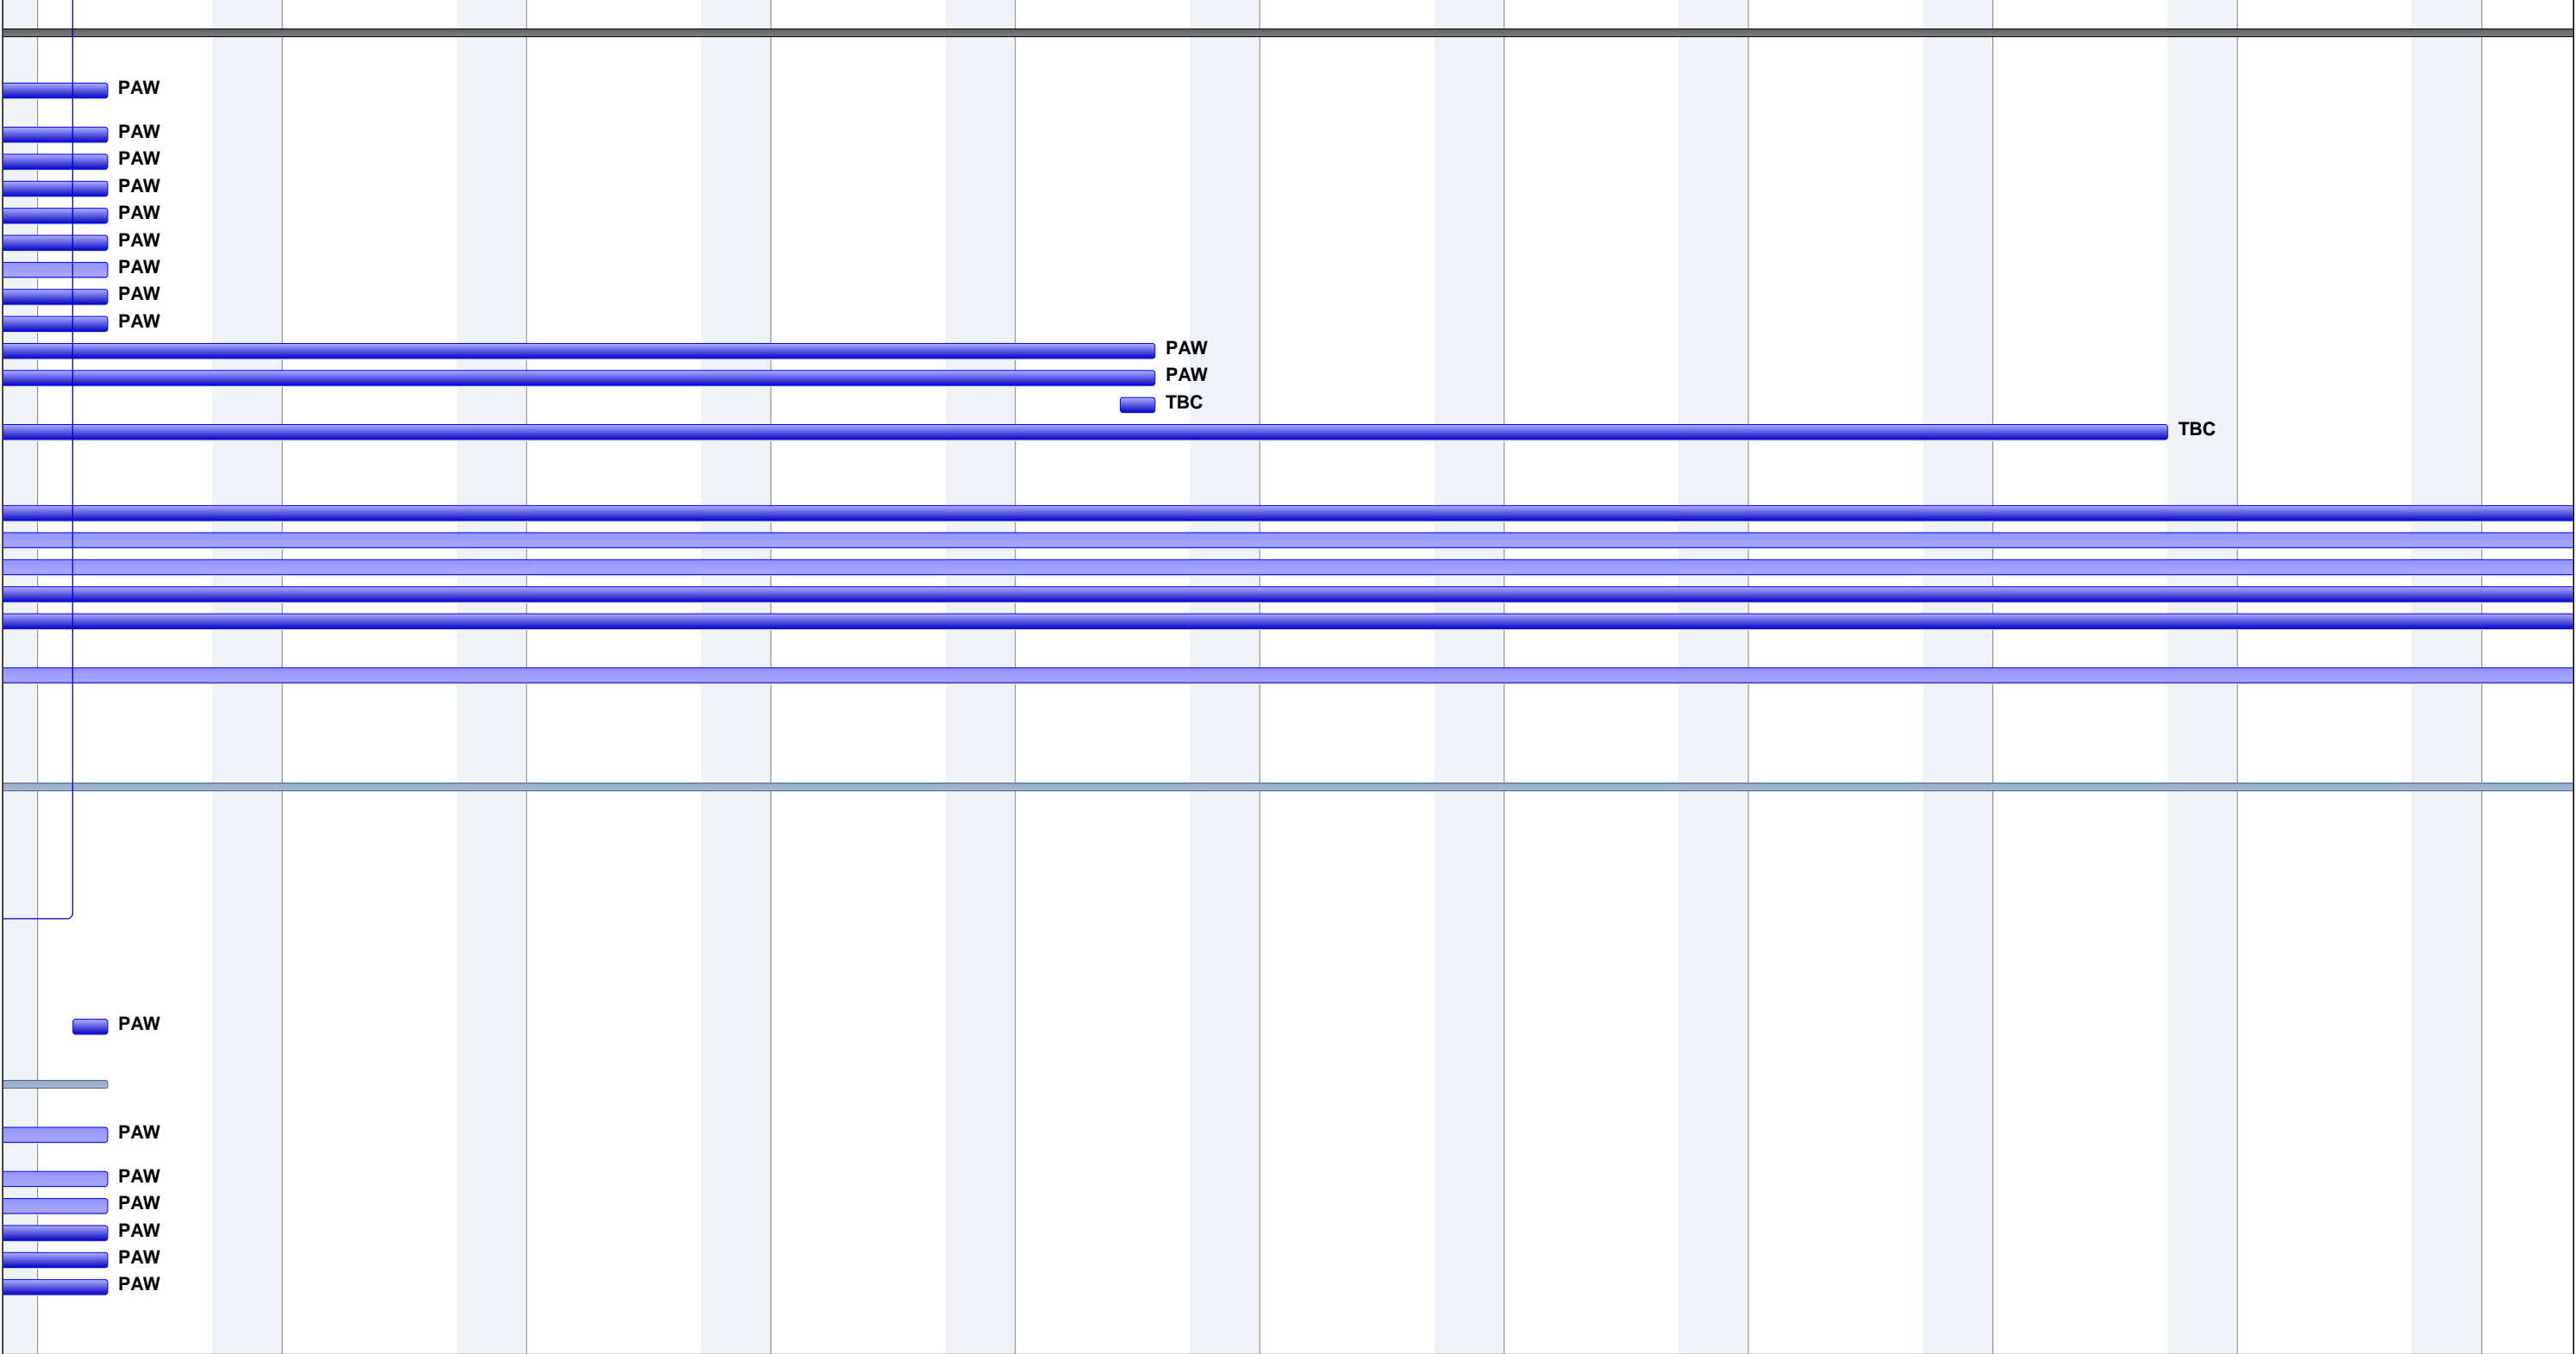

Project: Performance Assurance Plan
Date: Mon 02/02/15


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

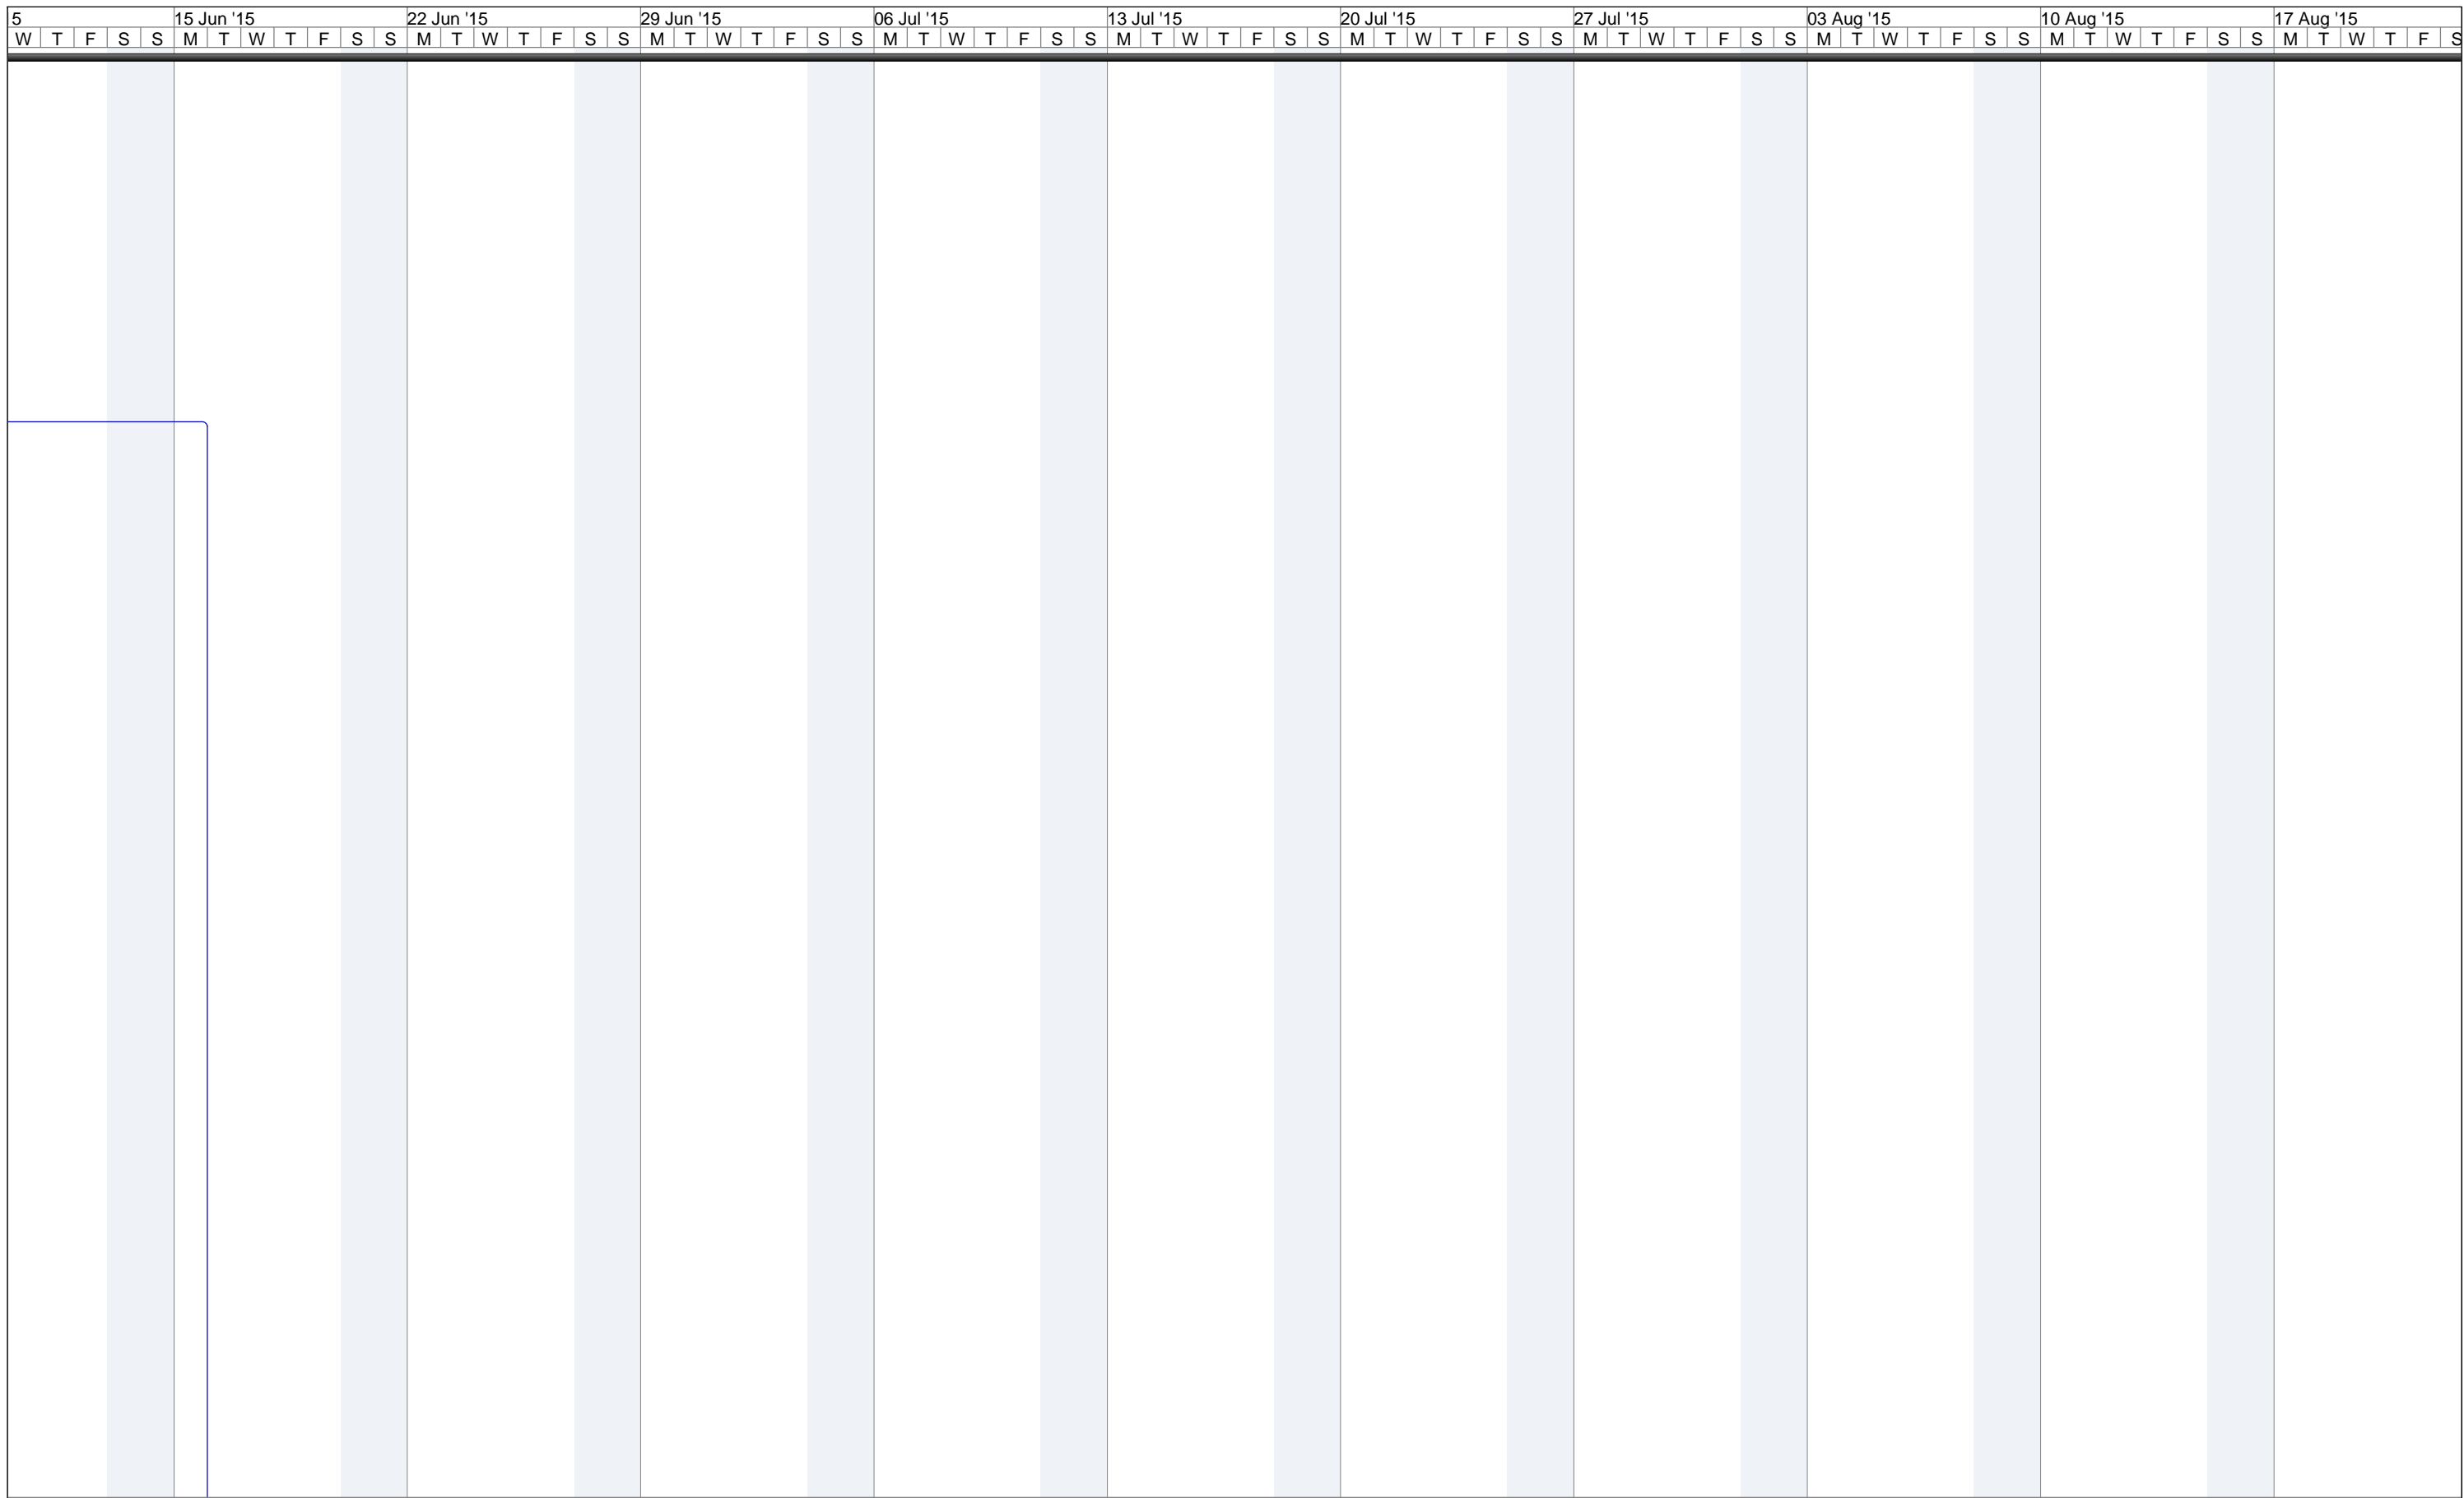

Project: Performance Assurance Plan
Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			


5 15 Jun '15 22 Jun '15 29 Jun '15 06 Jul '15 13 Jul '15 20 Jul '15 27 Jul '15 03 Aug '15 10 Aug '15 17 Aug '15
W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S



- PAW
- PAW
- PAW
- PAW


Project: Performance Assurance Plan
Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

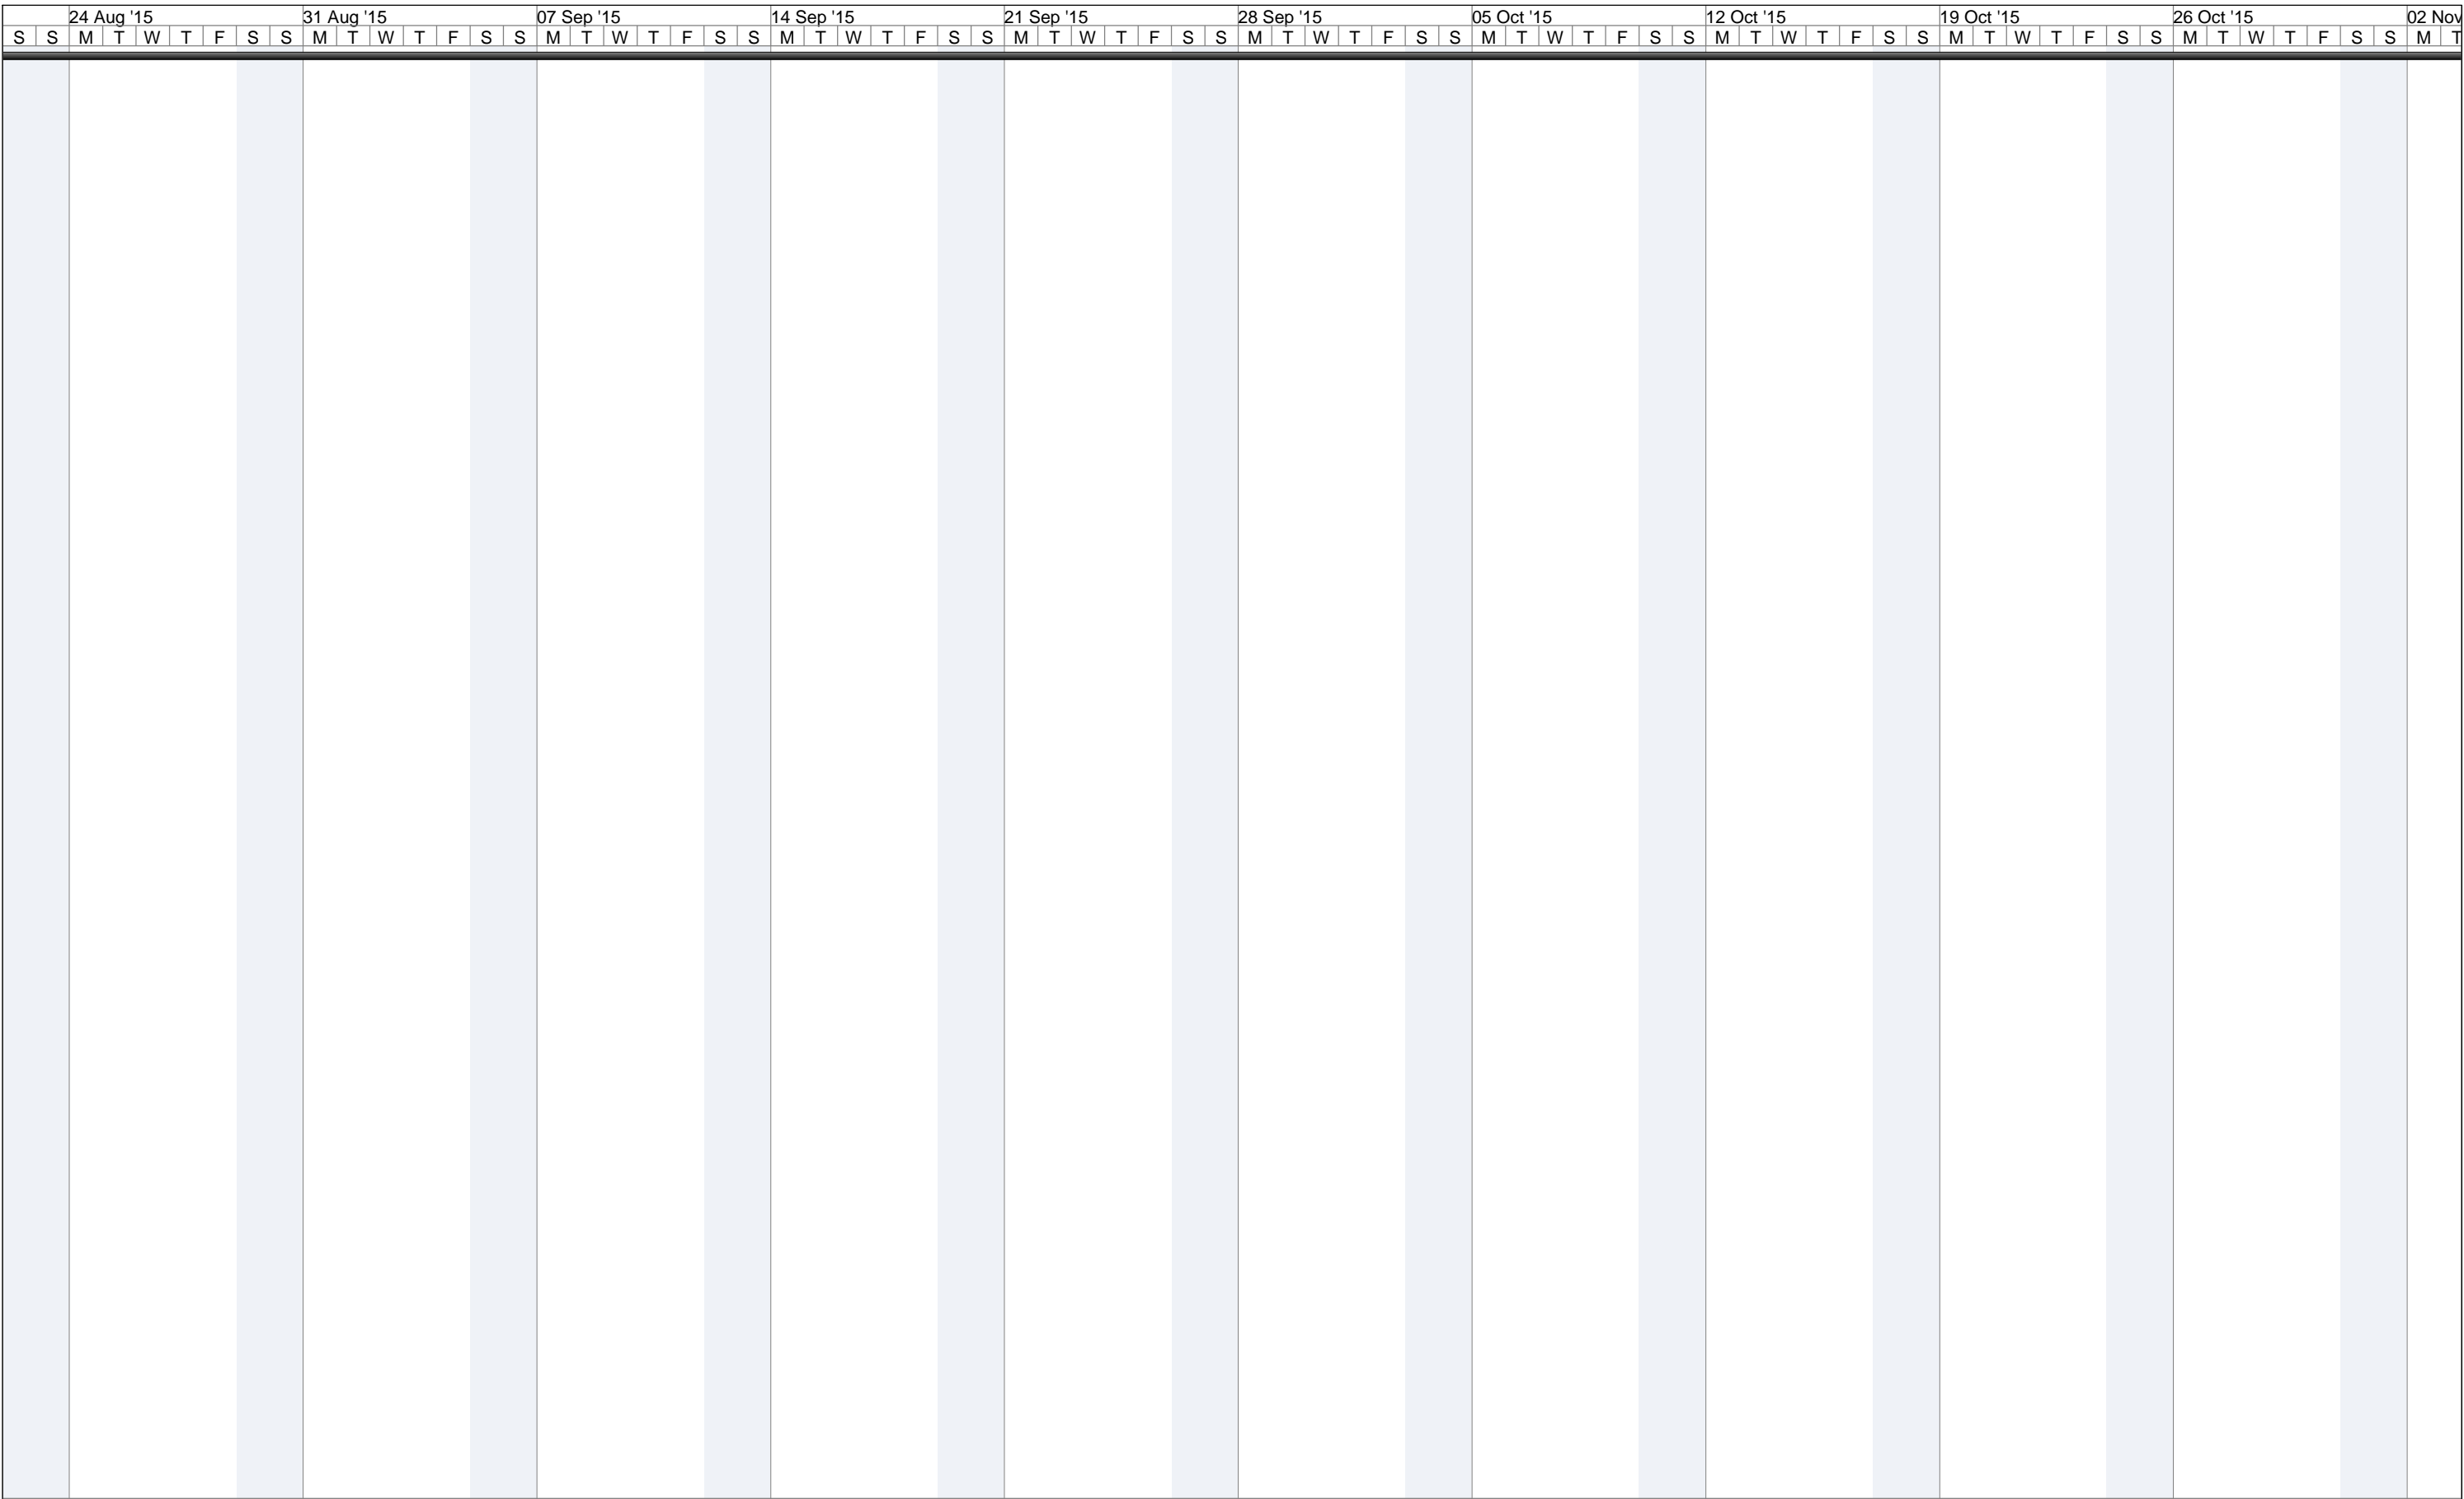

Project: Performance Assurance Plan
 Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

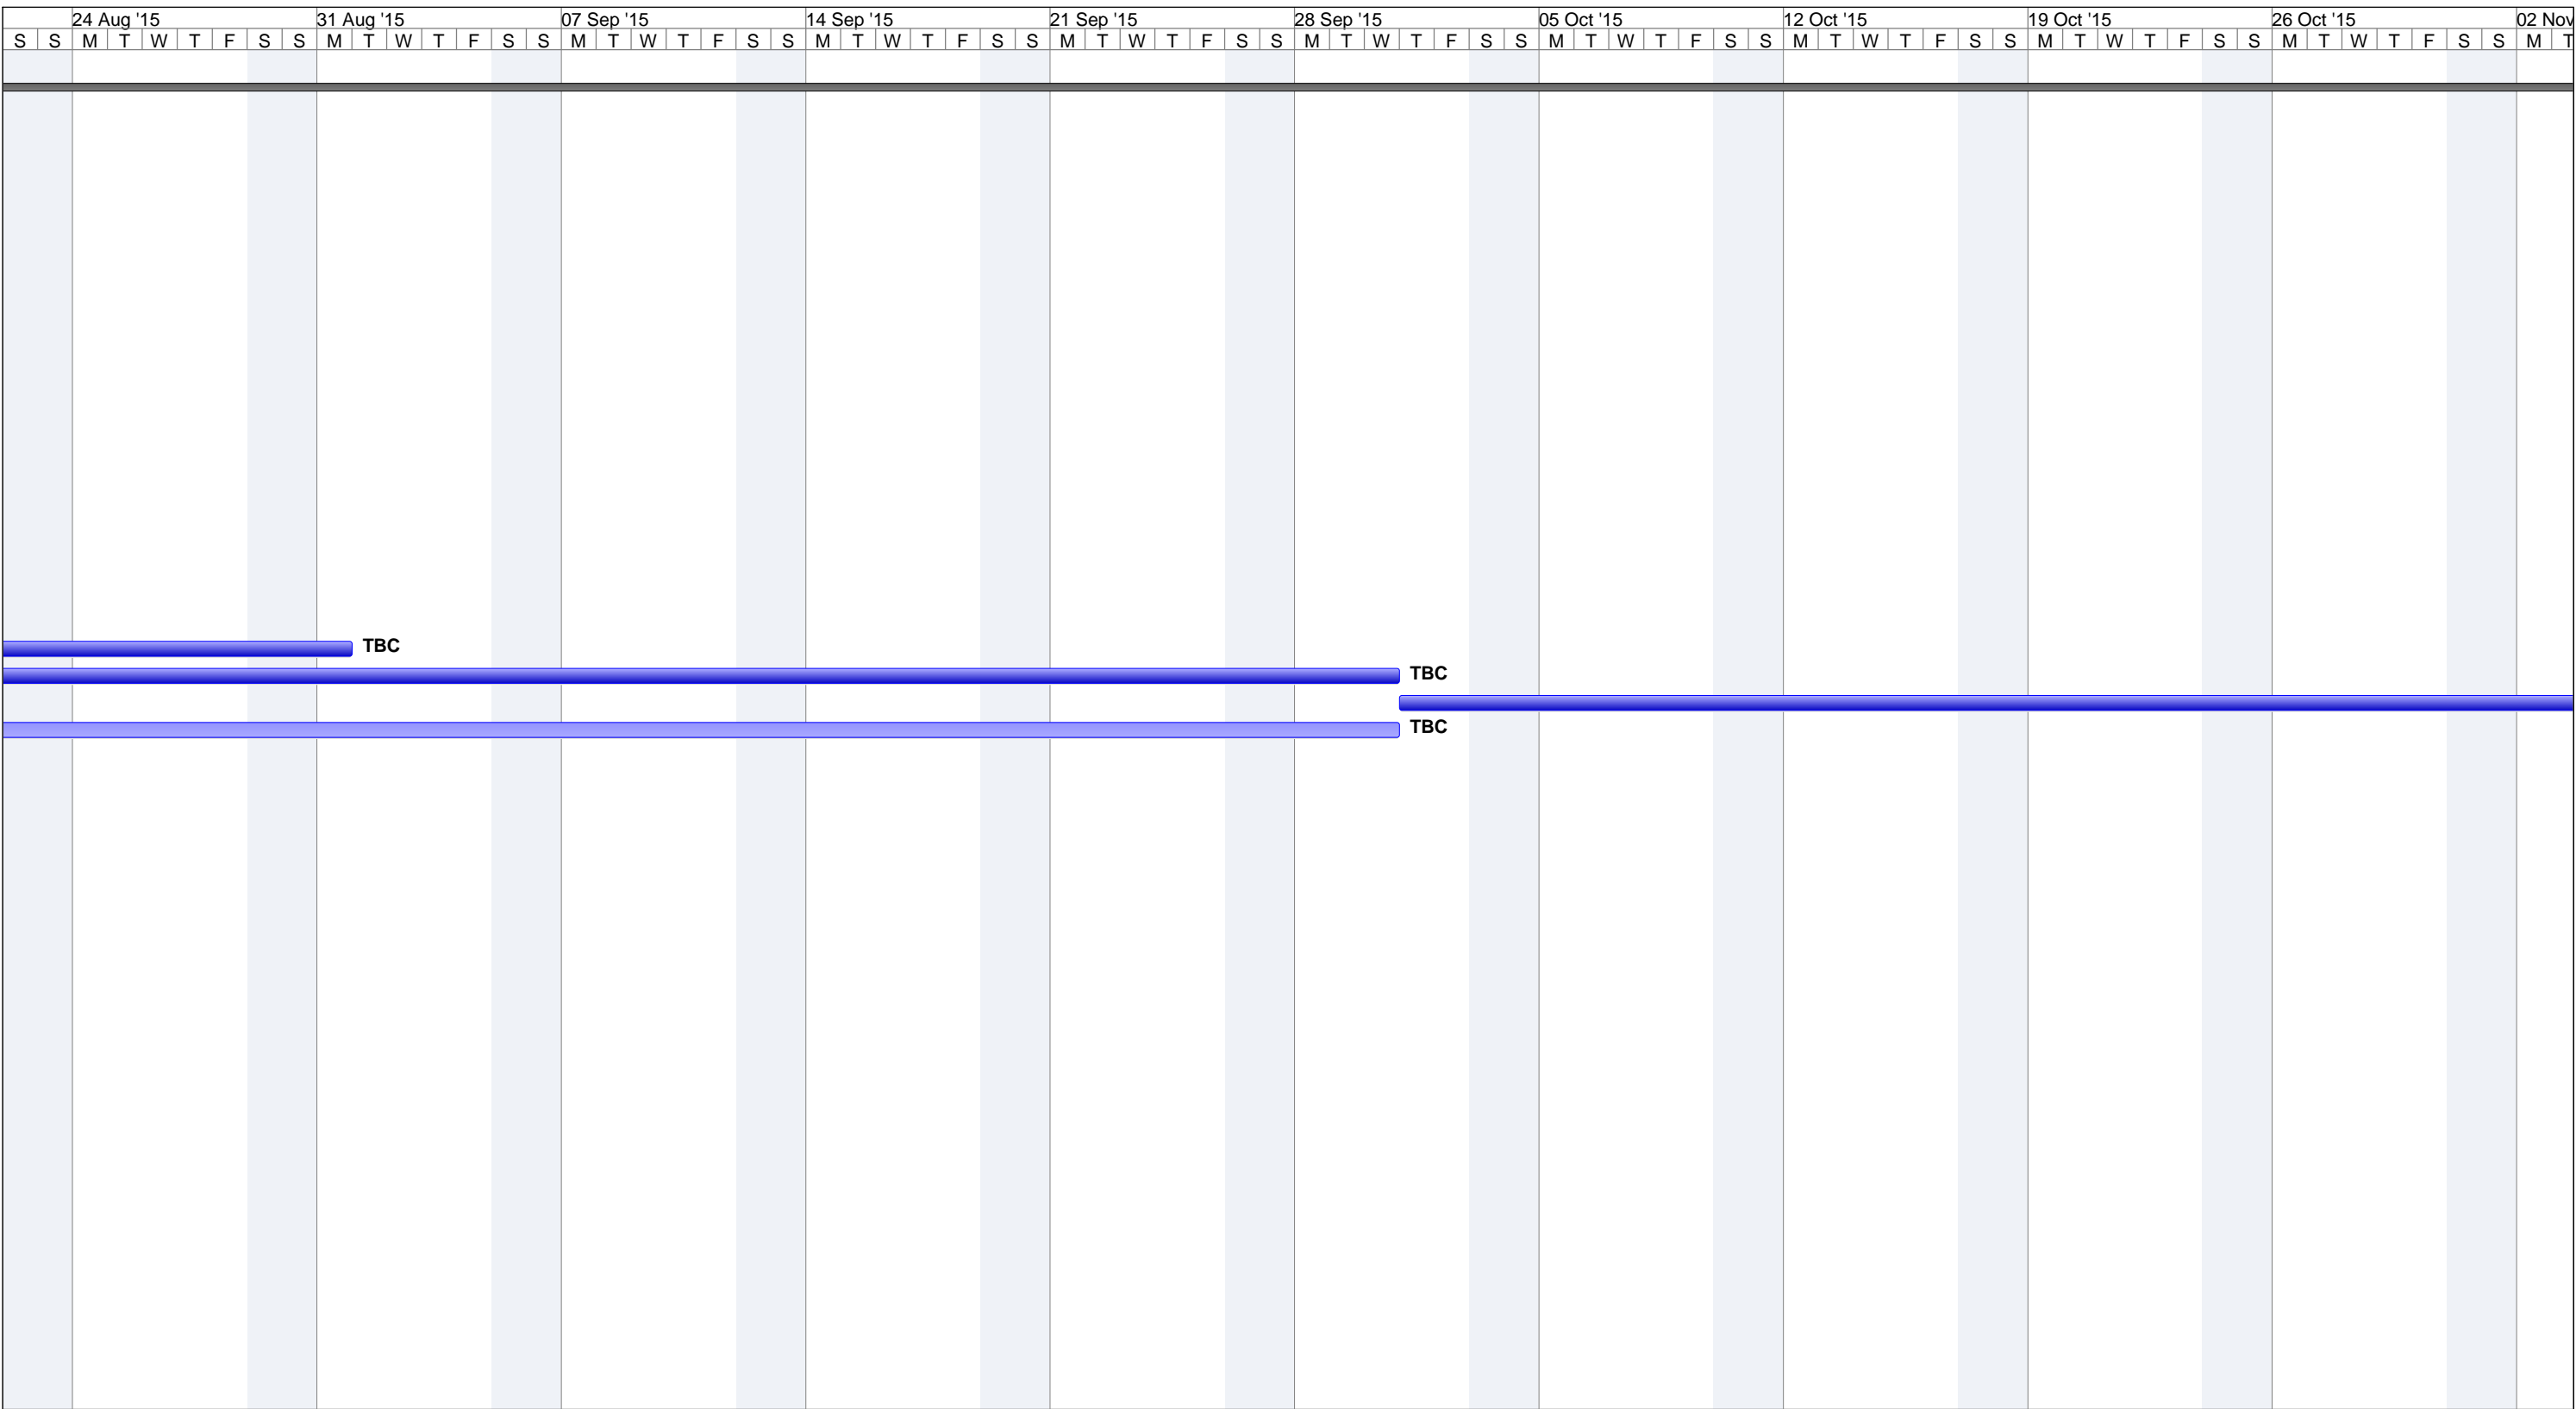

Project: Performance Assurance Plan
Date: Mon 02/02/15


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

09 Nov '15 16 Nov '15 23 Nov '15 30 Nov '15 07 Dec '15 14 Dec '15 21 Dec '15 28 Dec '15 04 Jan '16 11 Jan '16
 T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S



Project: Performance Assurance Plan Date: Mon 02/02/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

ov '15 09 Nov '15 16 Nov '15 23 Nov '15 30 Nov '15 07 Dec '15 14 Dec '15 21 Dec '15 28 Dec '15 04 Jan '16 11 Jan '16

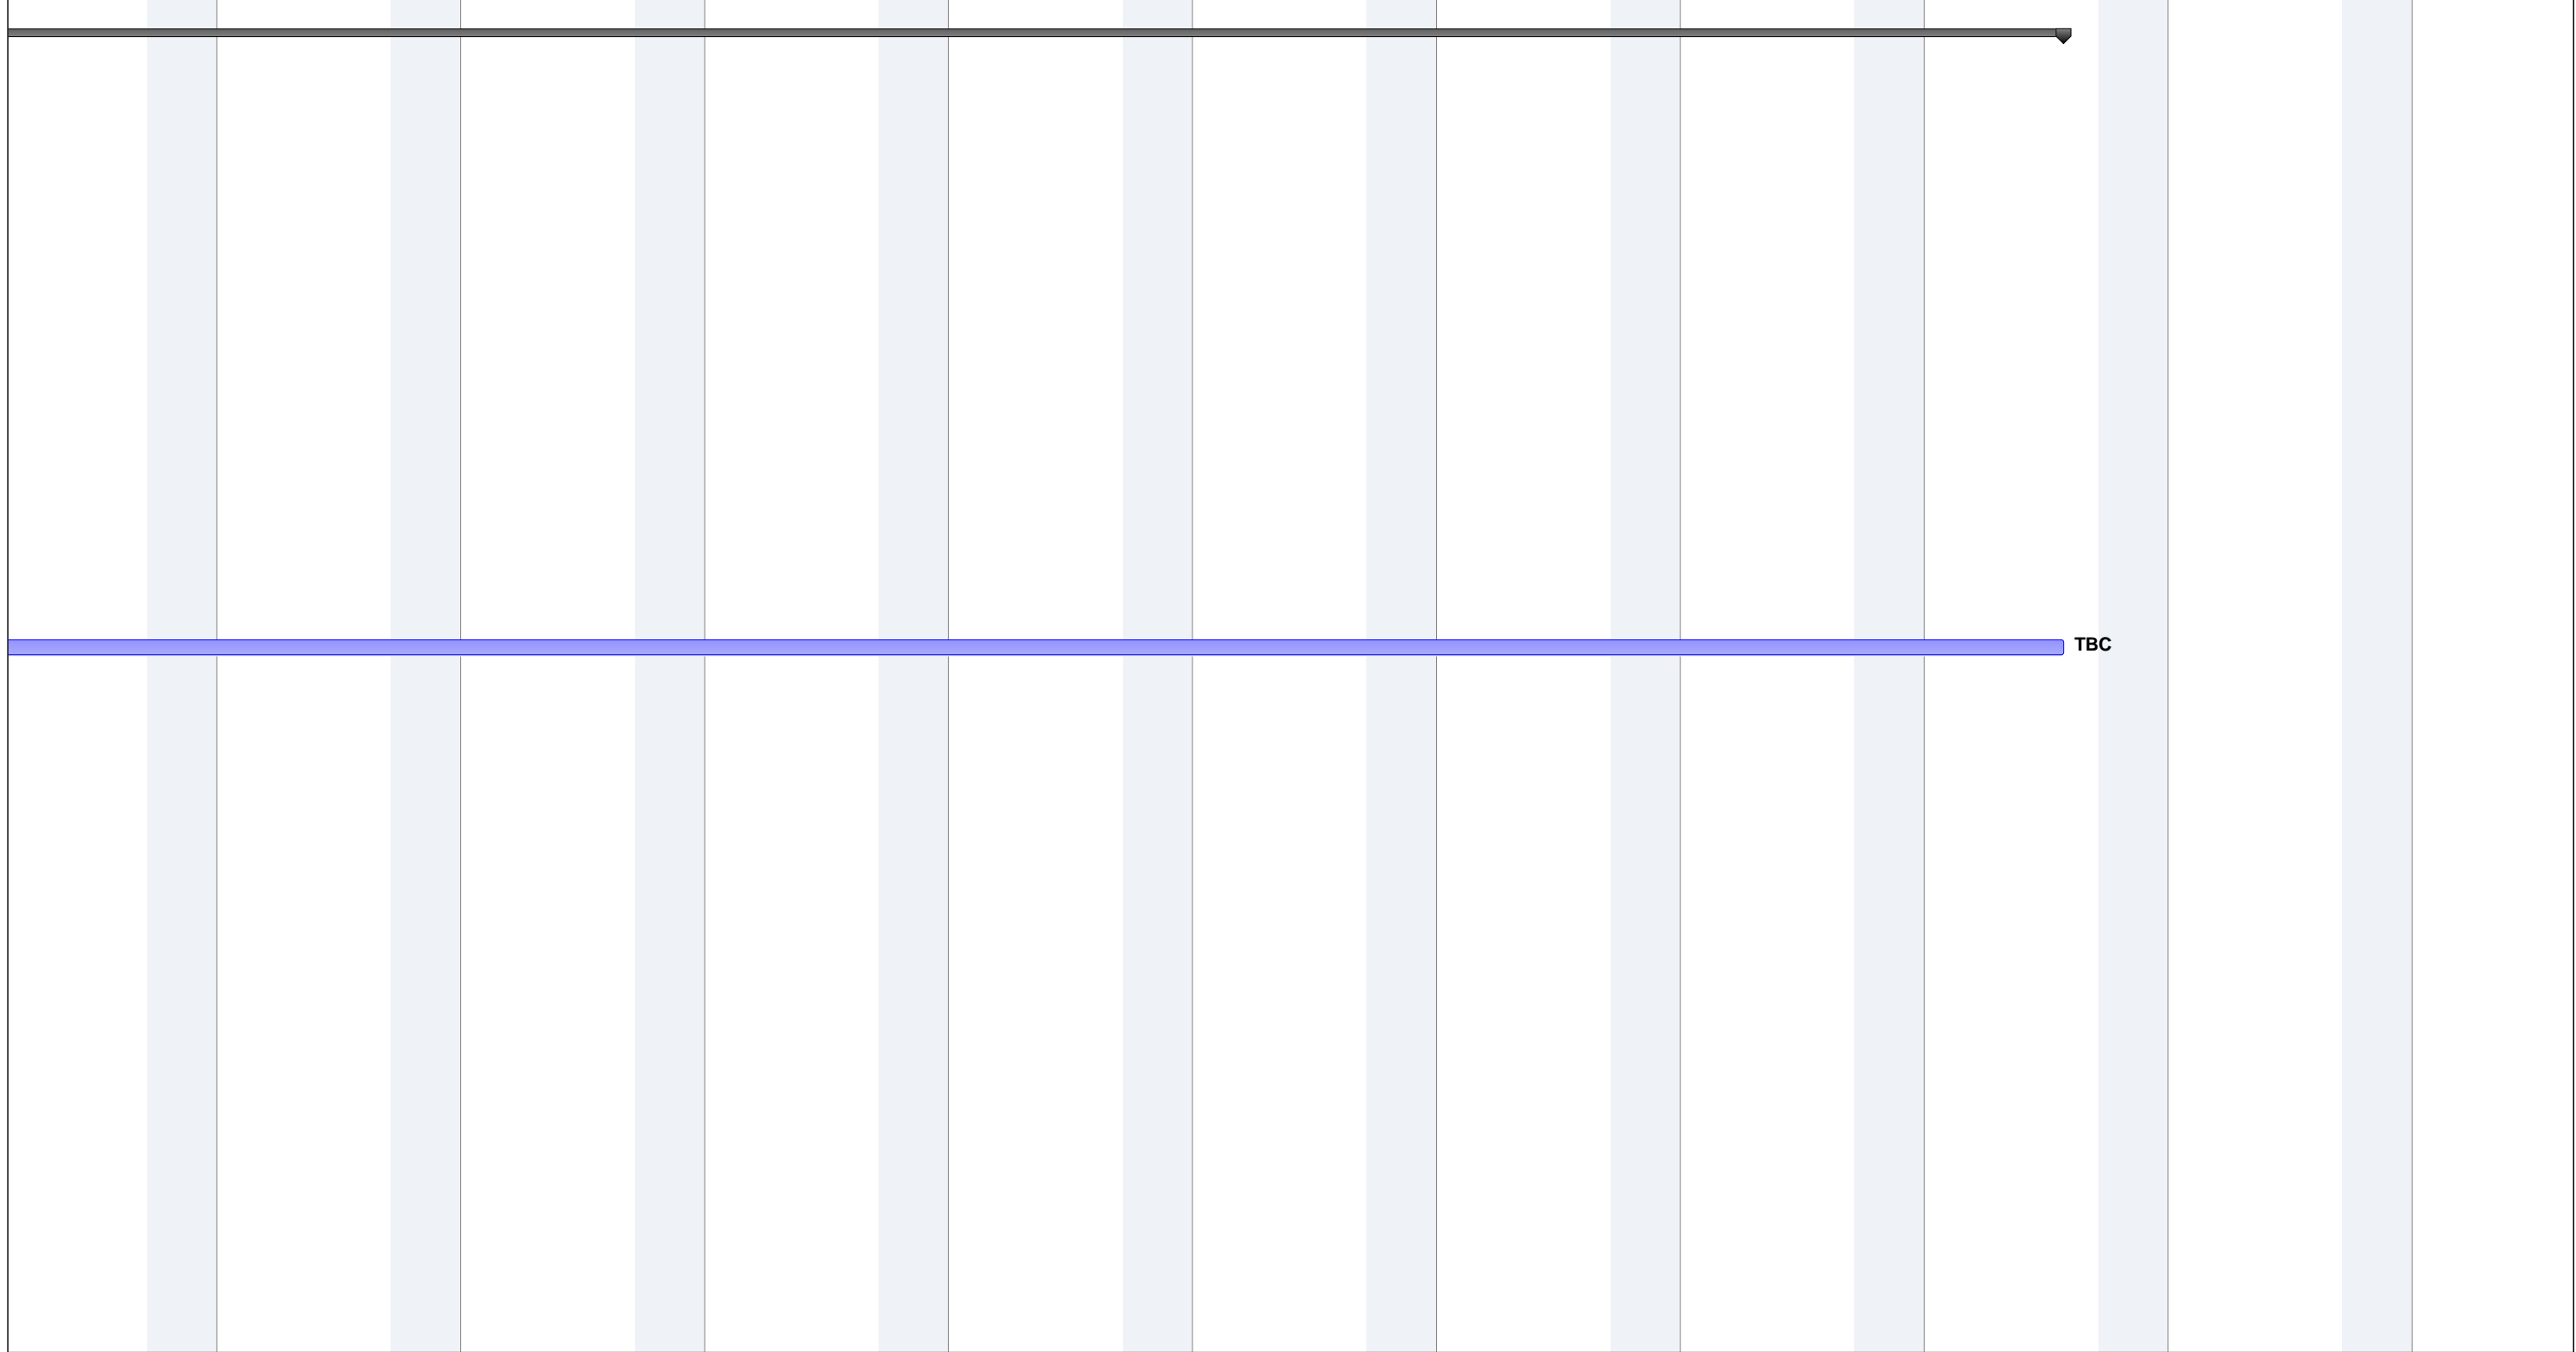

Project: Performance Assurance Plan
Date: Mon 02/02/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
