

ID	Task Name	Duration	Start	Baseline Finish	Finish	% Complete	Predecessors	18 Mar '13					25 Mar '13					01 Apr '13			
								M	T	W	T	F	S	S	M	T	W	T	F	S	S
1	<b>Overall Performance Assurance Plan</b>	727 days	Wed 20/03/13	Wed 31/12/14	Thu 31/12/15	25%															
2	<b>Independent Study of Performance Risk</b>	348 days	Wed 20/03/13	Wed 31/12/14	Fri 18/07/14	31%															
3	✓ Create scope for an independent study of the settlement process (incl consultation with Workgroup)	89 days	Wed 20/03/13	Mon 22/07/13	Mon 22/07/13	100%															
4	✓ Determine possible level of funding for the independent study	29 days	Wed 12/06/13	Mon 22/07/13	Mon 22/07/13	100%															
5	✓ Determine how the independent study will be funded	36 days	Mon 16/09/13	Mon 04/11/13	Mon 04/11/13	100%															
6	✓ Ofgem to write to EUK, ICOSS and ENA	56 days	Fri 04/10/13	Fri 04/10/13	Fri 20/12/13	100%															
7	✓ Responses from EUK, ICOSS and ENA	55 days	Mon 11/11/13	Mon 04/11/13	Fri 24/01/14	100%															
8	✓ Agree mechanism for paying for independent study	5 days	Mon 11/11/13	Mon 04/11/13	Fri 15/11/13	100%															
9	✓ Identify possible service providers for independent study	76 days	Mon 22/07/13	Mon 04/11/13	Mon 04/11/13	100%															
10	Calendar Tender for independent study	152 days	Fri 29/11/13	Fri 29/11/13	Mon 30/06/14	0%															
11	Calendar Undertake tender evaluation (including mtgs with tenderers)	150 days	Mon 02/12/13	Mon 09/12/13	Fri 27/06/14	0%															
12	Calendar Agree party for independent study	3 days	Wed 16/07/14	Mon 09/12/13	Fri 18/07/14	0%															
13	Calendar Contract with independent study party	135 days	Tue 24/12/13	Tue 24/12/13	Mon 30/06/14	0%															
14	Calendar Commence independent study	128 days	Thu 02/01/14	Wed 01/01/14	Mon 30/06/14	0%															
15	Calendar Conclude independent study (including risk register of "theoretical process")	1 day	Fri 13/06/14	Fri 18/04/14	Fri 13/06/14	0%															
16	Calendar PAF Group to consider independent study and any reporting required from Xoserve/SPAA	1 day	Fri 20/06/14	Thu 01/05/14	Fri 20/06/14	0%															
17	Calendar Xoserve/SPAA to provide reporting	117 days	Thu 16/01/14	Wed 31/12/14	Fri 27/06/14	0%															
18	Calendar PAF Group to consider reporting and agree materiality	1 day	Fri 27/06/14	Fri 31/01/14	Fri 27/06/14	0%															
19	Calendar PAF Group to consider ongoing data elements for PAF	96 days	Fri 14/02/14	Fri 14/02/14	Fri 27/06/14	0%															
20	Calendar 1st cut of data elements for PAF and performance monitoring to be reviewed by the PAF Group	1 day	Mon 30/06/14	Mon 30/06/14	Mon 30/06/14	0%															
21	<b>Performance Assurance Framework Development</b>	243 days	Wed 25/09/13	Wed 01/10/14	Fri 29/08/14	51%															
22	<b>Reporting</b>	198 days	Wed 25/09/13	Mon 31/03/14	Fri 27/06/14	70%															
23	✓ Consider reporting that Xoserve currently does	1 day	Wed 25/09/13	Wed 25/09/13	Wed 25/09/13	100%															
24	✓ Determine appropriateness of existing reporting	1 day	Wed 25/09/13	Wed 25/09/13	Wed 25/09/13	100%															
25	✓ Consider any additional reporting/controls necessary for post Nexus functionality/market model	105 days	Wed 25/09/13	Fri 29/11/13	Tue 18/02/14	100%															
26	✓ Agree future reporting required, in line with Project Nexus Workgroup	148 days	Wed 25/09/13	Fri 29/11/13	Fri 18/04/14	100%															
27	Calendar Determine individual elements and timings of reporting	139 days	Tue 17/12/13	Tue 31/12/13	Fri 27/06/14	0%															
28	✓ Determine individual elements and timings of performance monitoring	75 days	Tue 17/12/13	Mon 31/03/14	Mon 31/03/14	100%															
29	<b>Overall Governance Arrangements</b>	168 days	Mon 11/11/13	Fri 13/06/14	Wed 02/07/14	35%															
30	✓ Agree main parties to the PAF - e.g. Transporters, Shippers, Xoserve	1 day	Mon 11/11/13	Fri 31/01/14	Mon 11/11/13	100%															
31	Calendar Agree what current governance arrangements will be impacted by the PAF and if anything new will be required	140 days	Tue 17/12/13	Thu 15/05/14	Mon 30/06/14	0%															
32	Calendar Commence discussions with other governance bodies (if required)	140 days	Tue 17/12/13	Fri 28/02/14	Mon 30/06/14	0%															
33	✓ Agree the funding parties for PAF	75 days	Tue 17/12/13	Mon 31/03/14	Mon 31/03/14	100%															
34	✓ Agree if an annual budget is required	119 days	Tue 17/12/13	Mon 31/03/14	Fri 30/05/14	100%															
35	Calendar Determine how funding, budget and apportionments are agreed	44 days	Wed 30/04/14	Wed 30/04/14	Mon 30/06/14	0%															
36	Calendar Discuss and agree split of duties/responsibilities between SPAA and the UNC	1 day	Fri 27/06/14	Wed 30/04/14	Fri 27/06/14	0%															
37	Calendar Agree how the PAFA features in the PAF and interfaces with the UNC and SPAA	44 days	Wed 30/04/14	Wed 30/04/14	Mon 30/06/14	0%															
38	✓ Consider Ofgem's involvement/oversight	1 day	Fri 30/05/14	Wed 30/04/14	Fri 30/05/14	100%															
39	Calendar Agree, in principle, the basis for the settlement risk premium	1 day	Mon 23/06/14	Wed 30/04/14	Mon 23/06/14	0%	16														
40	Calendar Agree frequency (at least initial frequency) of the analysis of settlement risk and how often methodology needs to be updated (if at all)	1 day	Mon 23/06/14	Wed 30/04/14	Mon 23/06/14	0%	16														
41	✓ Agree governance around reporting - how to request new reports	1 day	Fri 30/05/14	Wed 14/05/14	Fri 30/05/14	100%	26														
42	Calendar Decide if there is any consultation needed with Parties/Ofgem following the determination of a settlement risk penalty	1 day	Tue 01/07/14	Wed 14/05/14	Tue 01/07/14	0%	37														
43	Calendar Determine individual elements and timings of incentive regime and invoicing (if deemed required under action 1)	1 day	Wed 02/07/14	Fri 13/06/14	Wed 02/07/14	0%	42														
44	Calendar Determine individual elements and timings of assurance (if deemed required under action 1)	1 day	Fri 13/06/14	Fri 13/06/14	Fri 13/06/14	0%	28														
45	✓ <b>Day to Day Governance Arrangements</b>	108 days	Mon 02/12/13	Wed 30/04/14	Wed 30/04/14	100%															
49	<b>Introducing the PAF</b>	210 days	Mon 11/11/13	Wed 01/10/14	Fri 29/08/14	0%															
50	Calendar Develop business rules for PAF MOD	210 days	Mon 11/11/13	Fri 29/08/14	Fri 29/08/14	0%															
51	✓ Mod raised by BGT on independent study	1 day	Fri 07/02/14	Fri 07/02/14	Fri 07/02/14	100%															
52	Calendar Consider two Mods for PAF and Policing / Administration	45 days	Wed 09/04/14	Wed 09/04/14	Tue 10/06/14	0%															
53	Calendar Raise two Mods for PAF and Policing / Administration	43 days	Wed 30/04/14	Wed 30/04/14	Fri 27/06/14	0%															
54	Calendar Mod panel meeting to discuss two Mods	24 days	Thu 15/05/14	Thu 15/05/14	Tue 17/06/14	0%															
55	<b>Performance Assurance Framework Administrator (PAFA)</b>	563 days	Tue 05/11/13	Wed 31/12/14	Thu 31/12/15	1%															
56	✓ Consider Elexon Tools	29 days	Tue 21/01/14	Fri 28/02/14	Fri 28/02/14	100%															


Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Baseline Finish	Finish	% Complete	Predecessors	18 Mar '13							25 Mar '13							01 Apr '13			
								M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T		
57	Determine scope for the work on the PAF Administrator, based on model of assurance and performance requirements	163 days	Tue 17/12/13	Thu 31/07/14	Thu 31/07/14	0%																			
58	Determine the scope of the PAFA performance reporting and analysis role	163 days	Tue 17/12/13	Thu 31/07/14	Thu 31/07/14	0%																			
59	Consider if the PAFA will have an assurance role, as well as performance monitoring	163 days	Tue 17/12/13	Thu 31/07/14	Thu 31/07/14	0%																			
60	Agree if the PAFA will provide "training services" for new entrants	163 days	Tue 17/12/13	Thu 31/07/14	Thu 31/07/14	0%																			
61	Agree if the PAFA will provide "education" to parties performing poorly	163 days	Tue 17/12/13	Thu 31/07/14	Thu 31/07/14	0%																			
62	Consider options for the contracting of the PAF administrator	138 days	Tue 21/01/14	Fri 29/08/14	Thu 31/07/14	0%																			
63	Should the PAFA have a statutory role?	193 days	Tue 05/11/13	Fri 29/08/14	Thu 31/07/14	0%																			
64	Who should contract the PAFA (a) initially and (b) ongoing?	138 days	Tue 21/01/14	Fri 29/08/14	Thu 31/07/14	0%																			
65	Determine route to agree appointment, tender and award of PAFA	138 days	Tue 21/01/14	Fri 29/08/14	Thu 31/07/14	0%																			
66	Identify possible service providers for PAFA	21 days	Fri 01/08/14	Fri 29/08/14	Fri 29/08/14	0%																			
67	Prepare tender for PAFA appointment	21 days	Mon 01/09/14	Mon 29/09/14	Mon 29/09/14	0%																			
68	Issue tender for the provision of PAFA	1 day	Tue 30/09/14	Tue 30/09/14	Tue 30/09/14	0%																			
69	Undertake tender evaluation (including mtgs with tenderers)	23 days	Wed 01/10/14	Fri 31/10/14	Fri 31/10/14	0%																			
70	Agree successful party who will do the PAFA work	1 day	Fri 14/11/14	Fri 14/11/14	Fri 14/11/14	0%																			
71	Contract party for PAFA work	11 days	Fri 14/11/14	Fri 28/11/14	Fri 28/11/14	0%	15																		
72	PAFA commences work - preparation (including meeting industry parties)	23 days	Mon 01/12/14	Wed 31/12/14	Wed 31/12/14	0%																			
73	PAFA takes model from the independent study and supporting documentation and becomes familiar with it	23 days	Mon 01/12/14	Wed 31/12/14	Wed 31/12/14	0%																			
74	PAFA establishes links with Xoserve (and possibly SPAA) to gain data necessary to run risk model	23 days	Mon 01/12/14	Wed 31/12/14	Wed 31/12/14	0%																			
75	PAFA creates reporting on the agreed parameters deemed most material for settlement accuracy	45 days	Mon 01/12/14	Wed 31/12/14	Fri 30/01/15	0%																			
76	PAFA issues reports to industry and Ofgem on a monthly basis to update on progress	218 days	Mon 01/12/14	Wed 31/12/14	Wed 30/09/15	0%																			
77	PAFA liaises with Xoserve on monthly charges and re-distribution to be applied	66 days	Thu 01/10/15	Wed 31/12/14	Thu 31/12/15	0%																			
78	PAFA issues first performance reports against Risk Register	218 days	Mon 01/12/14	Wed 31/12/14	Wed 30/09/15	0%																			

Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

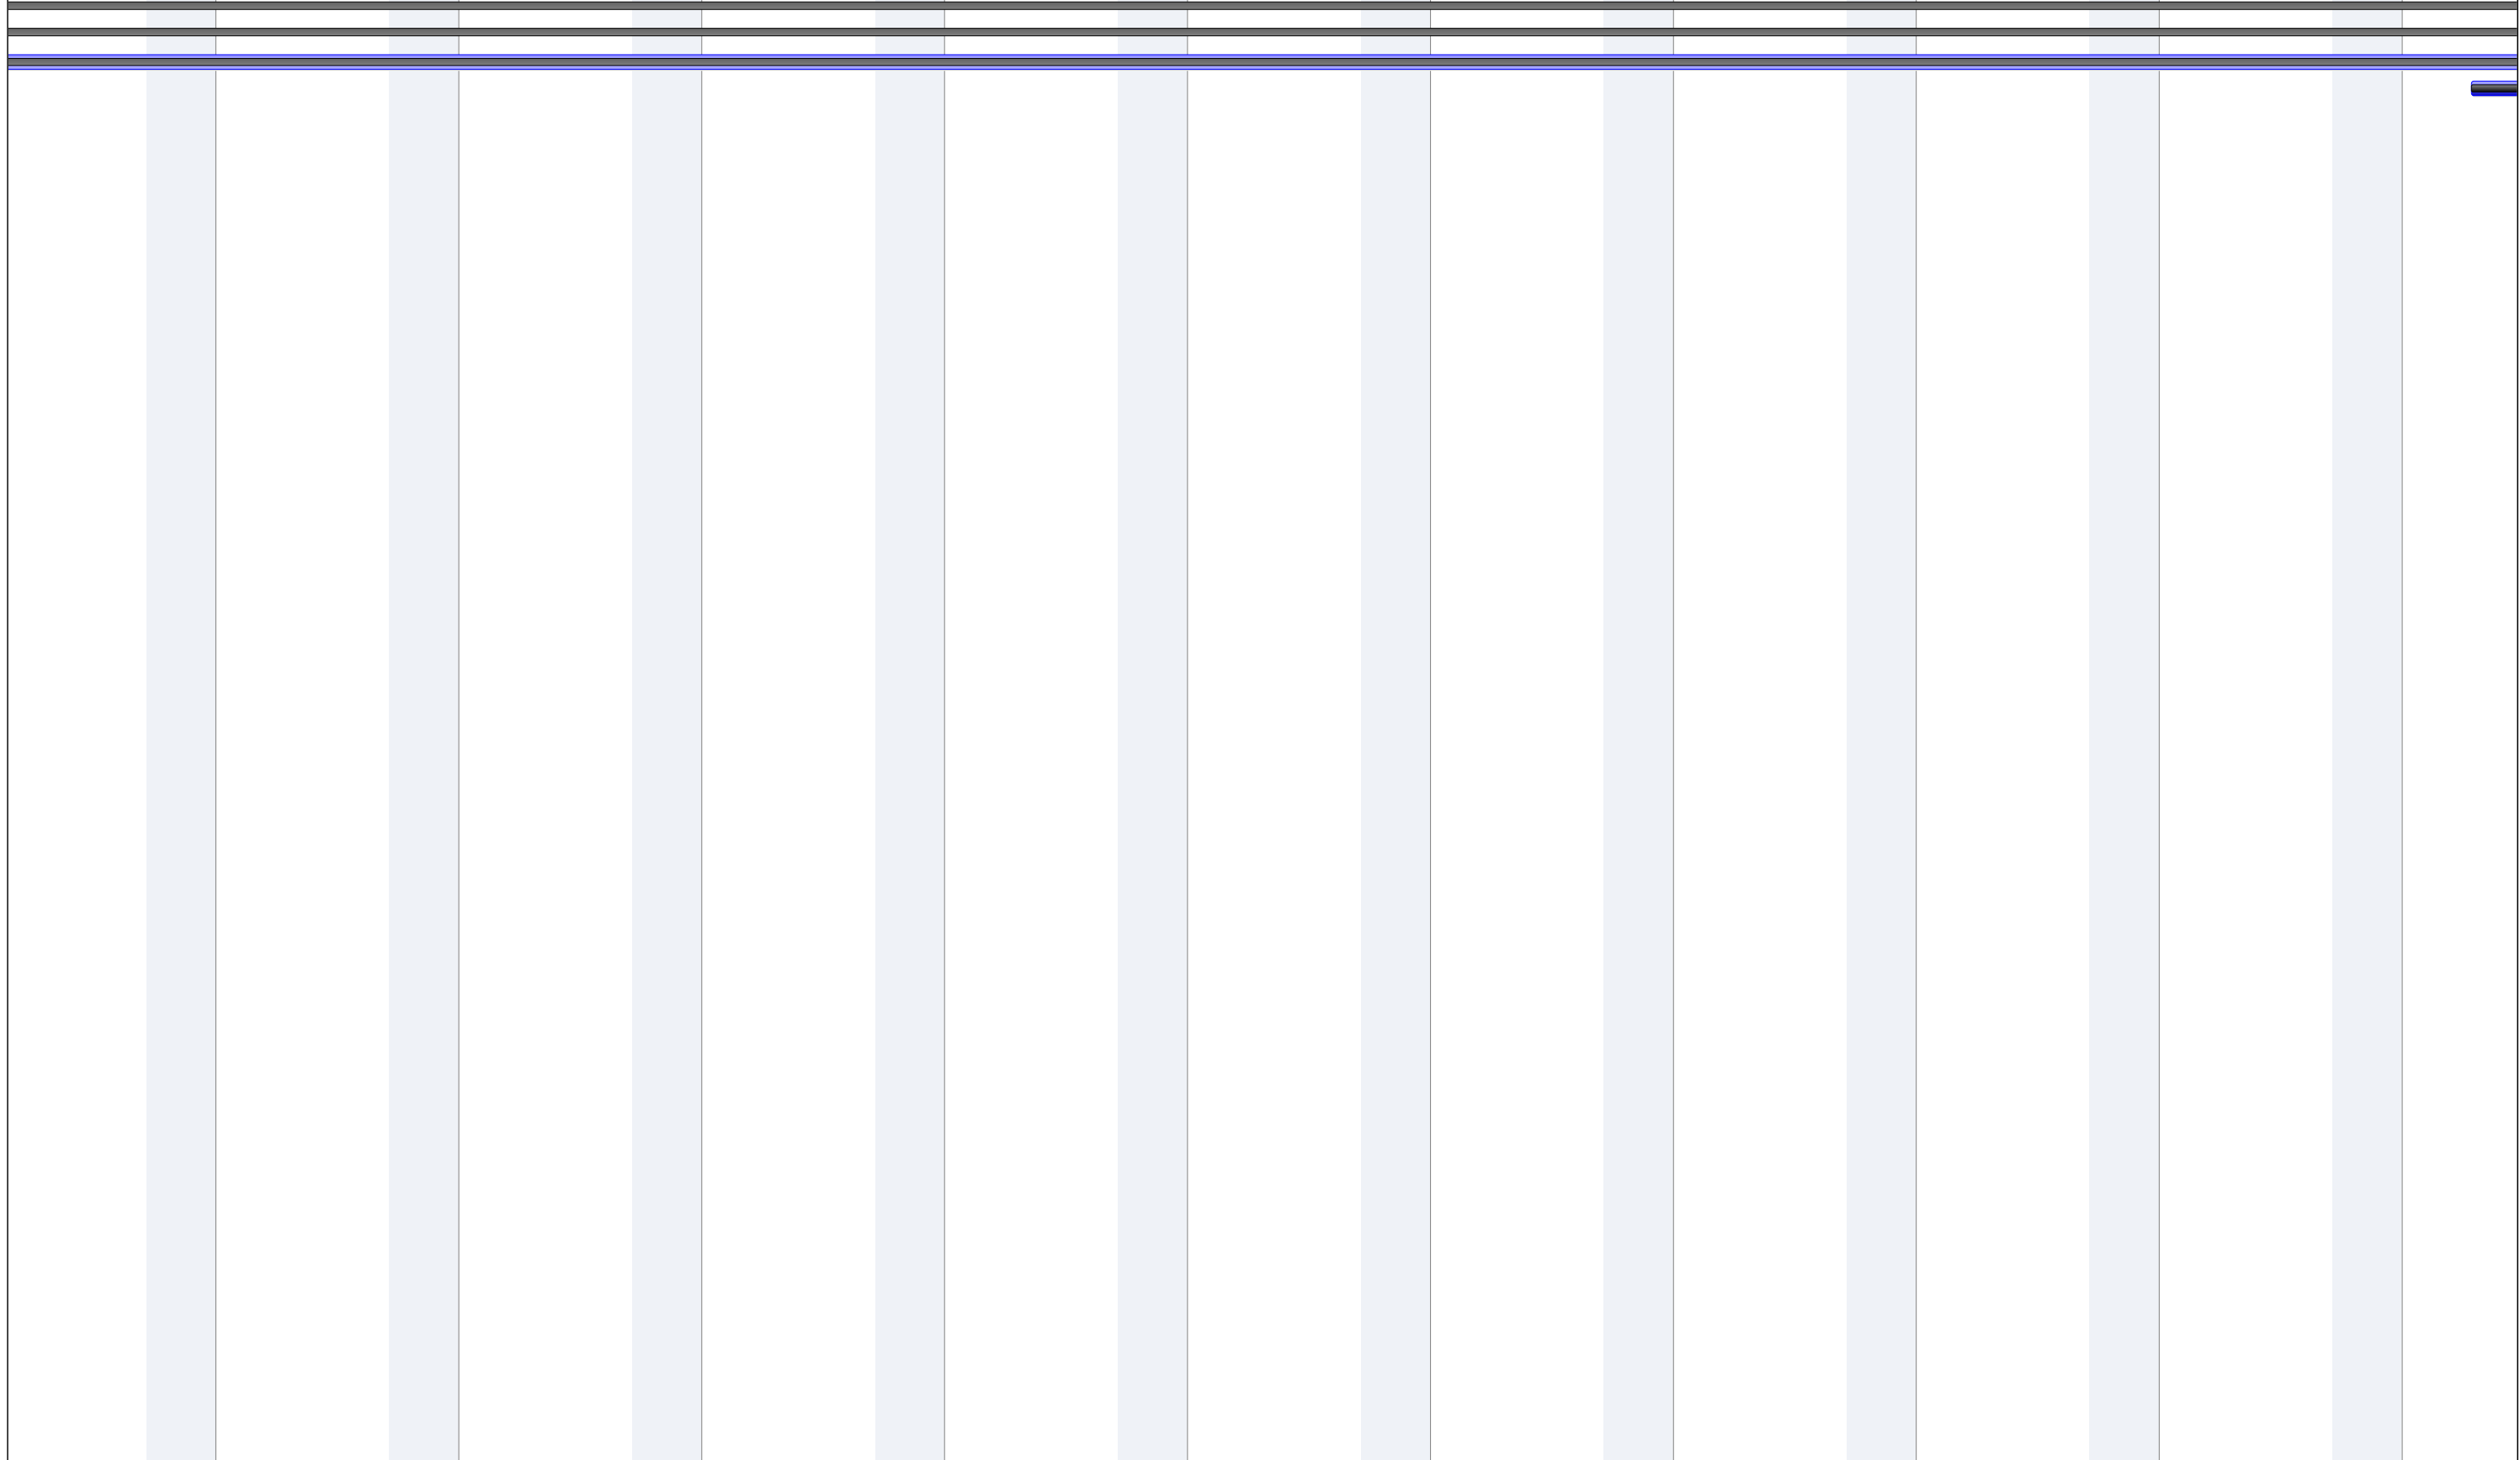


Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

pr '13		08 Apr '13					15 Apr '13					22 Apr '13					29 Apr '13					06 May '13					13 May '13					20 May '13					27 May '13					03 Jun '13					10 Jun '13										
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W




Project: Performance Assurance Plan Date: Mon 09/06/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

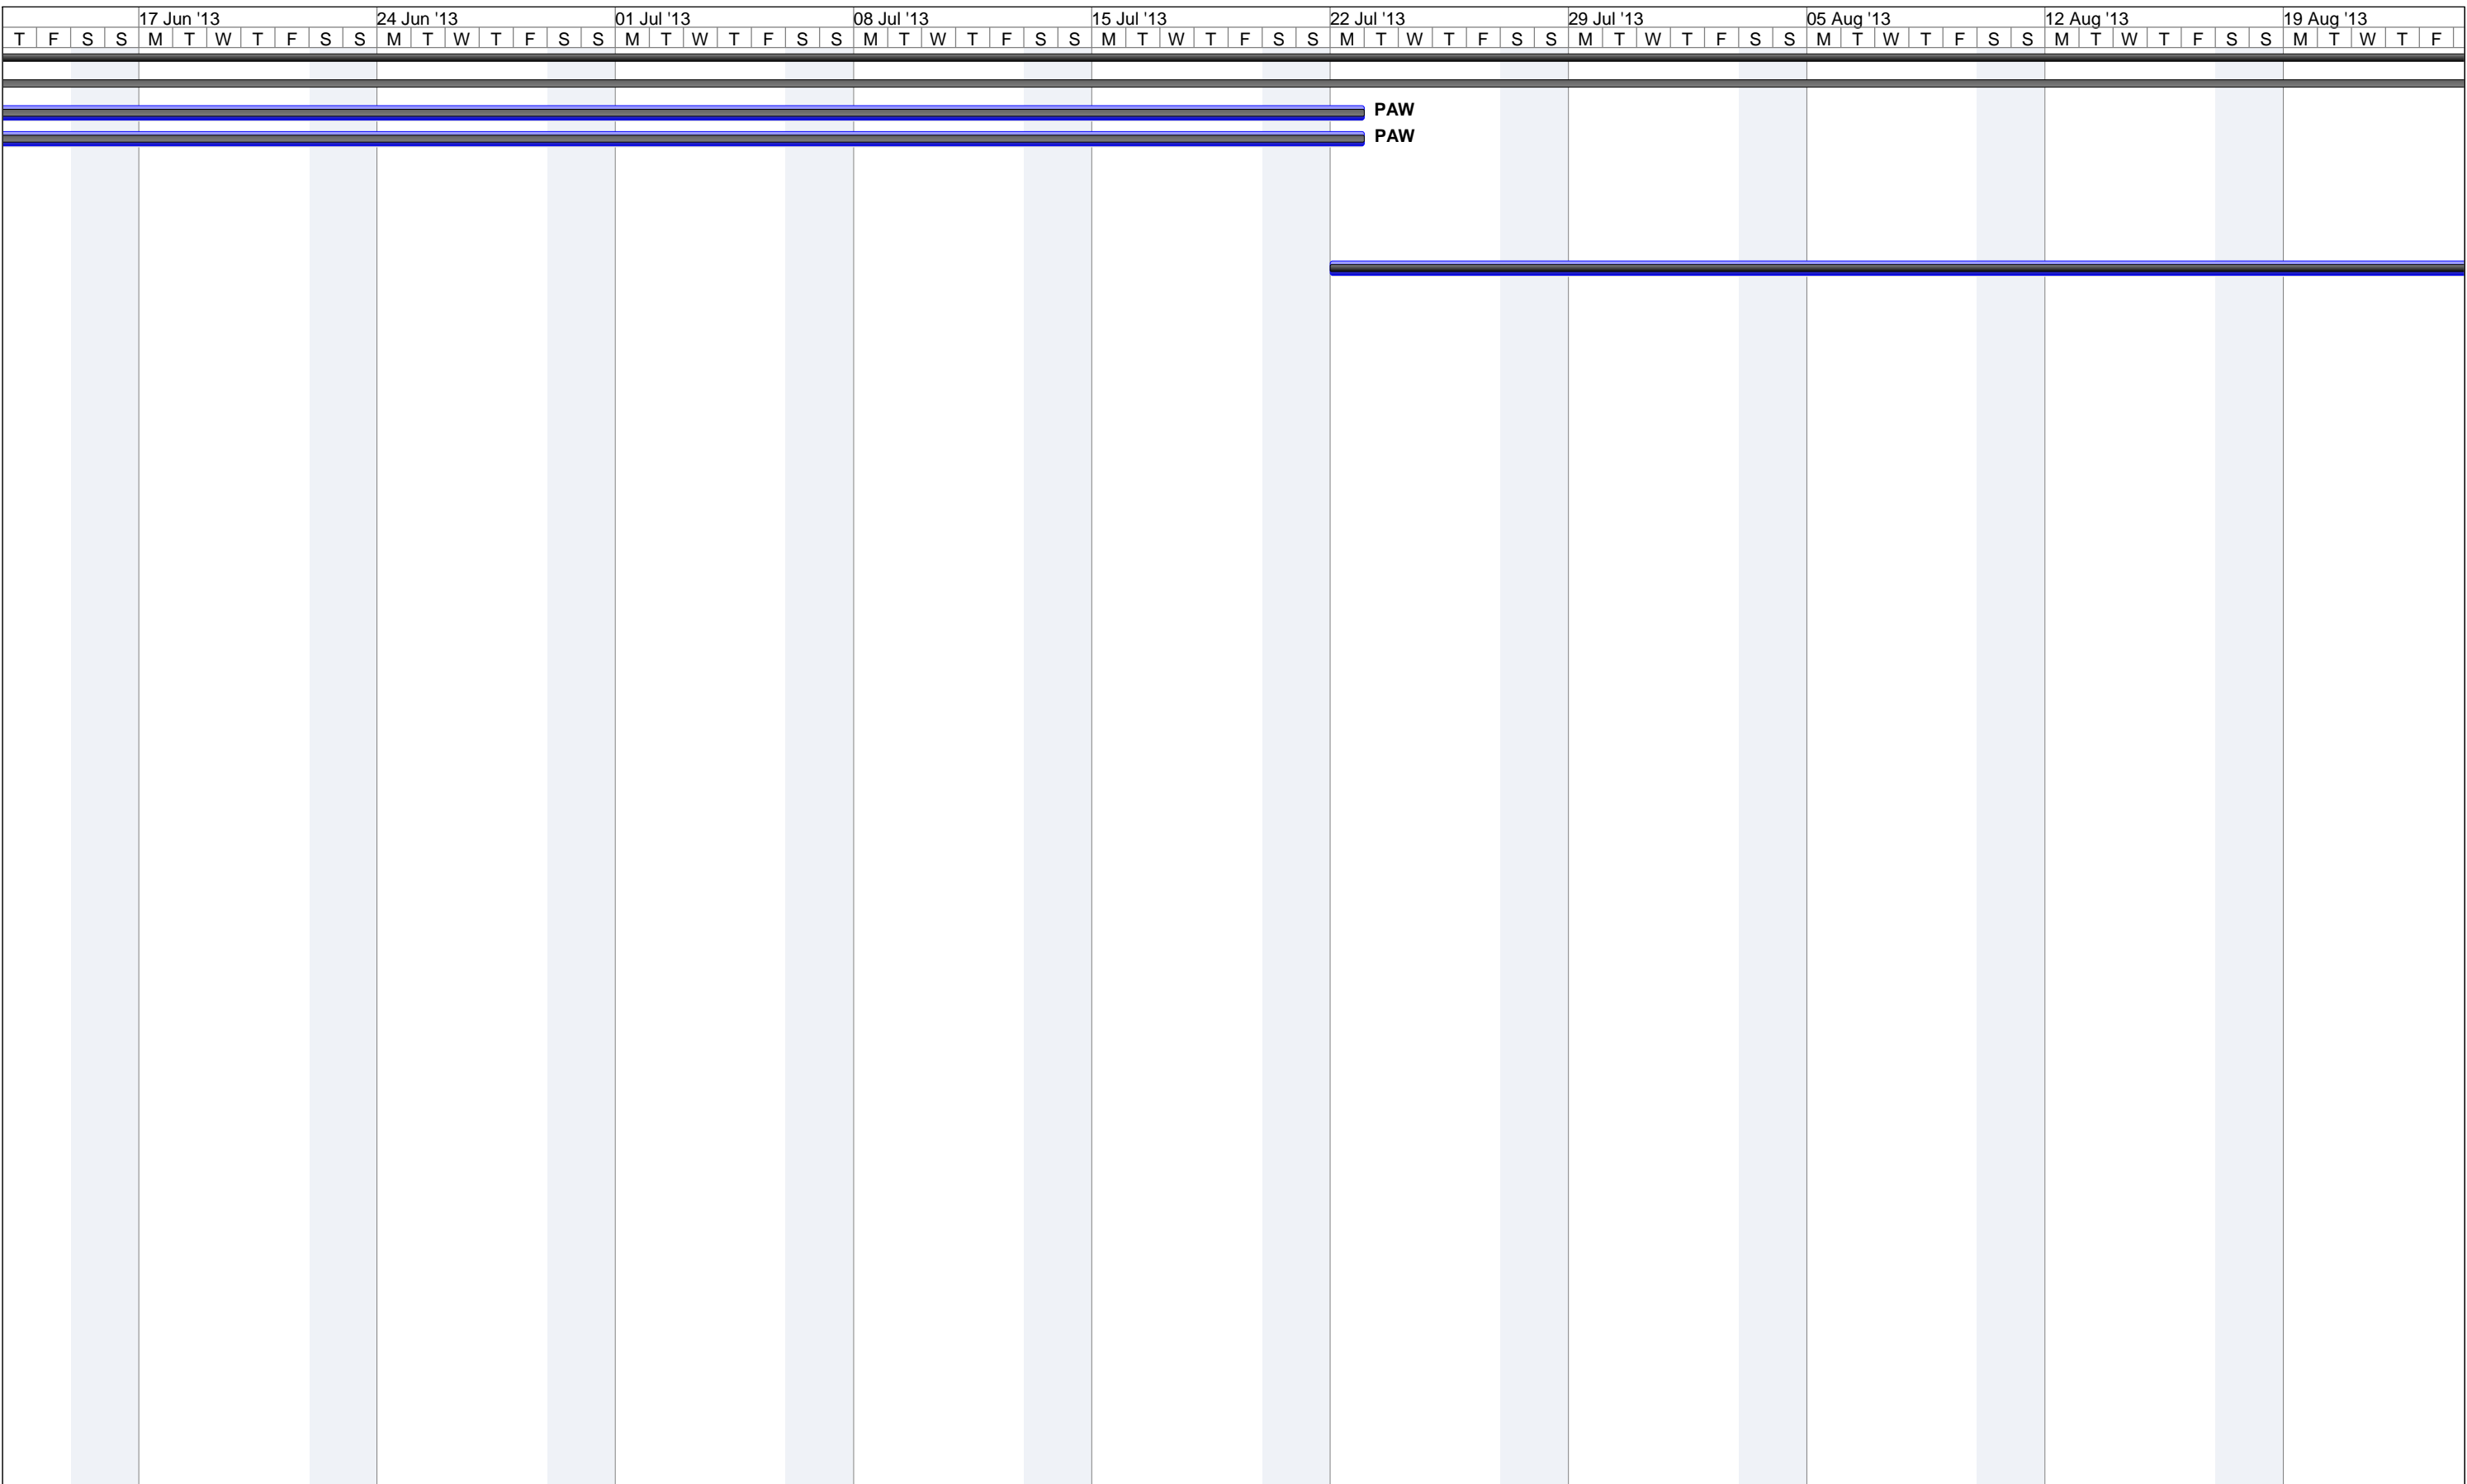

Project: Performance Assurance Plan  
 Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

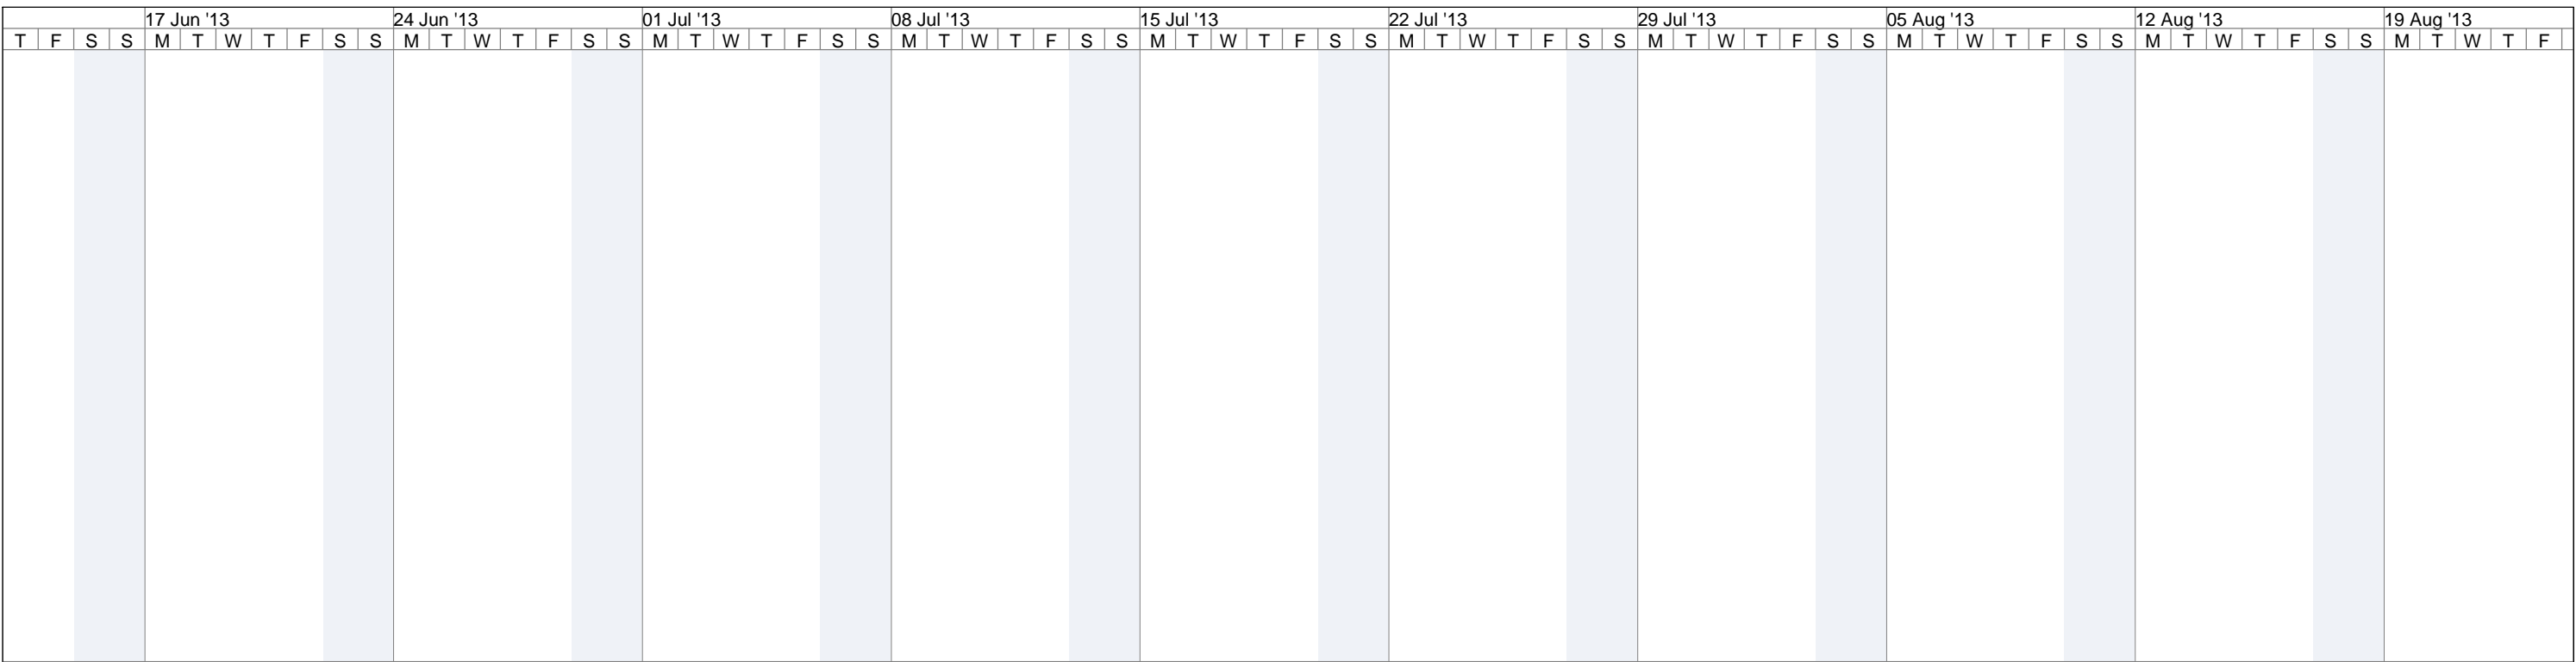


Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

26 Aug '13 02 Sep '13 09 Sep '13 16 Sep '13 23 Sep '13 30 Sep '13 07 Oct '13 14 Oct '13 21 Oct '13 28 Oct '13 0

S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S

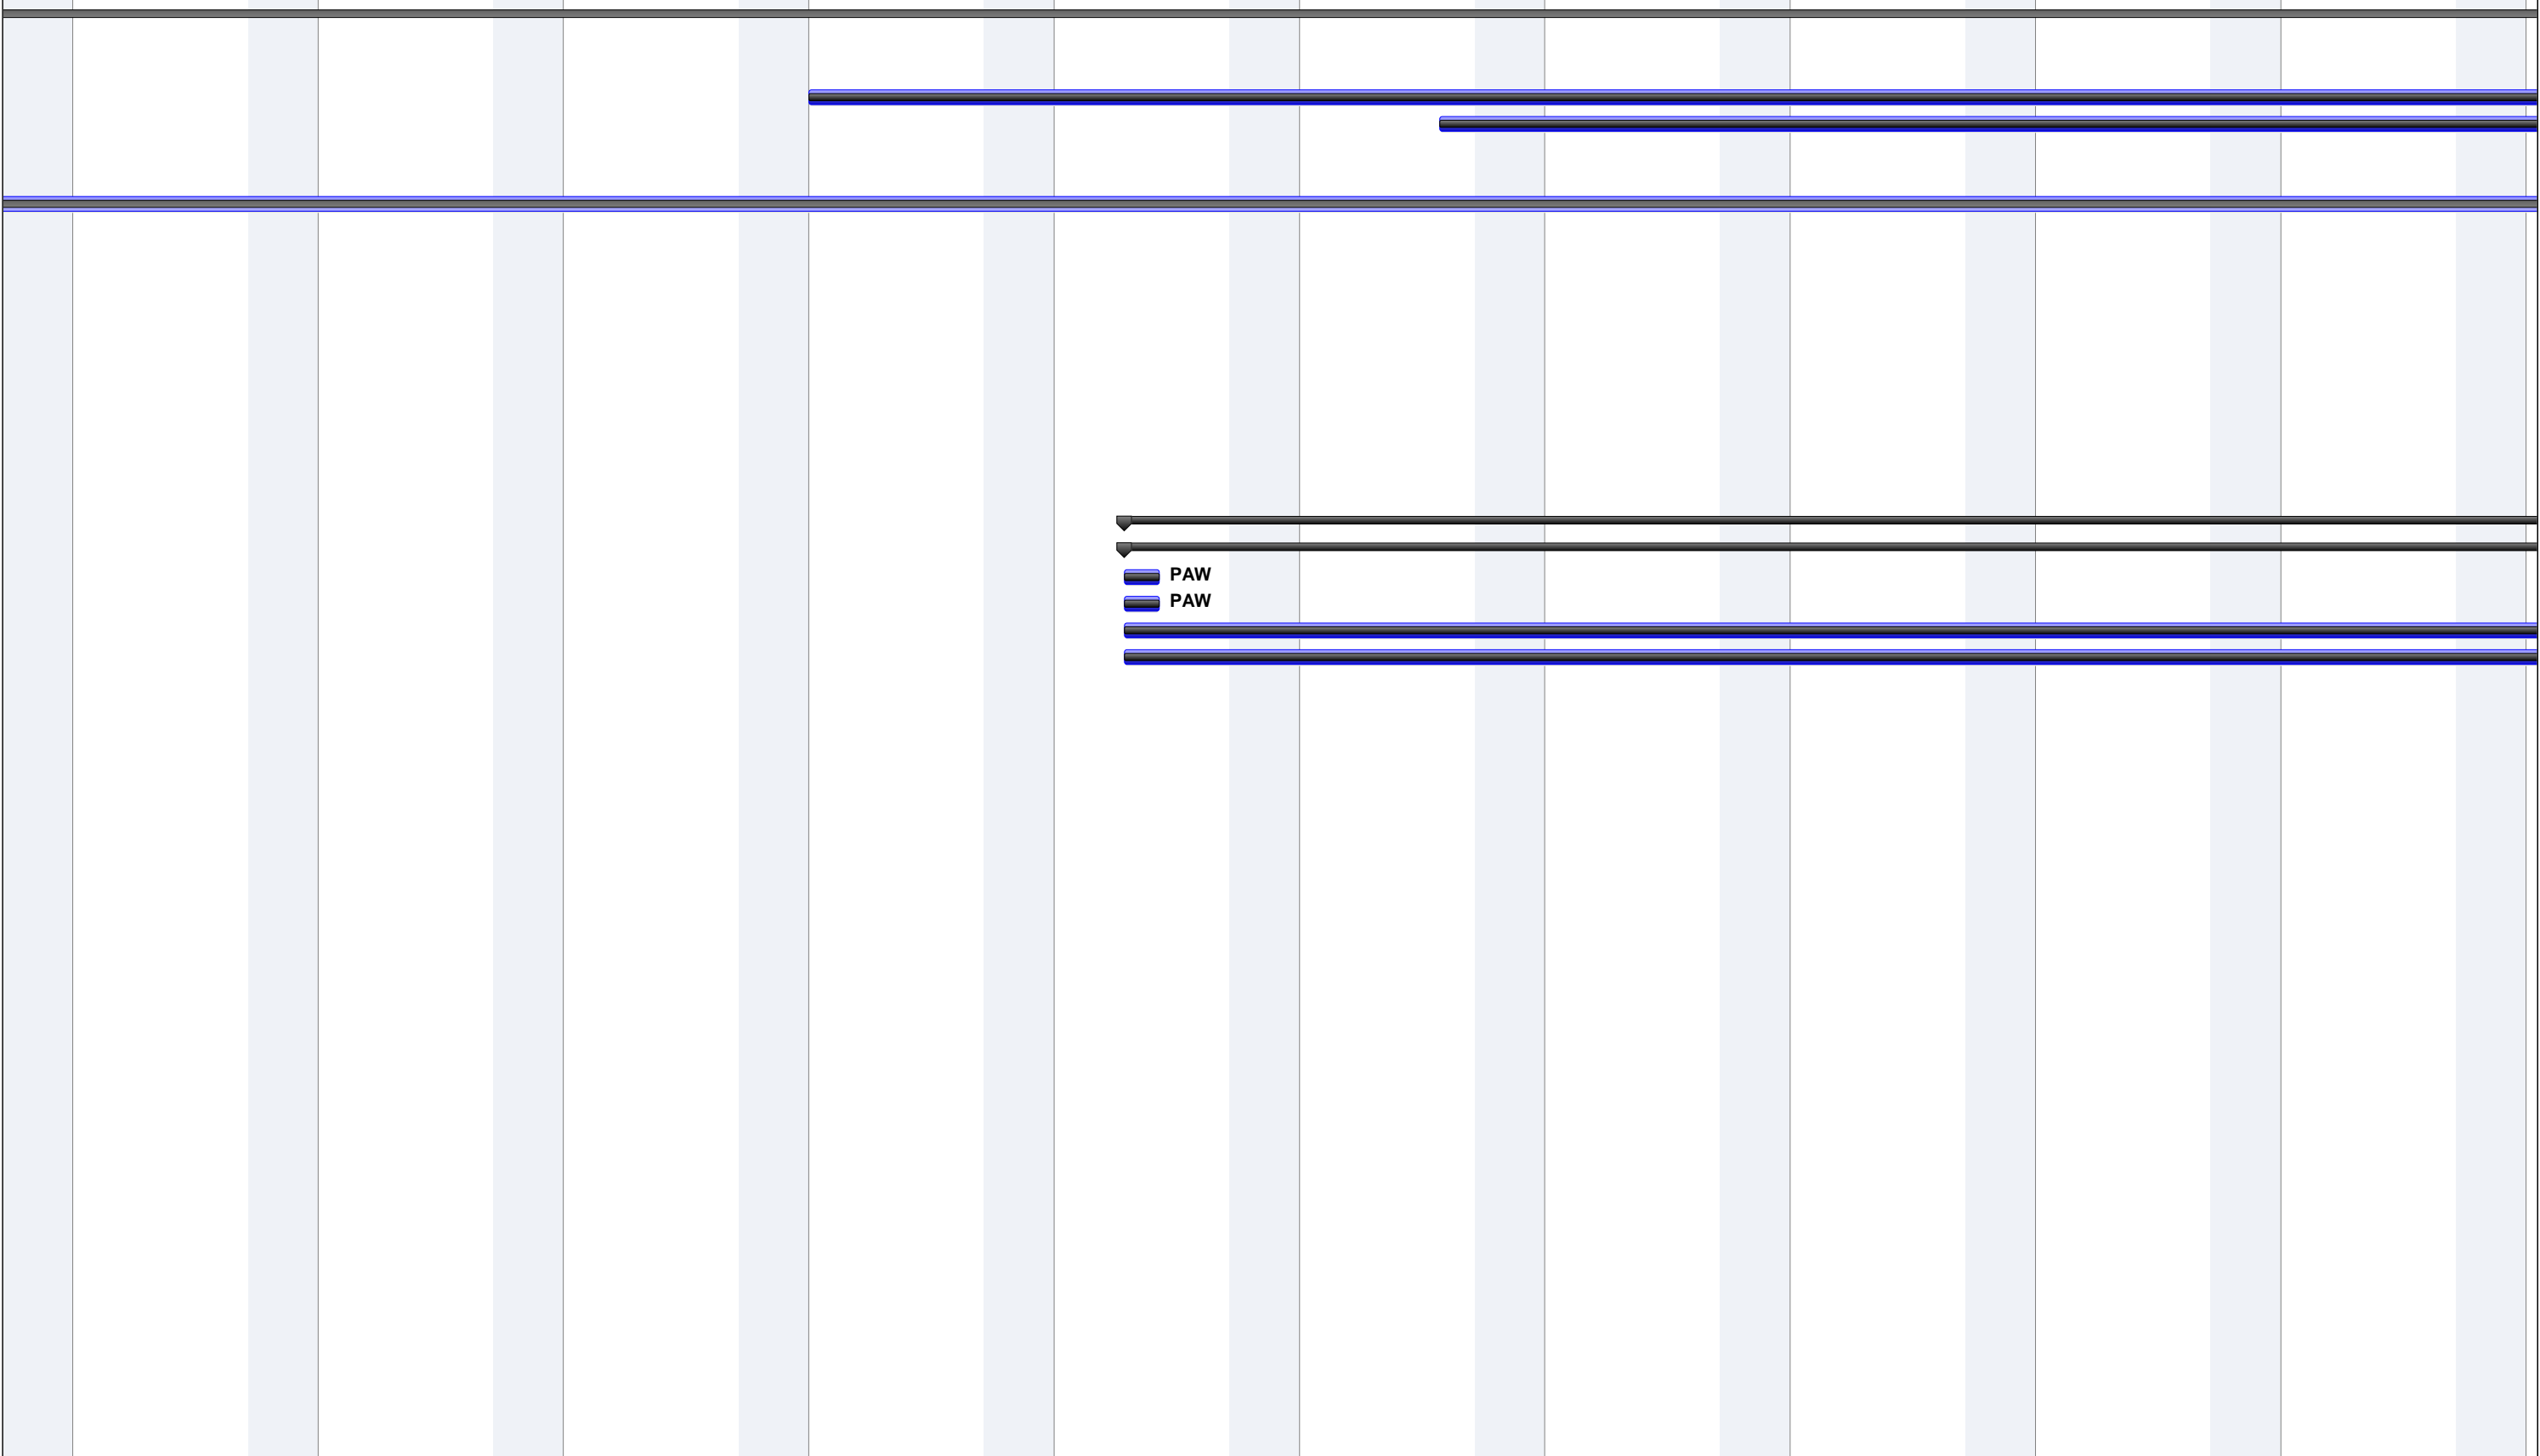

PAW
   
 PAW

Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			


26 Aug '13		02 Sep '13		09 Sep '13		16 Sep '13		23 Sep '13		30 Sep '13		07 Oct '13		14 Oct '13		21 Oct '13		28 Oct '13		0																							
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S



Project: Performance Assurance Plan Date: Mon 09/06/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			




04 Nov '13 11 Nov '13 18 Nov '13 25 Nov '13 02 Dec '13 09 Dec '13 16 Dec '13 23 Dec '13 30 Dec '13 06 Jan '14 13 Jan '14  
M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T

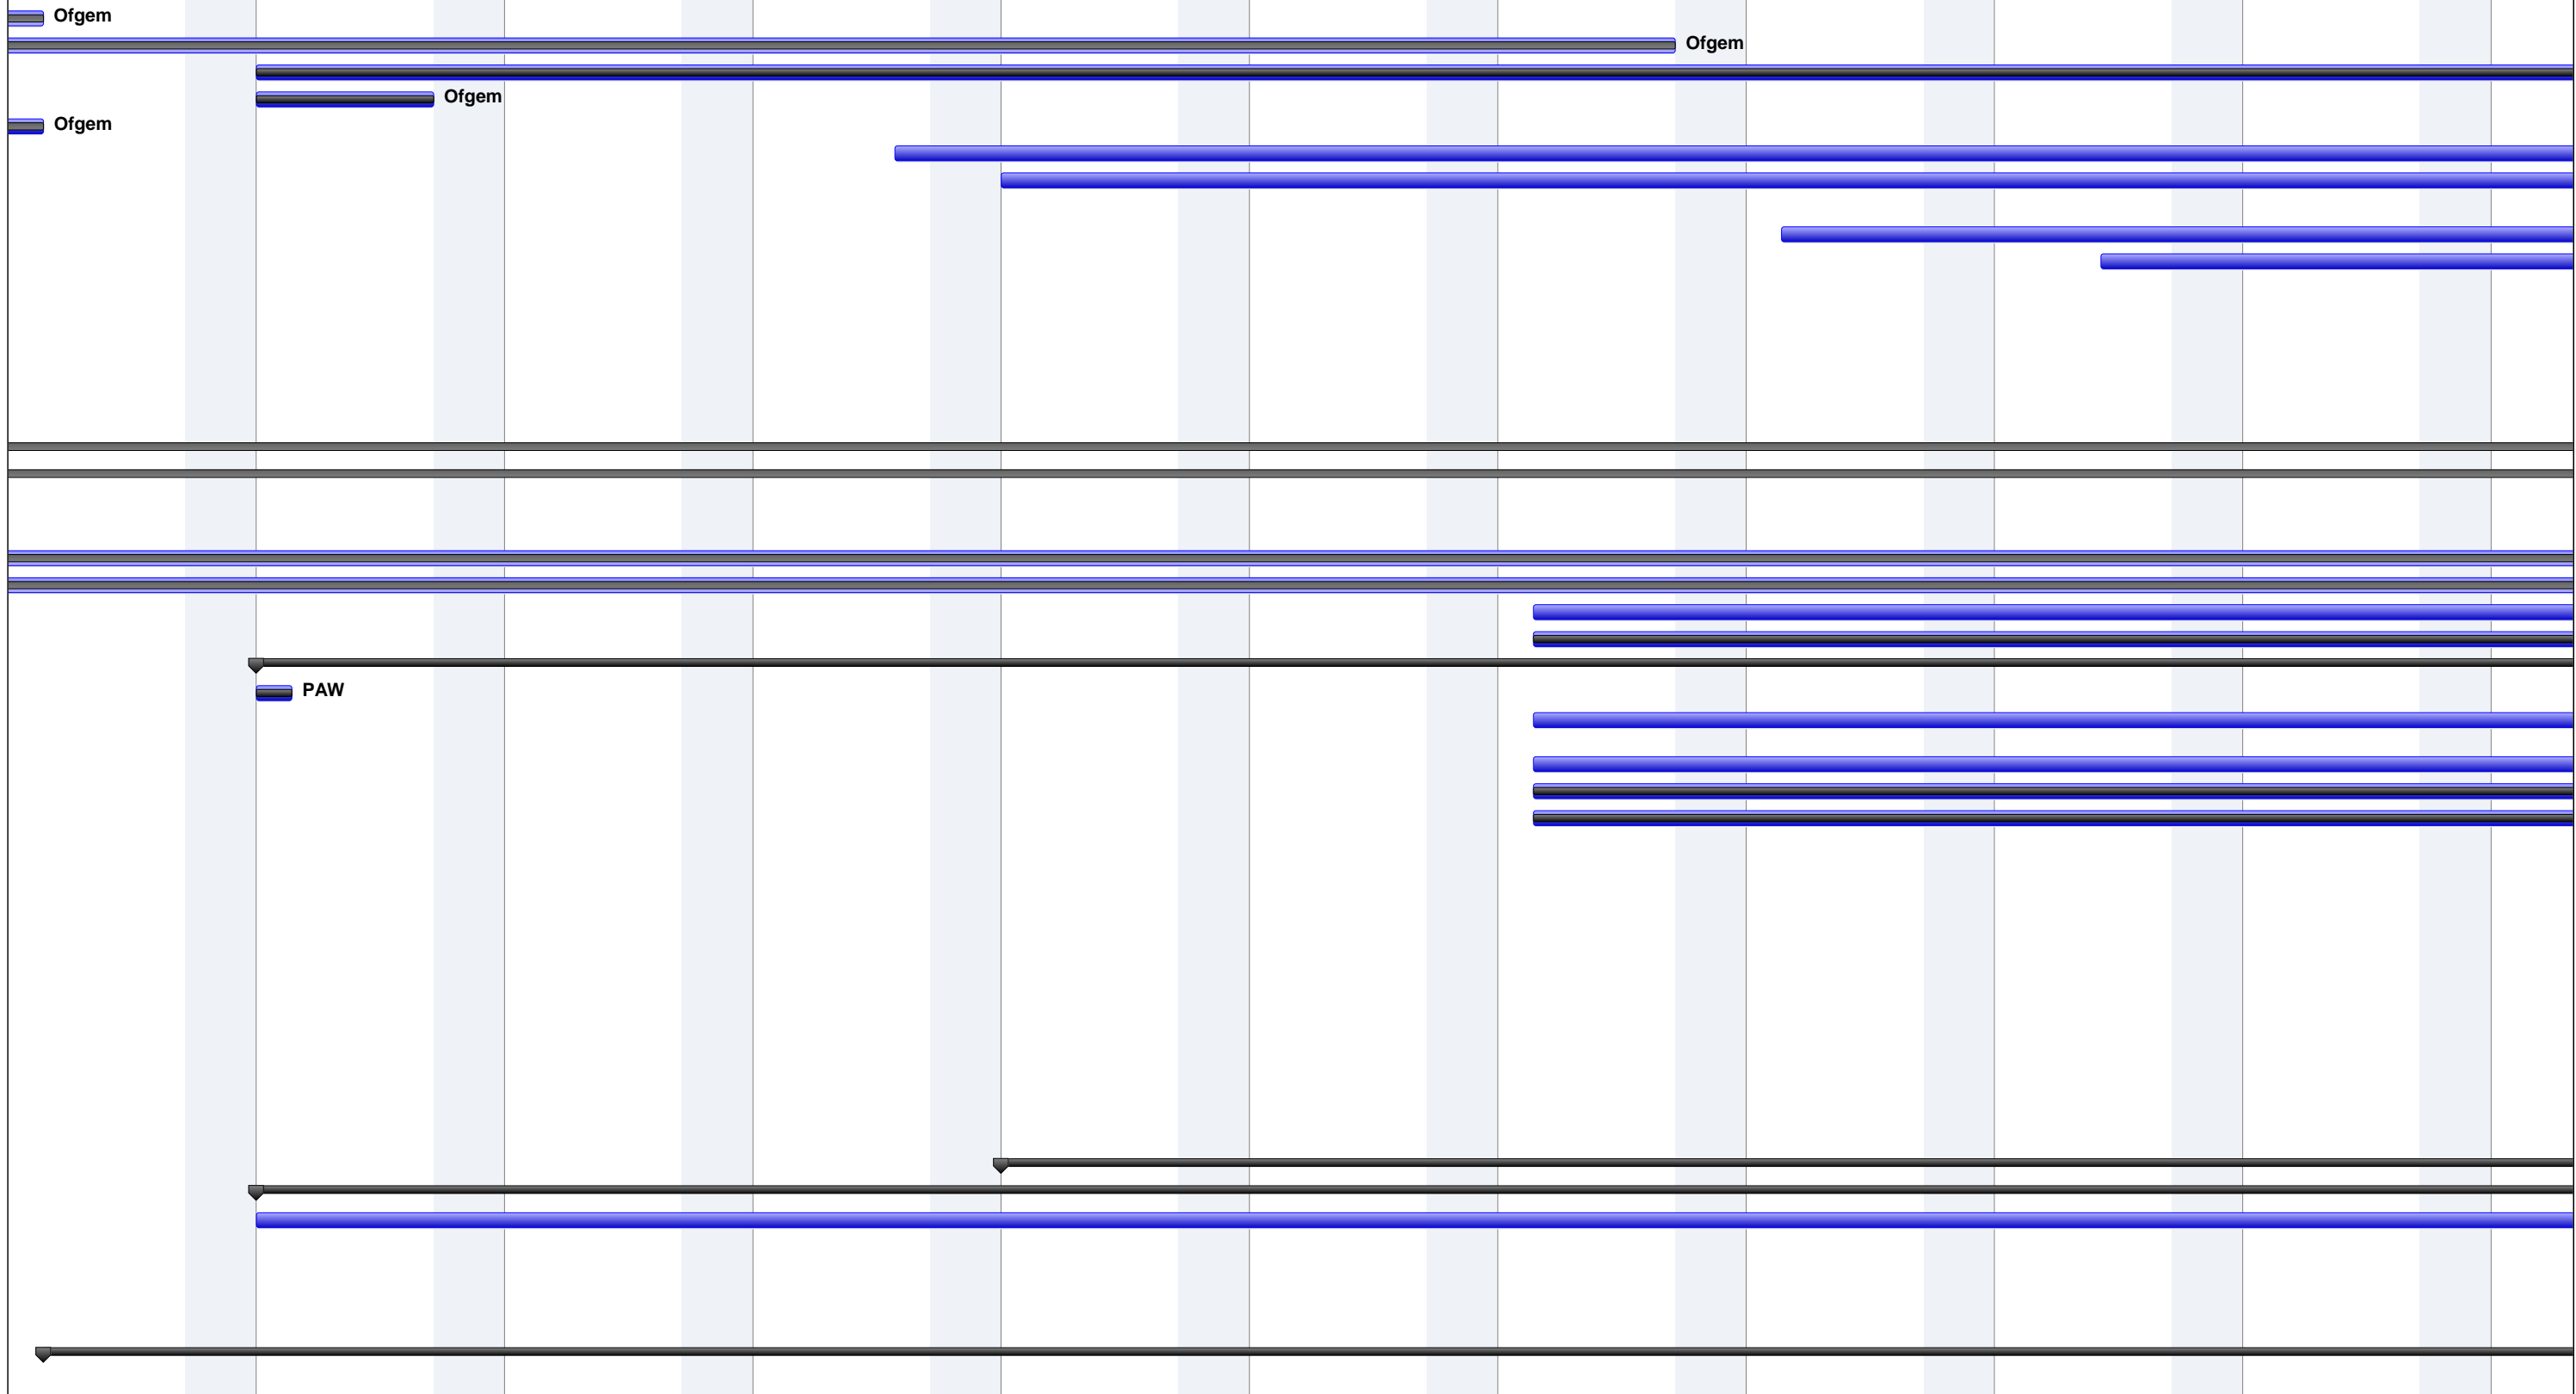


Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

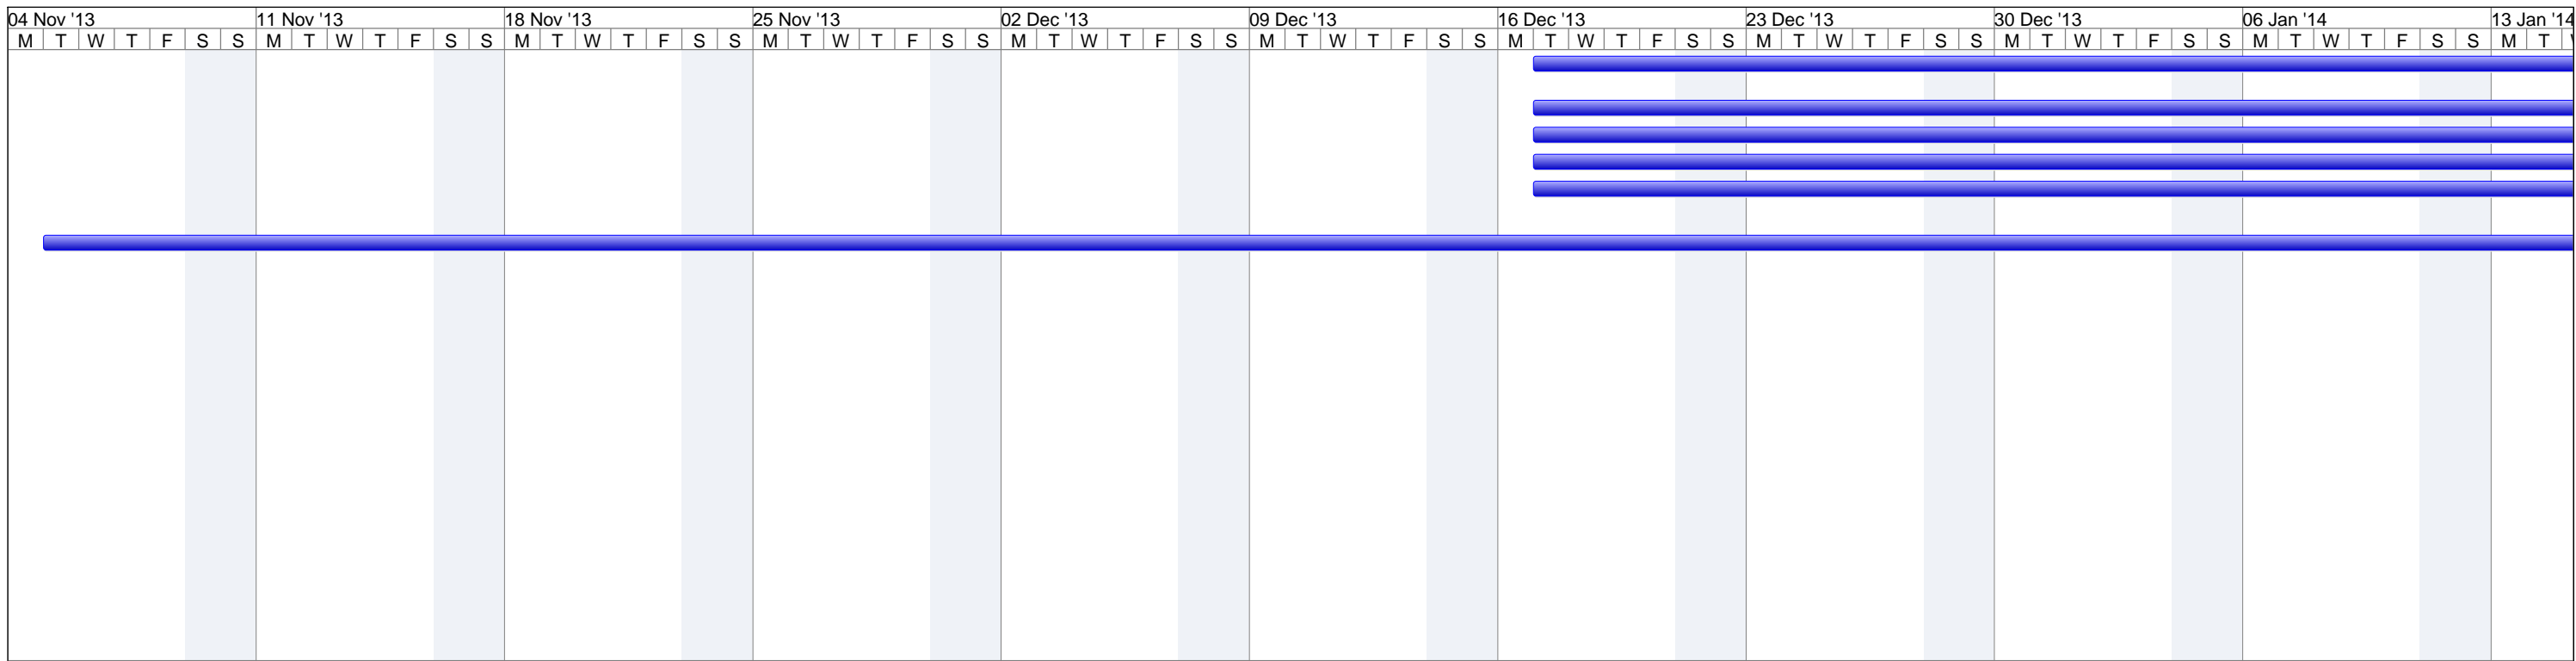


Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

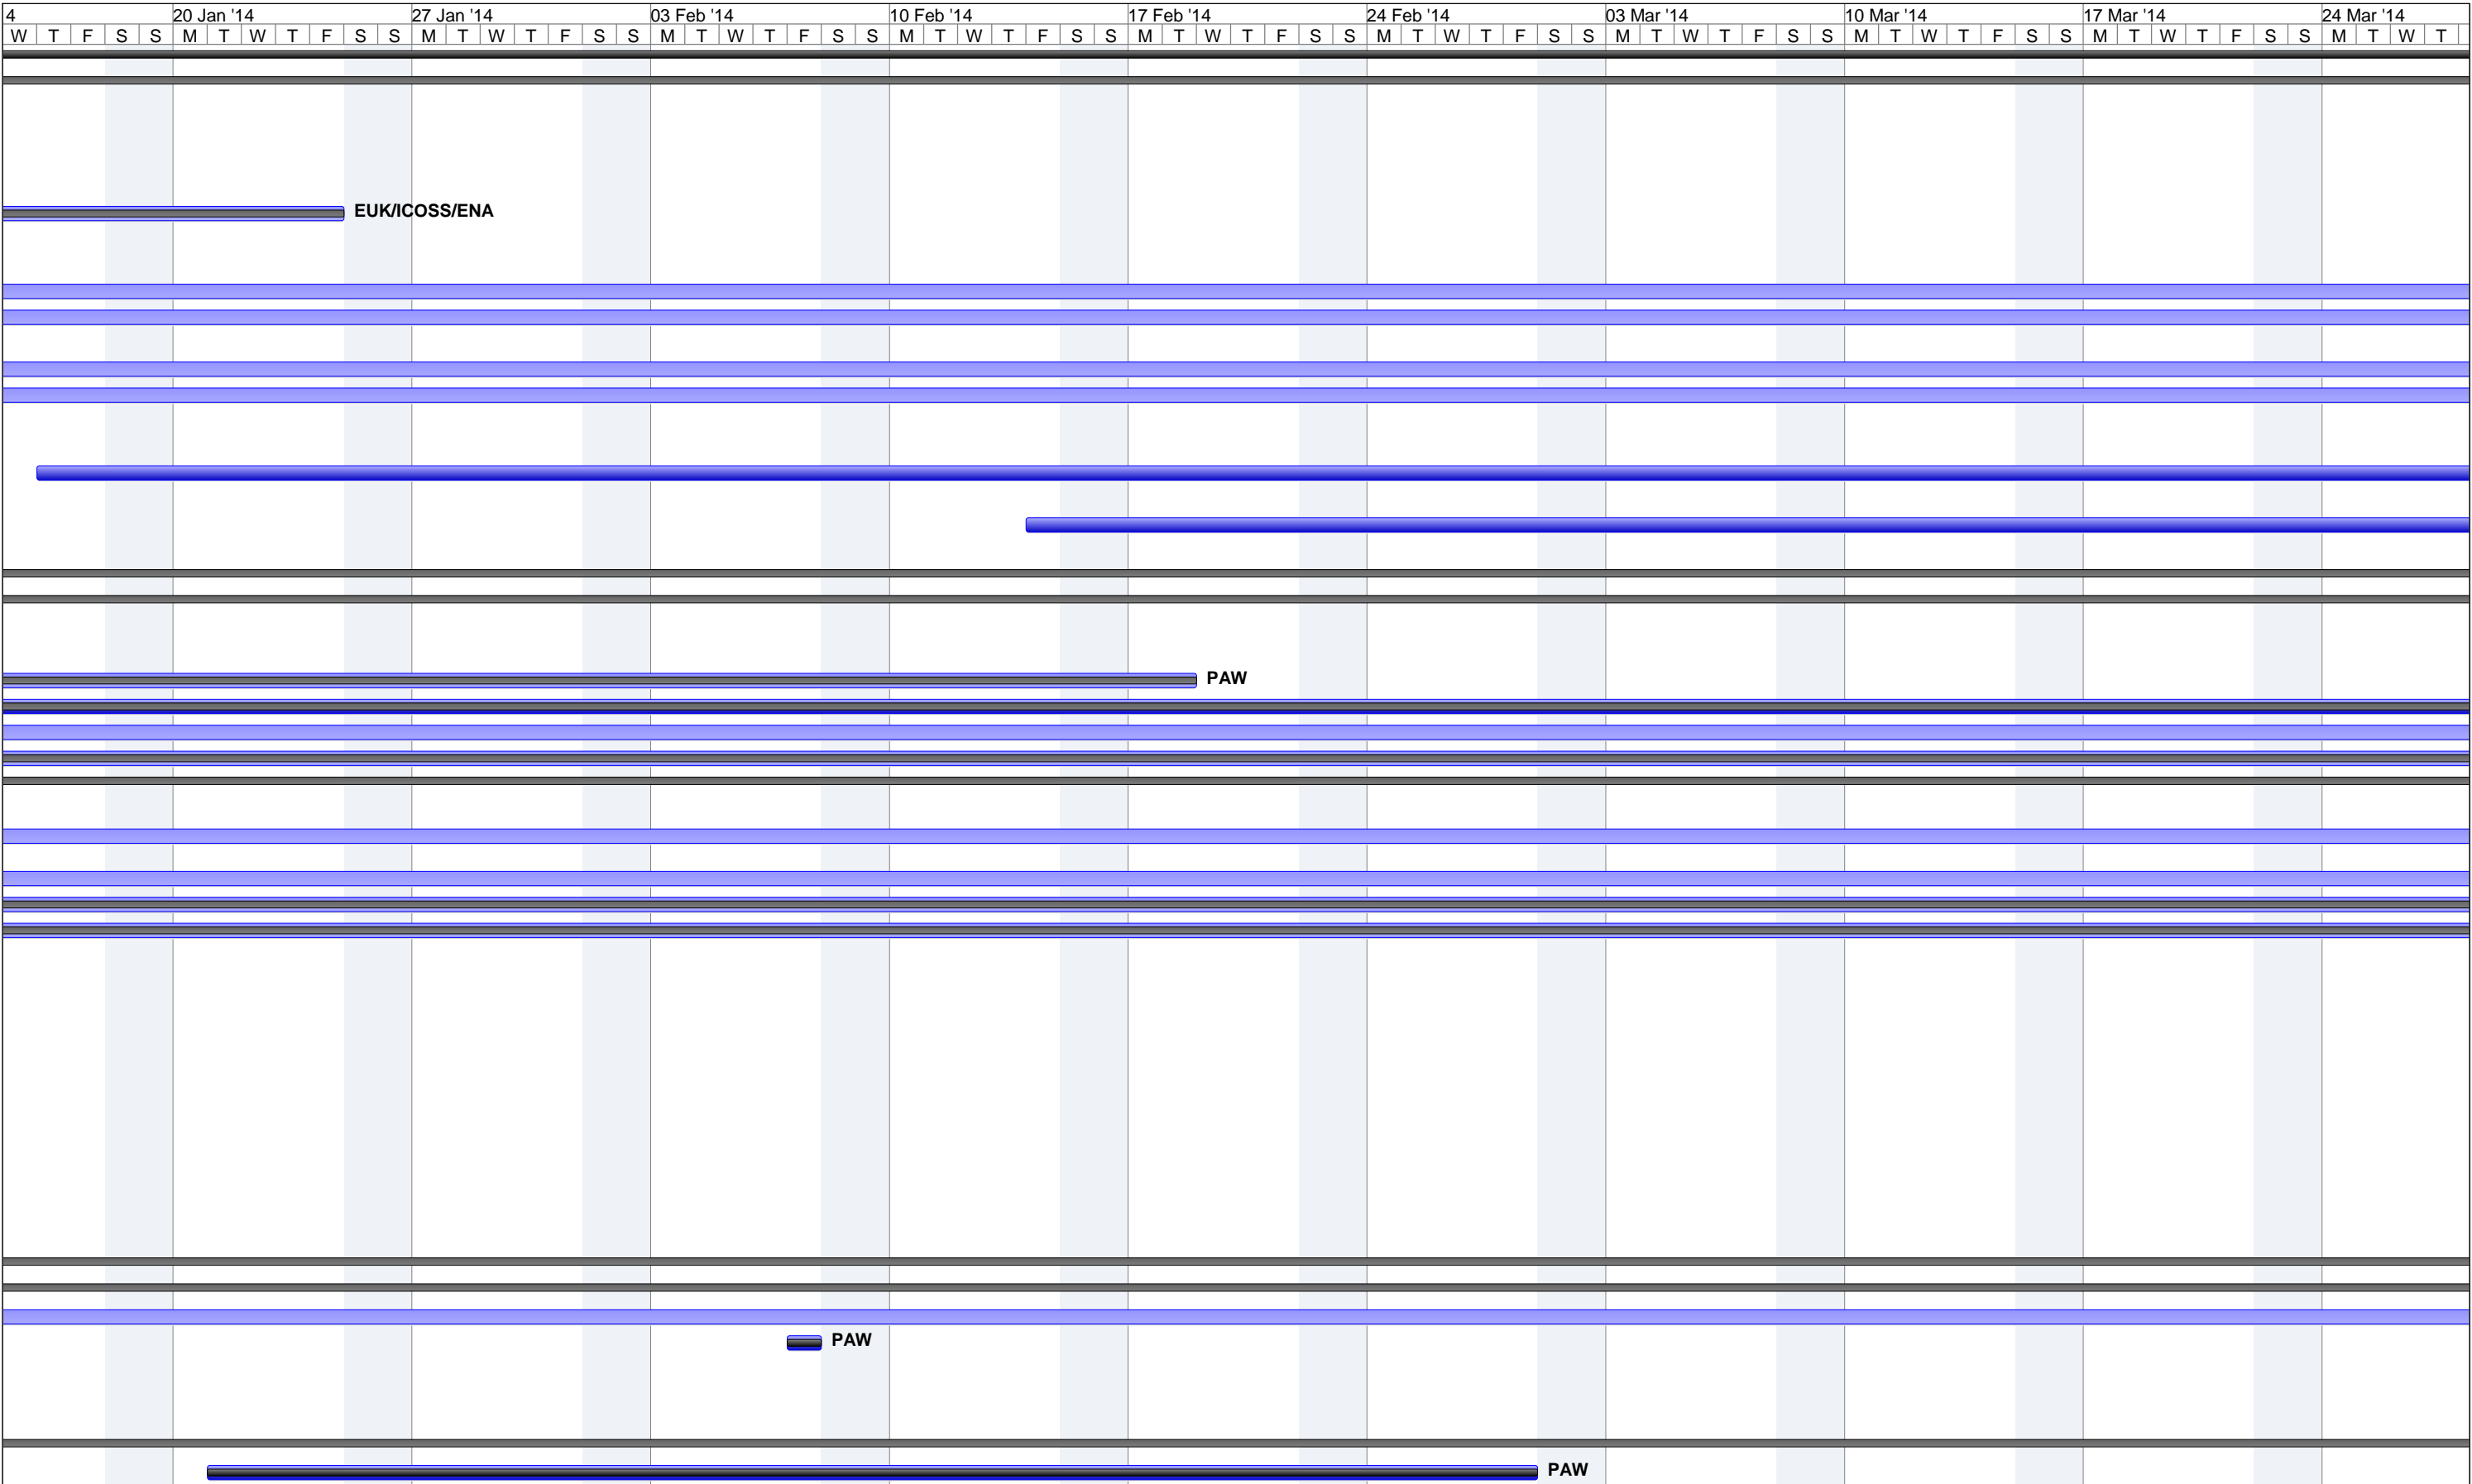

Project: Performance Assurance Plan  
 Date: Mon 09/06/14


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

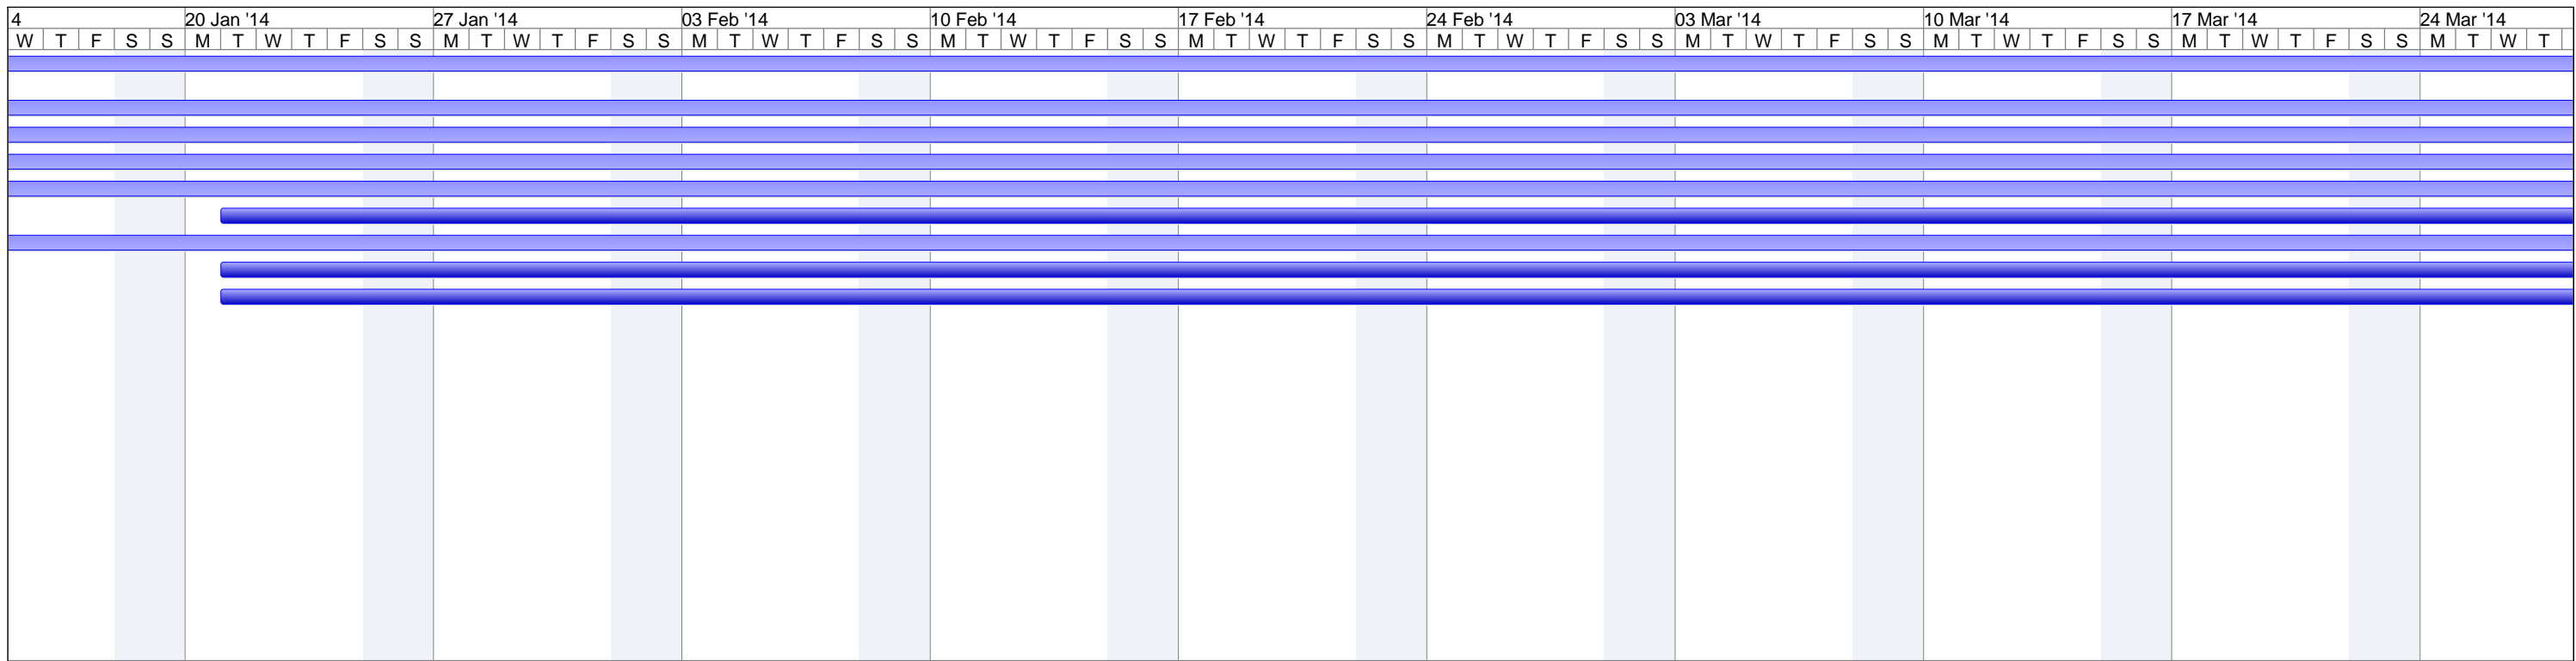

Project: Performance Assurance Plan  
Date: Mon 09/06/14


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

31 Mar '14 07 Apr '14 14 Apr '14 21 Apr '14 28 Apr '14 05 May '14 12 May '14 19 May '14 26 May '14 02 Jun '14

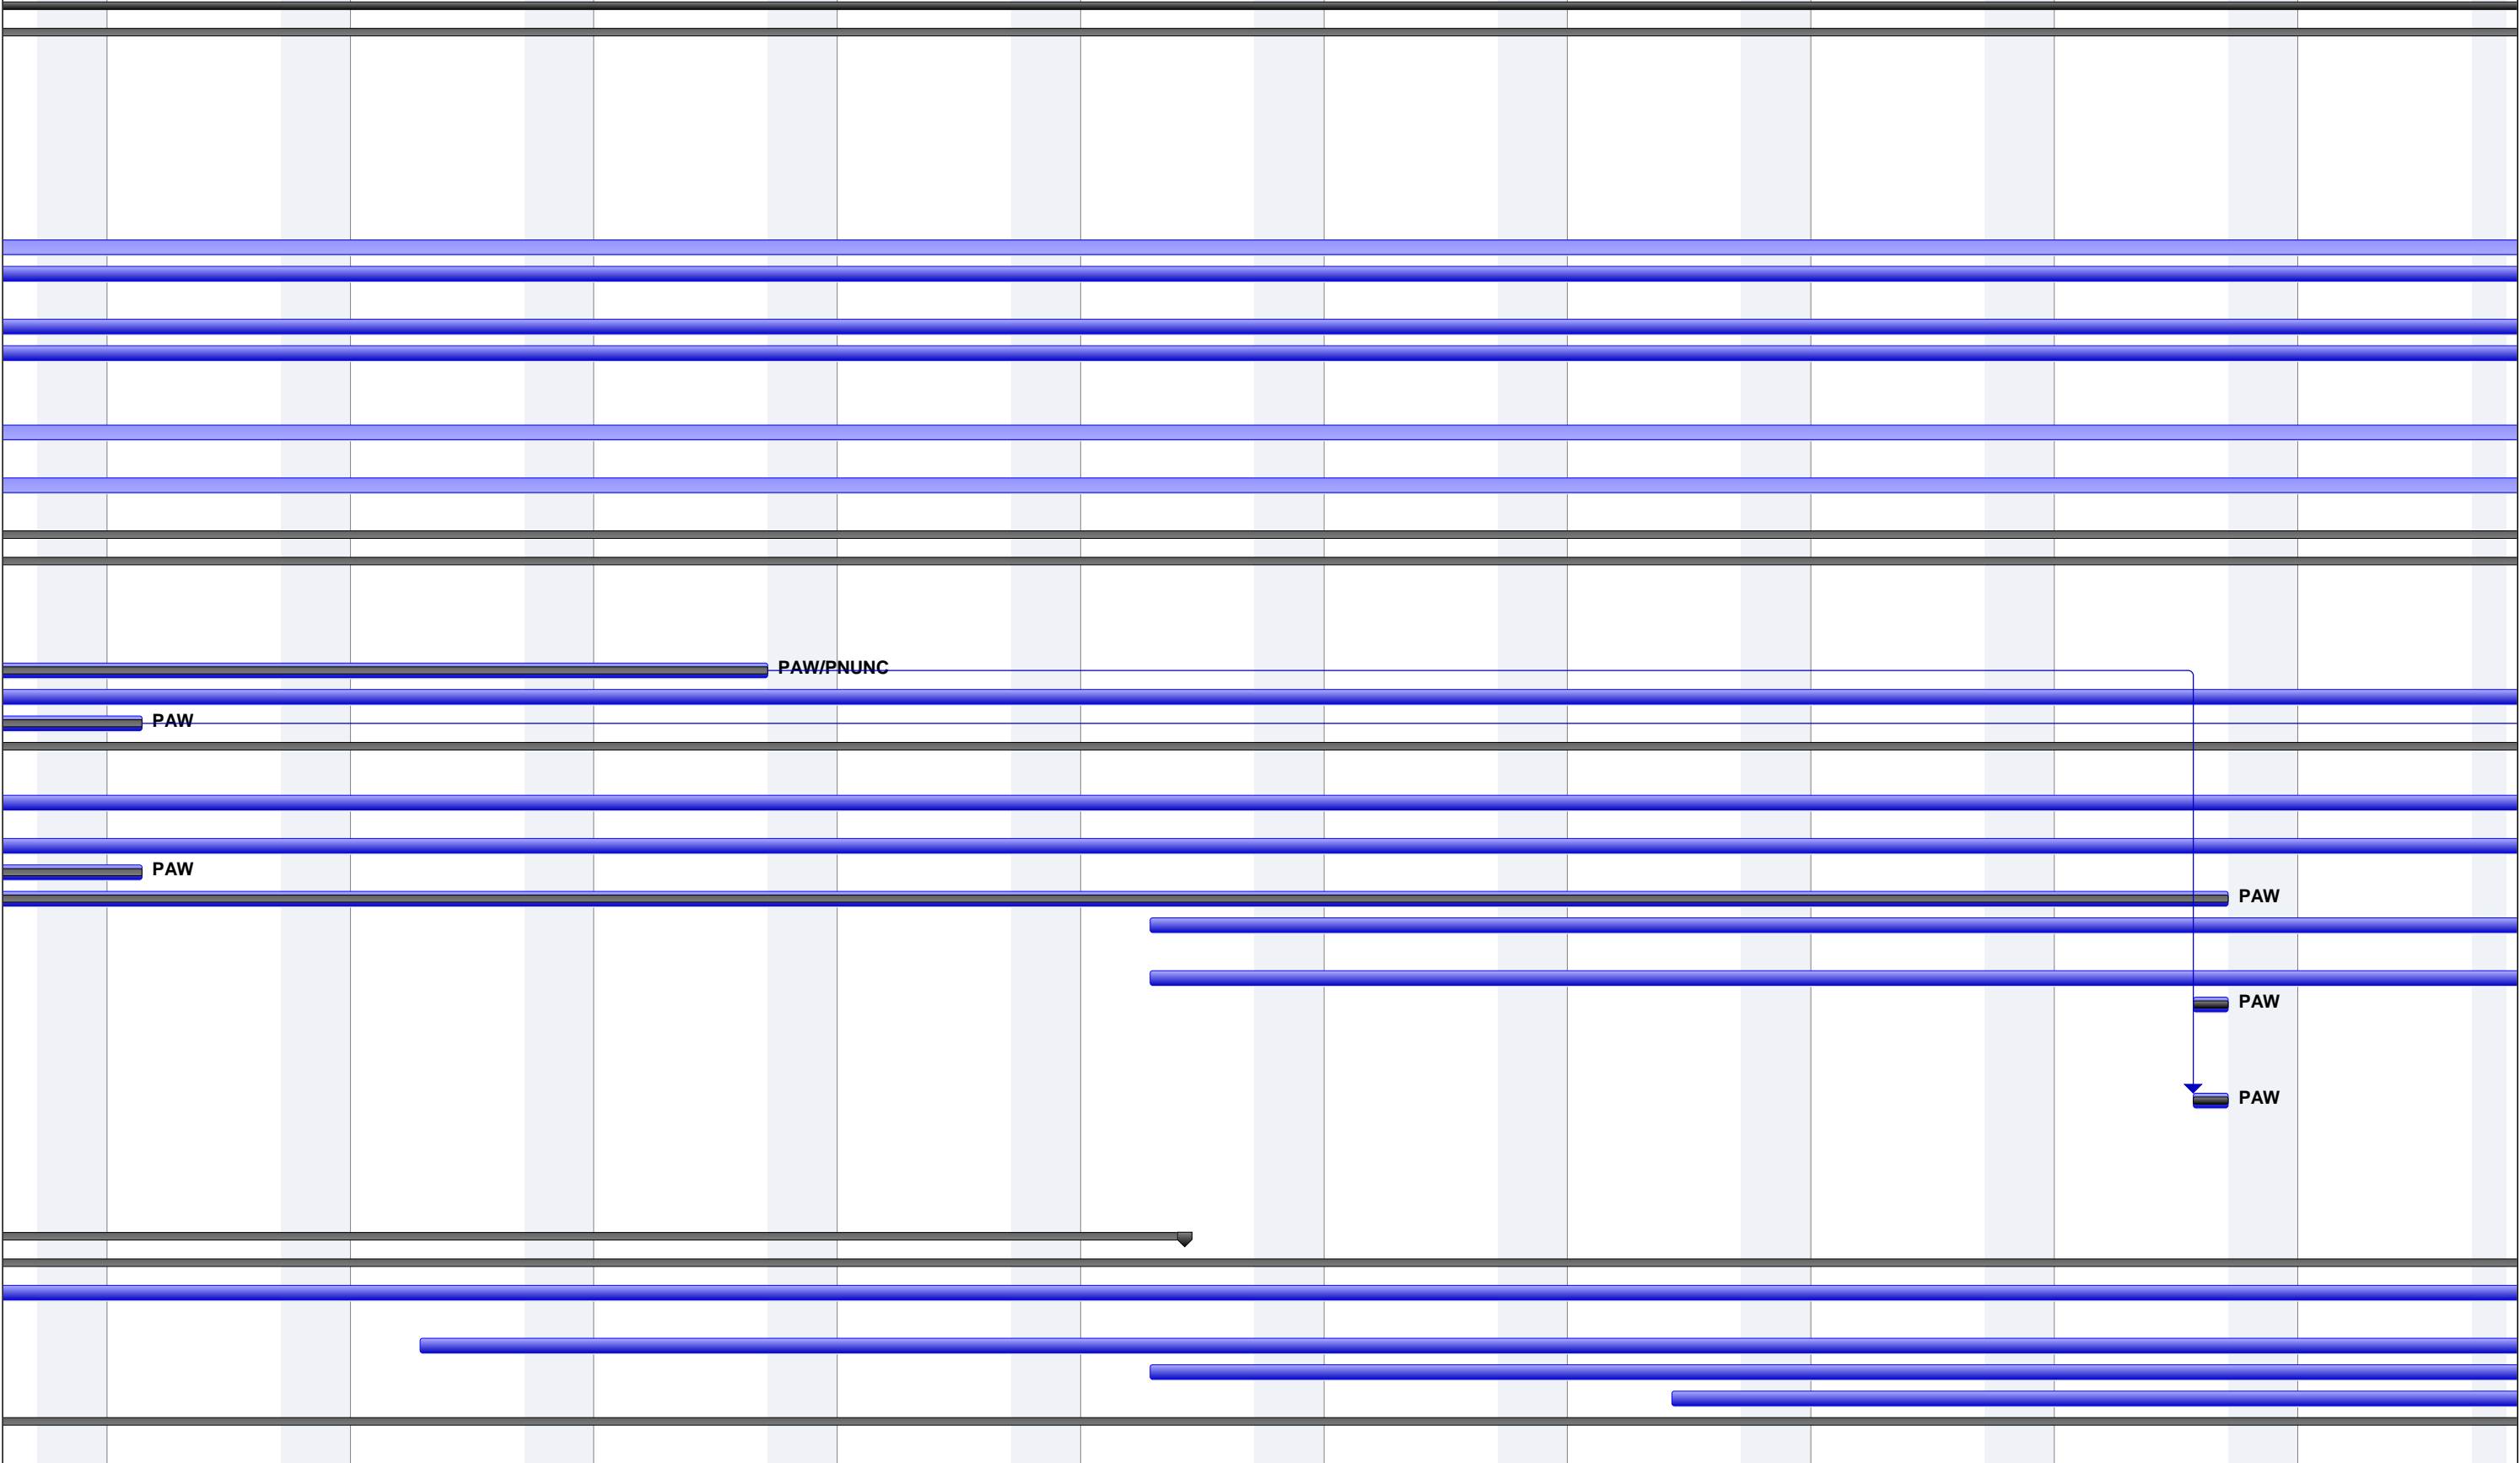

Project: Performance Assurance Plan  
Date: Mon 09/06/14


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

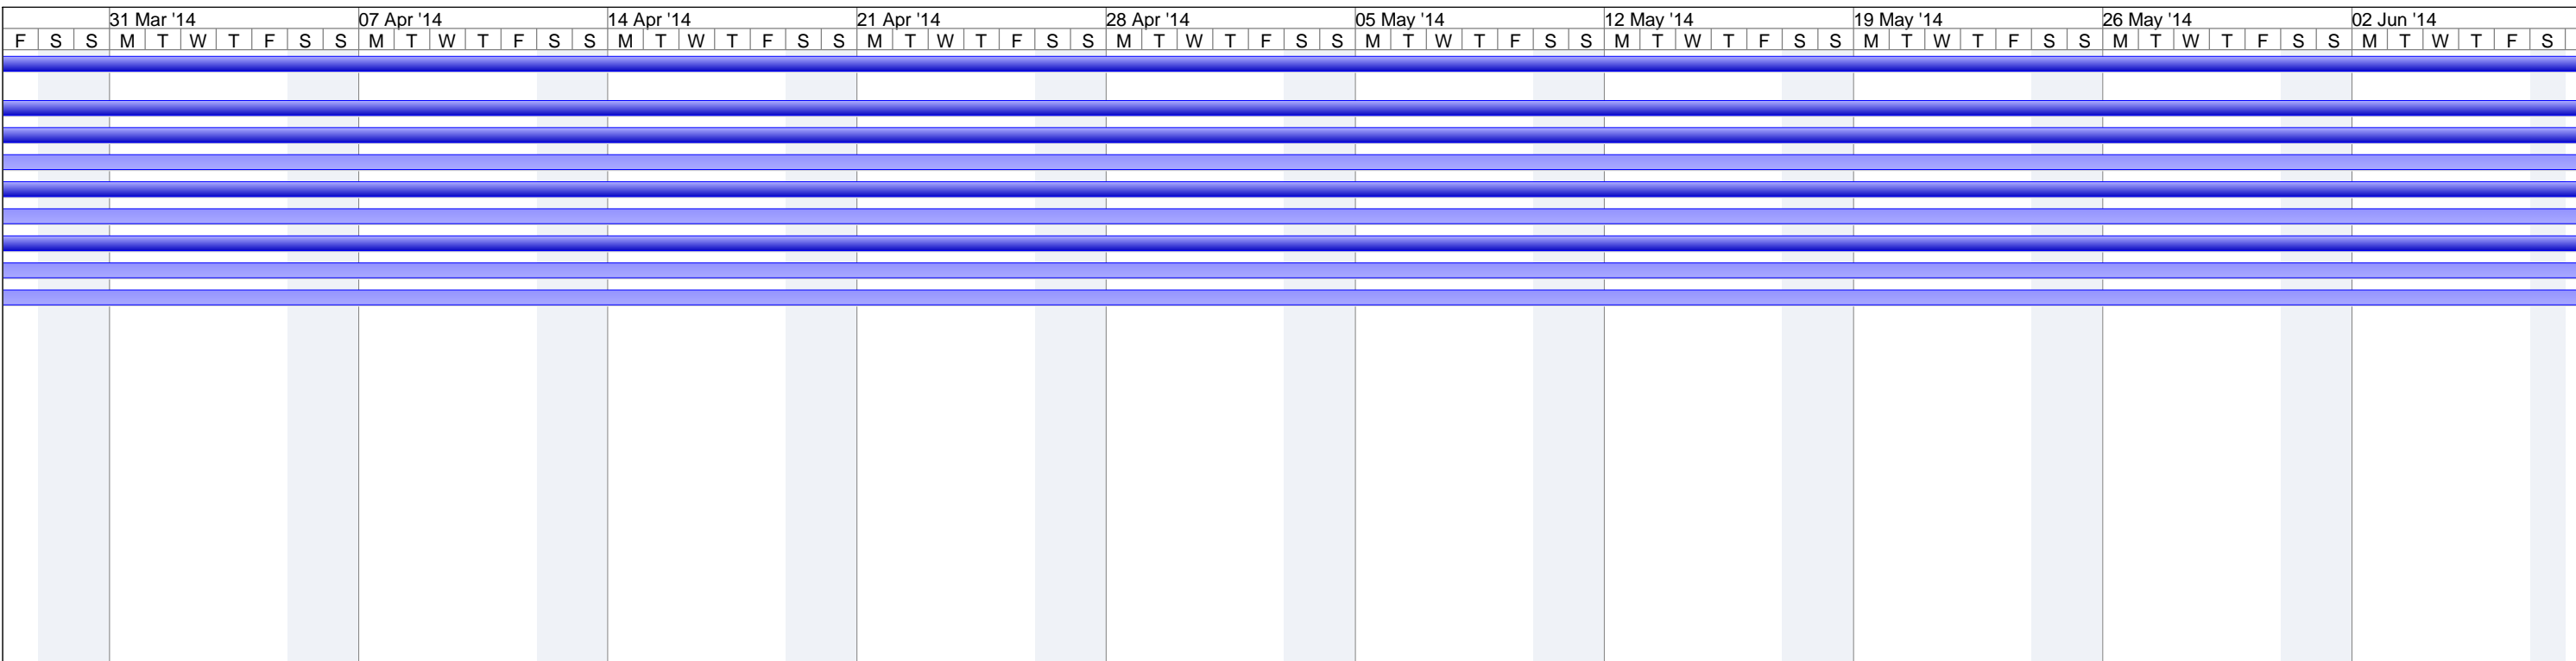

Project: Performance Assurance Plan  
Date: Mon 09/06/14


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

09 Jun '14 16 Jun '14 23 Jun '14 30 Jun '14 07 Jul '14 14 Jul '14 21 Jul '14 28 Jul '14 04 Aug '14 11 Aug '14 18 Au

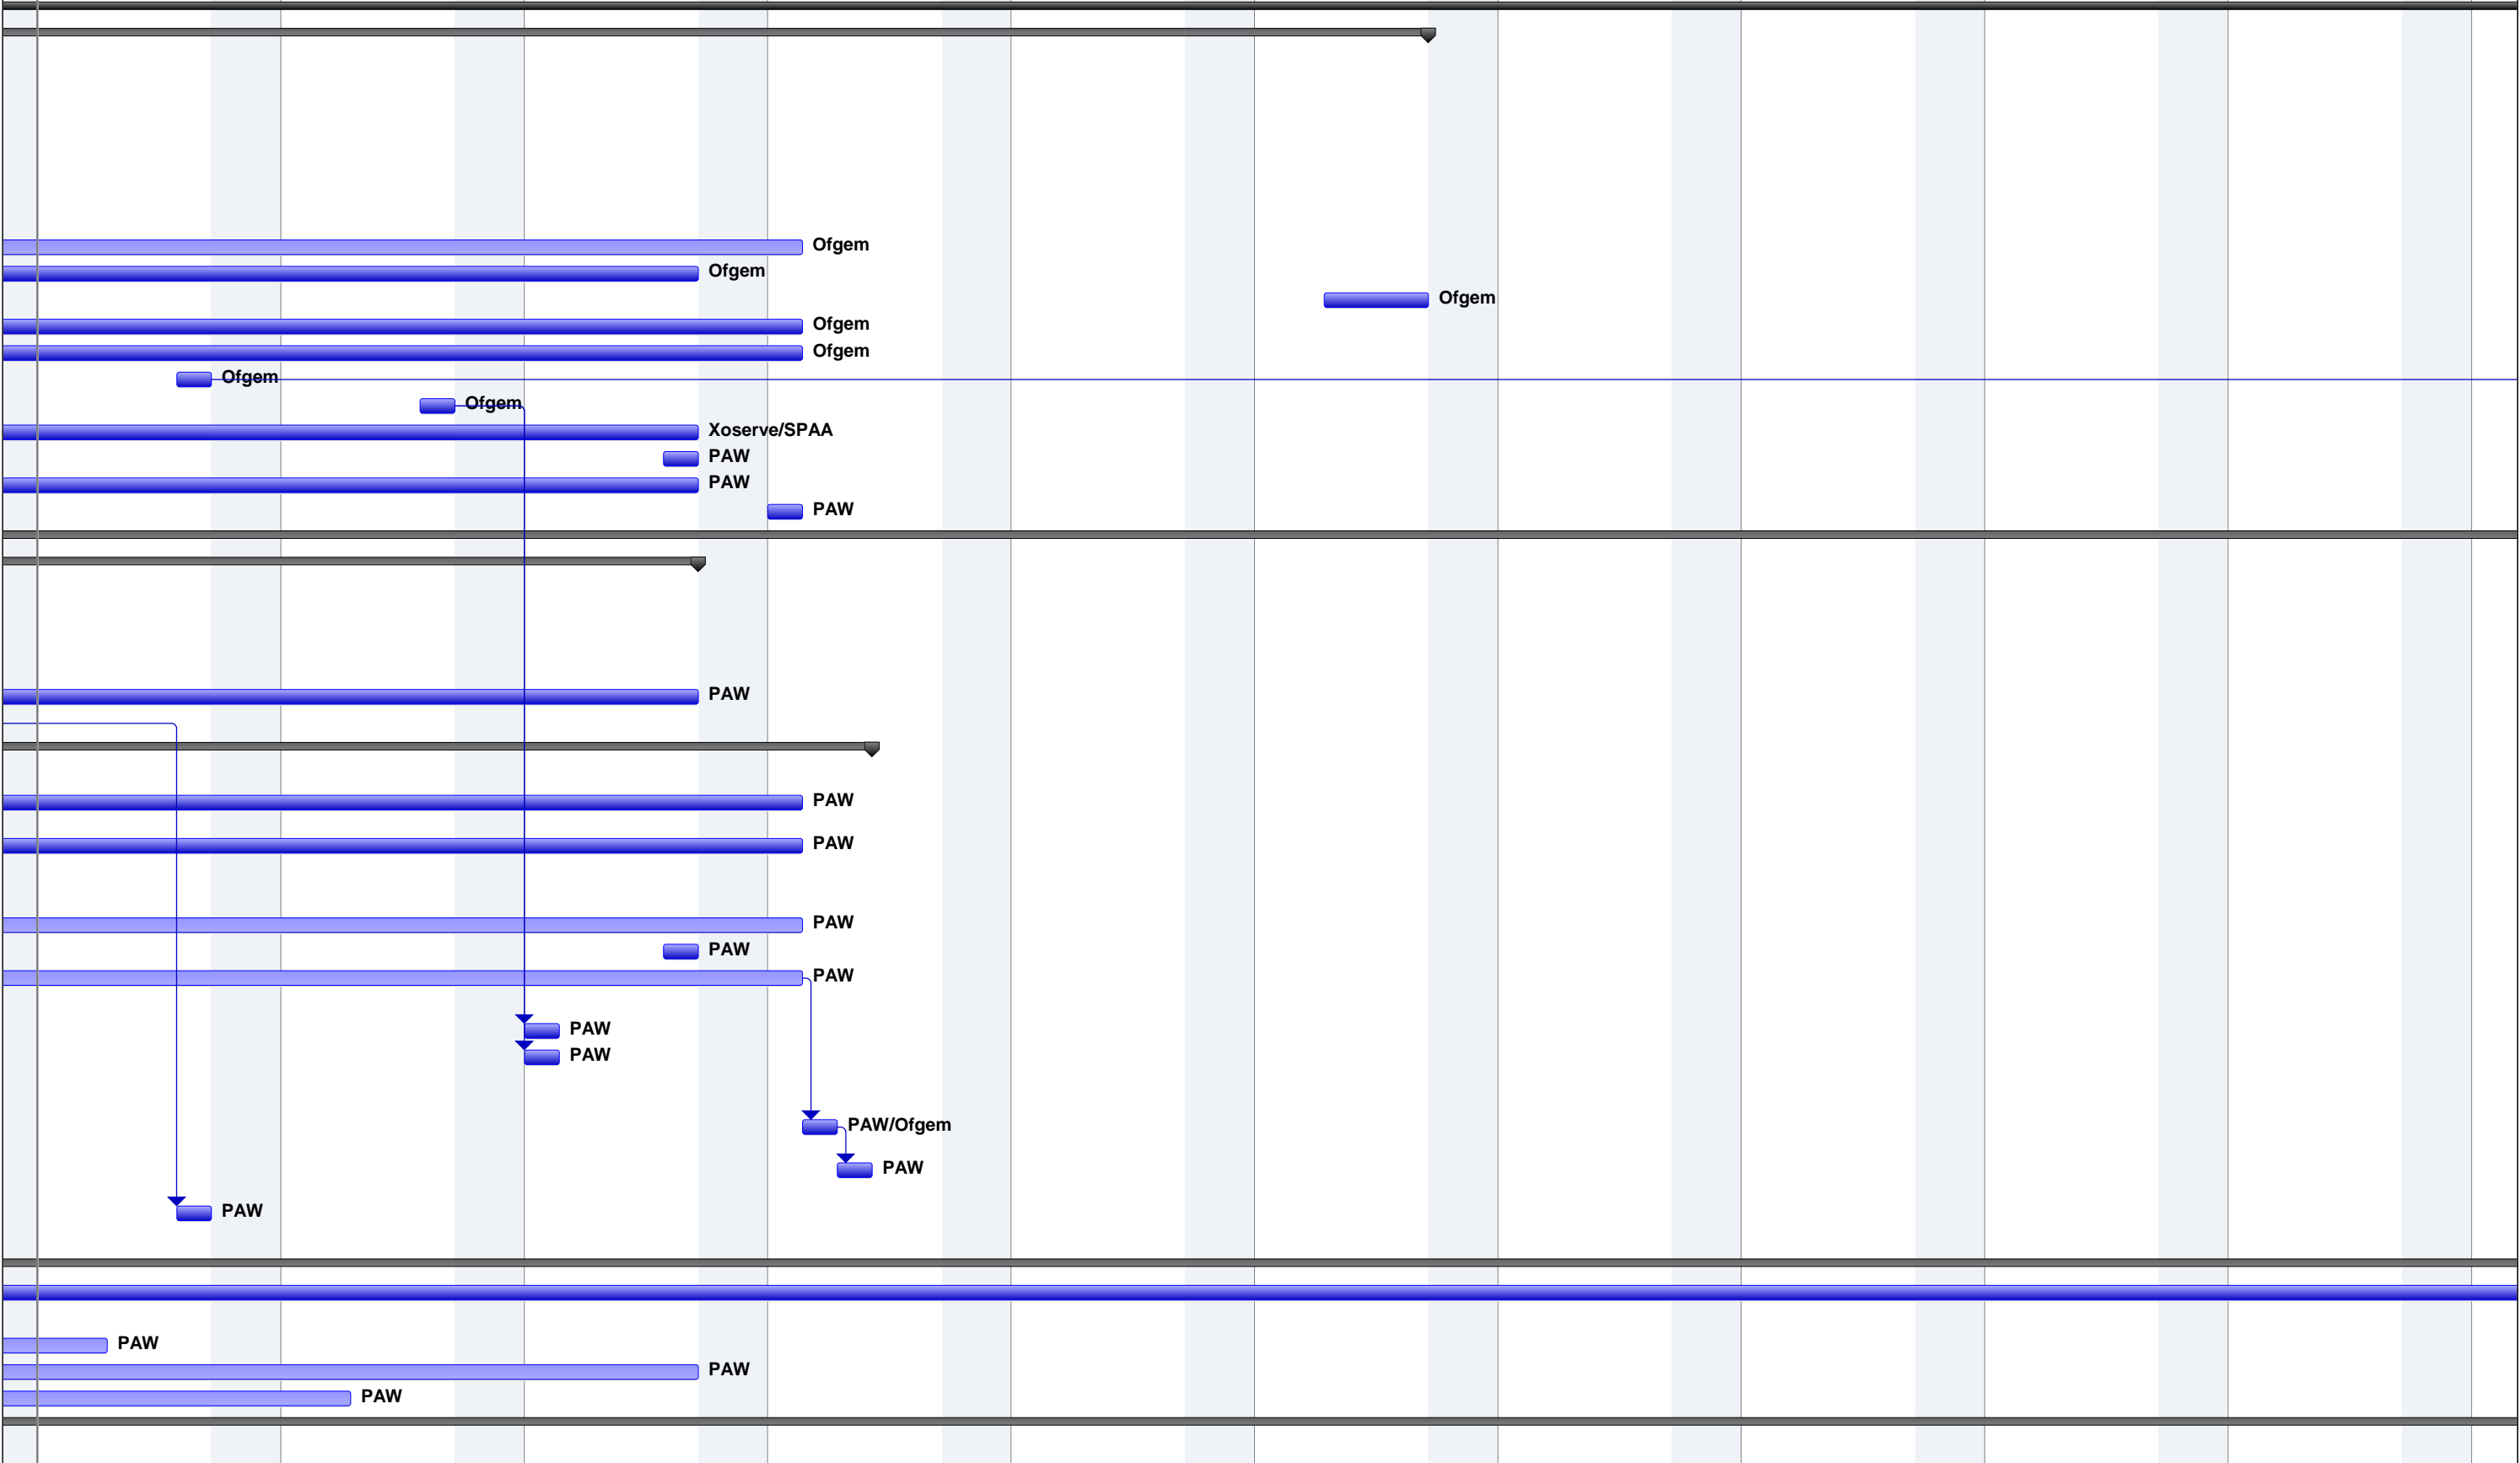

Project: Performance Assurance Plan  
Date: Mon 09/06/14


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

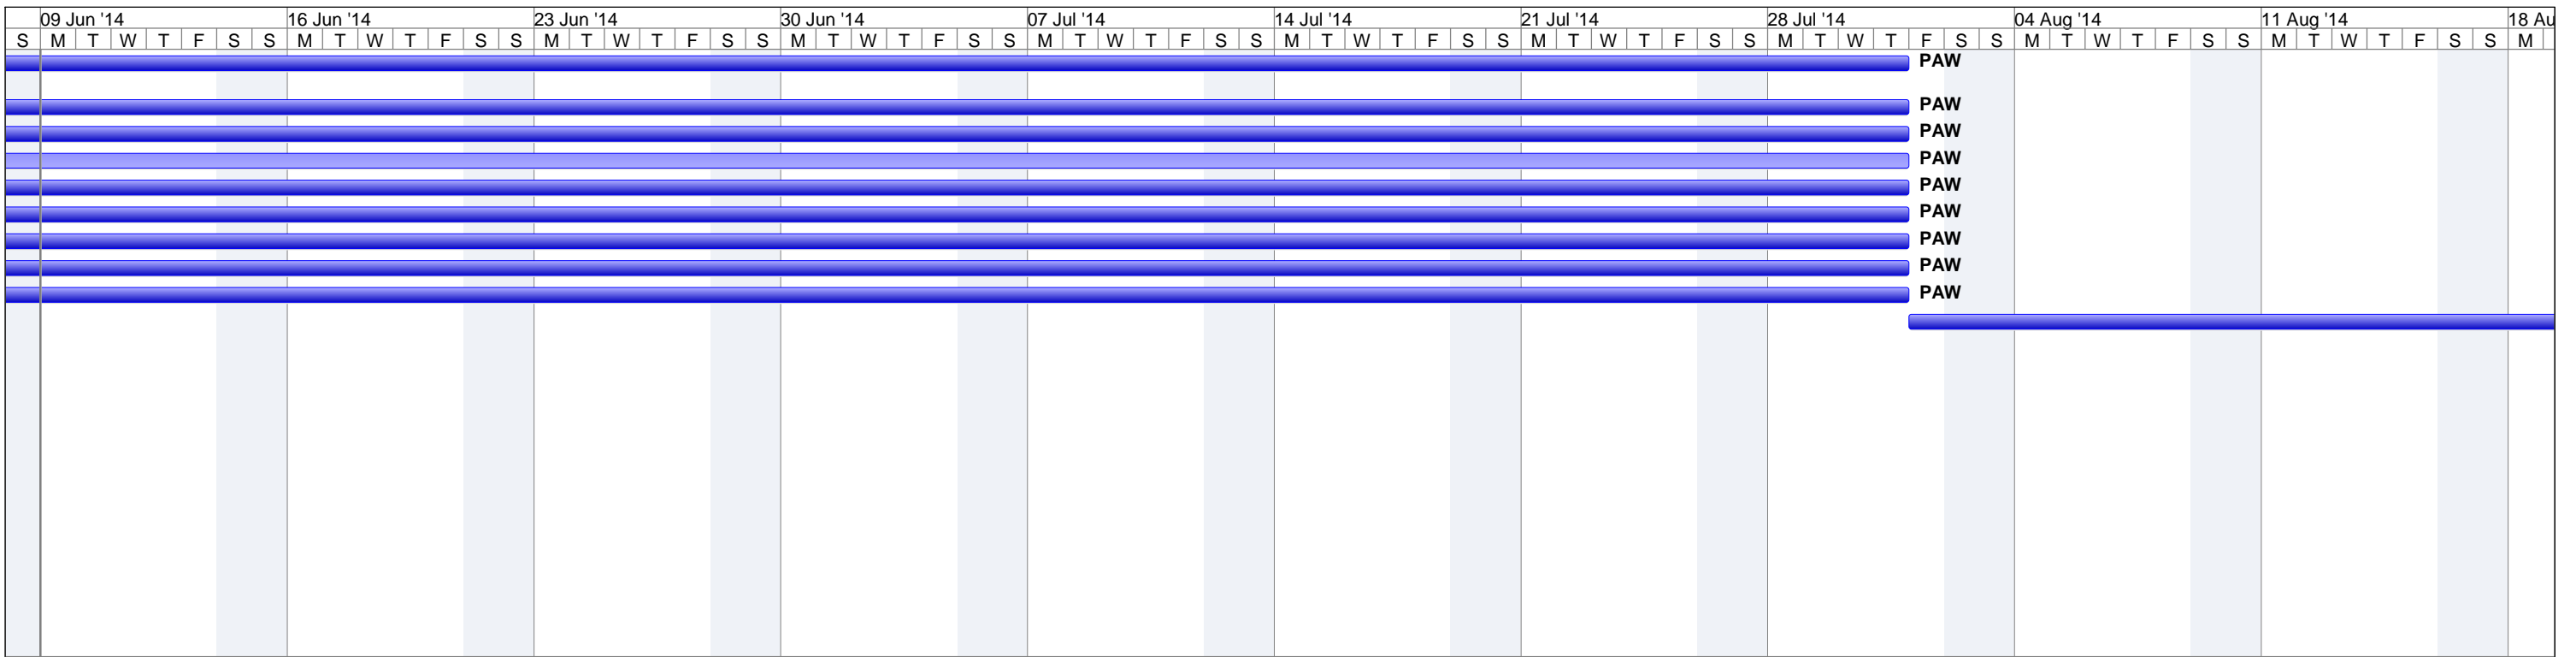

Project: Performance Assurance Plan  
Date: Mon 09/06/14


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			



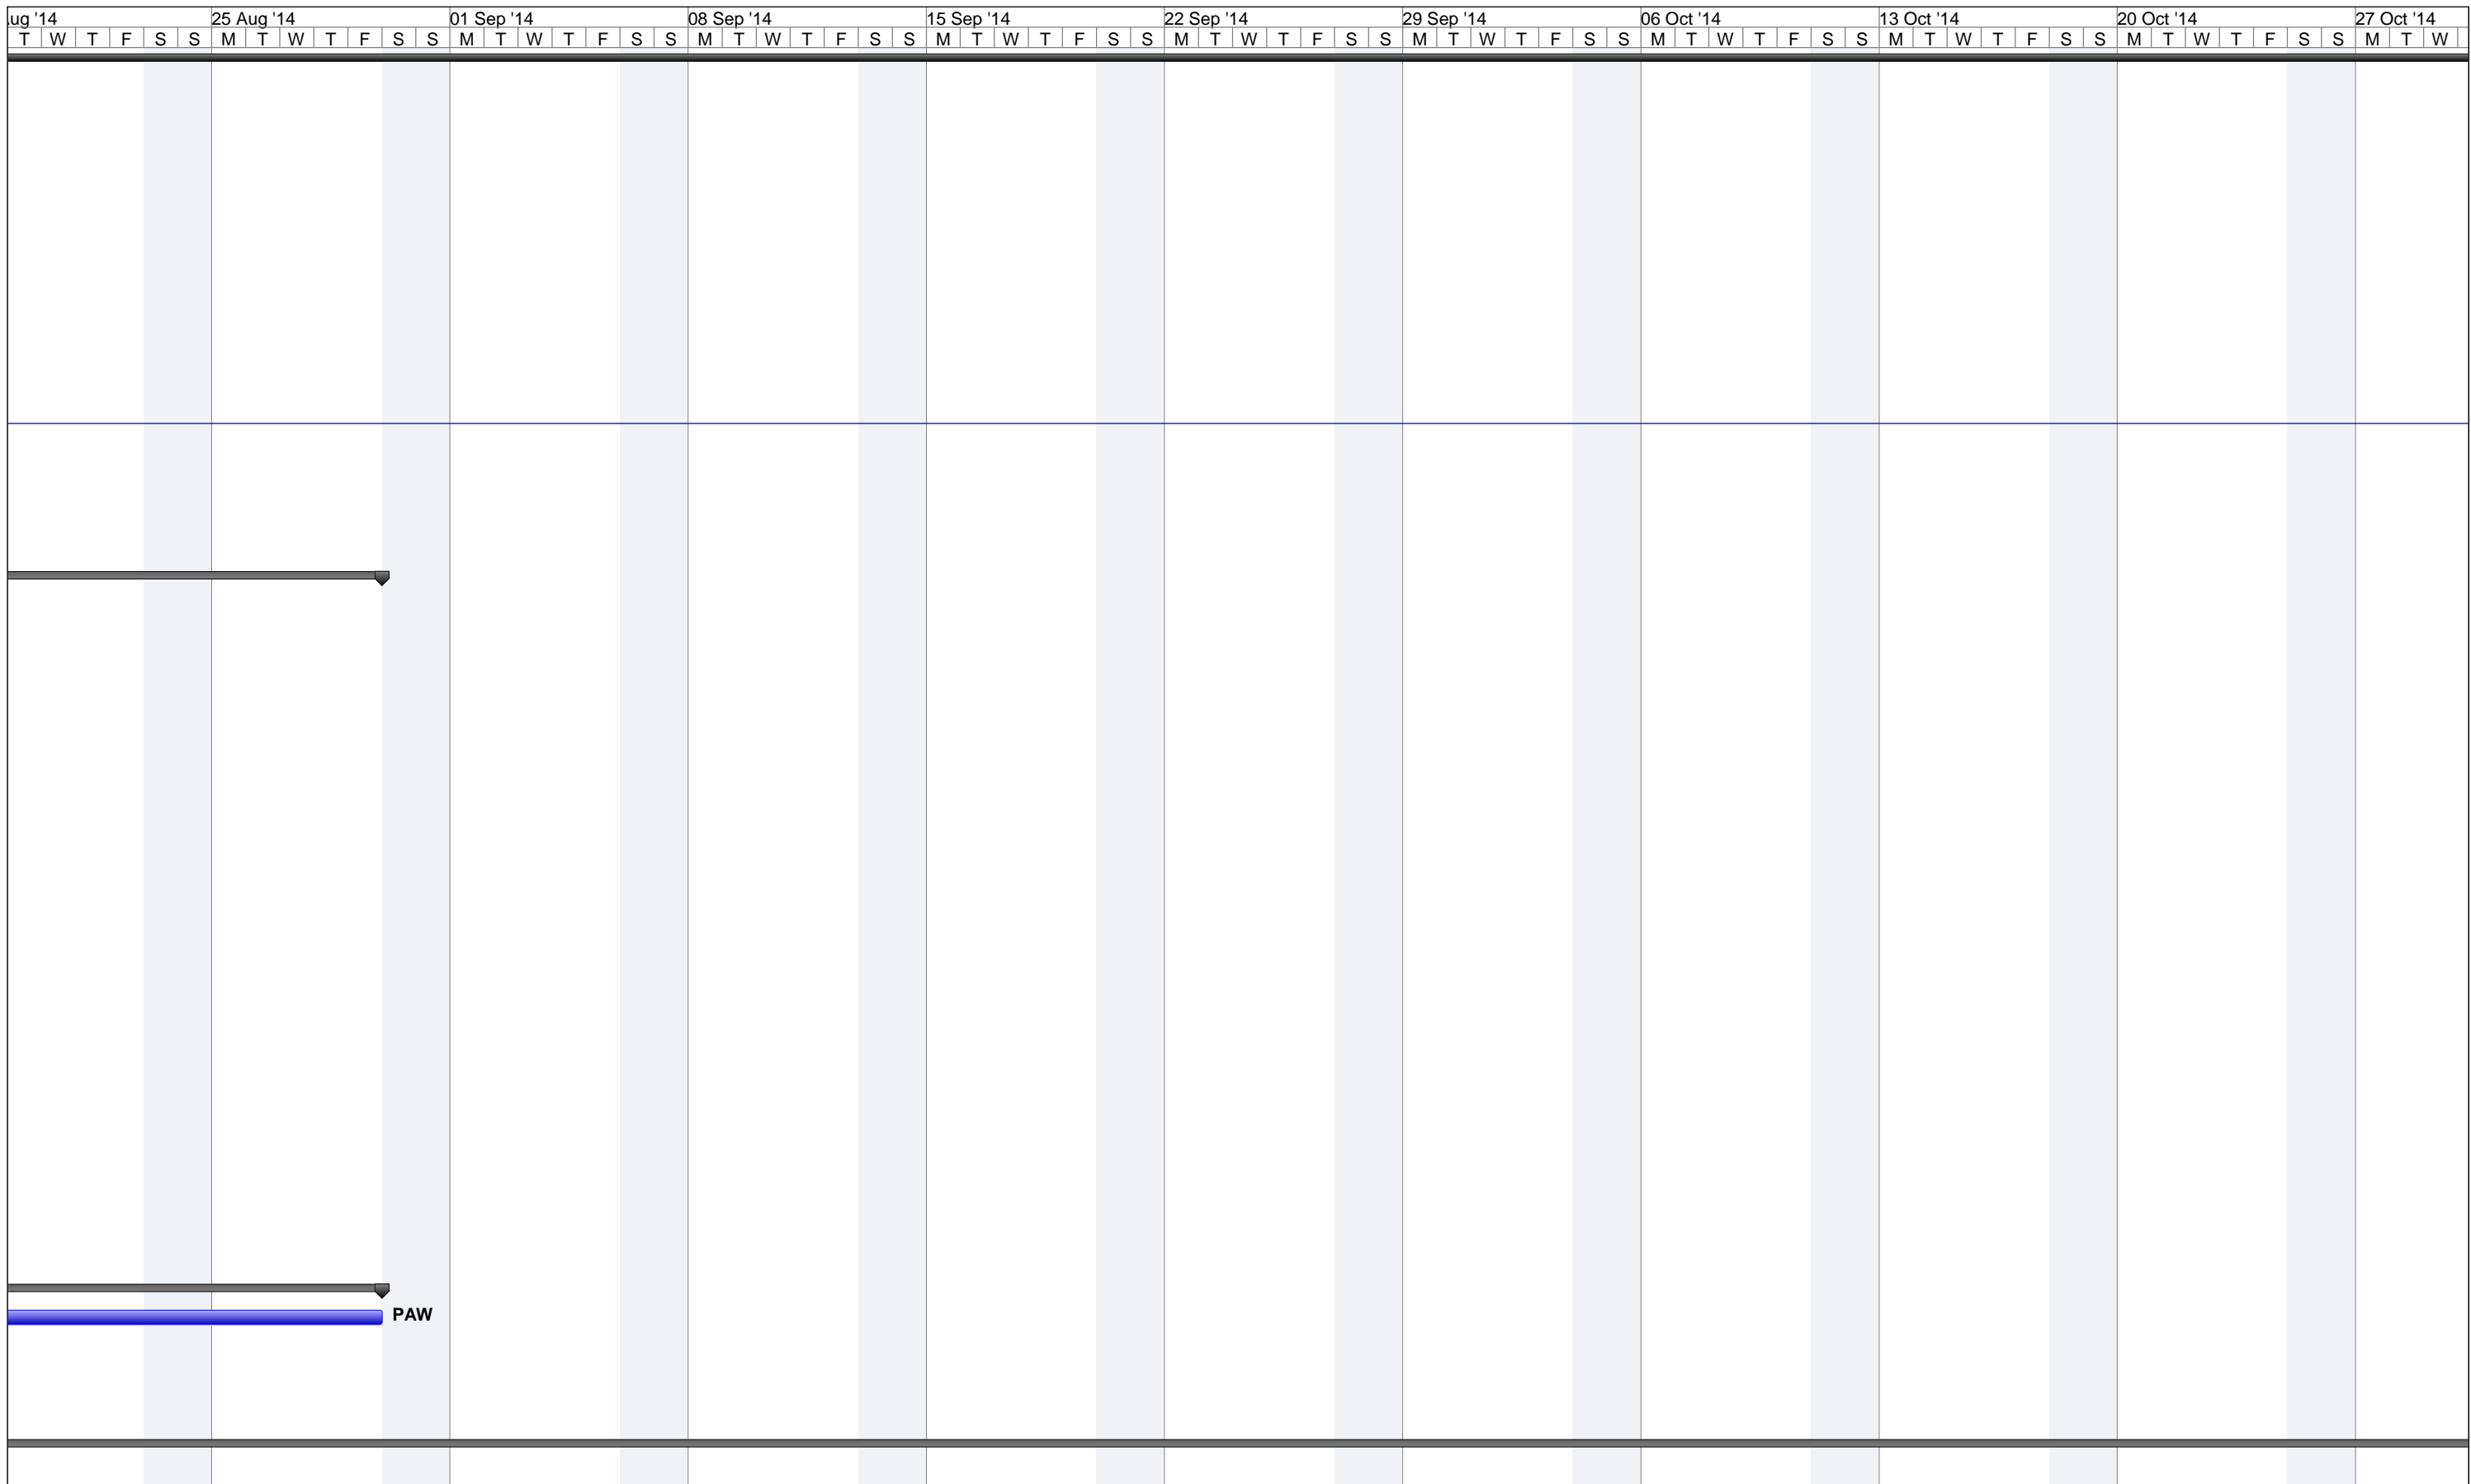

Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

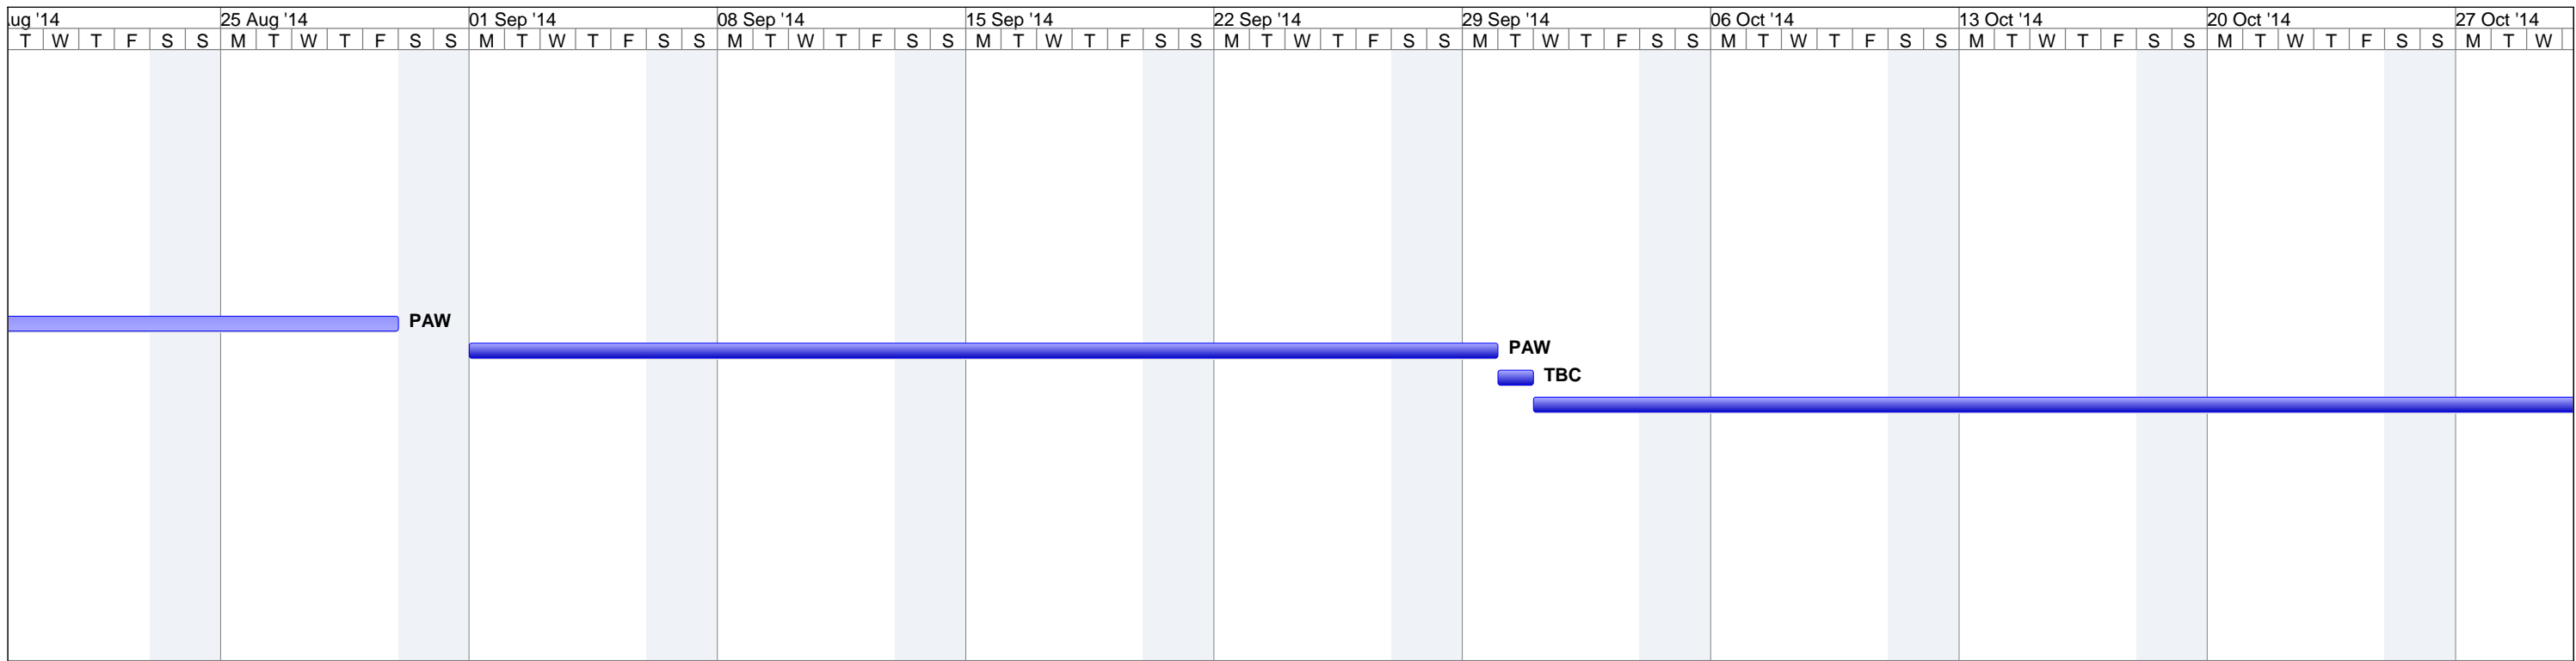


Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			




Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

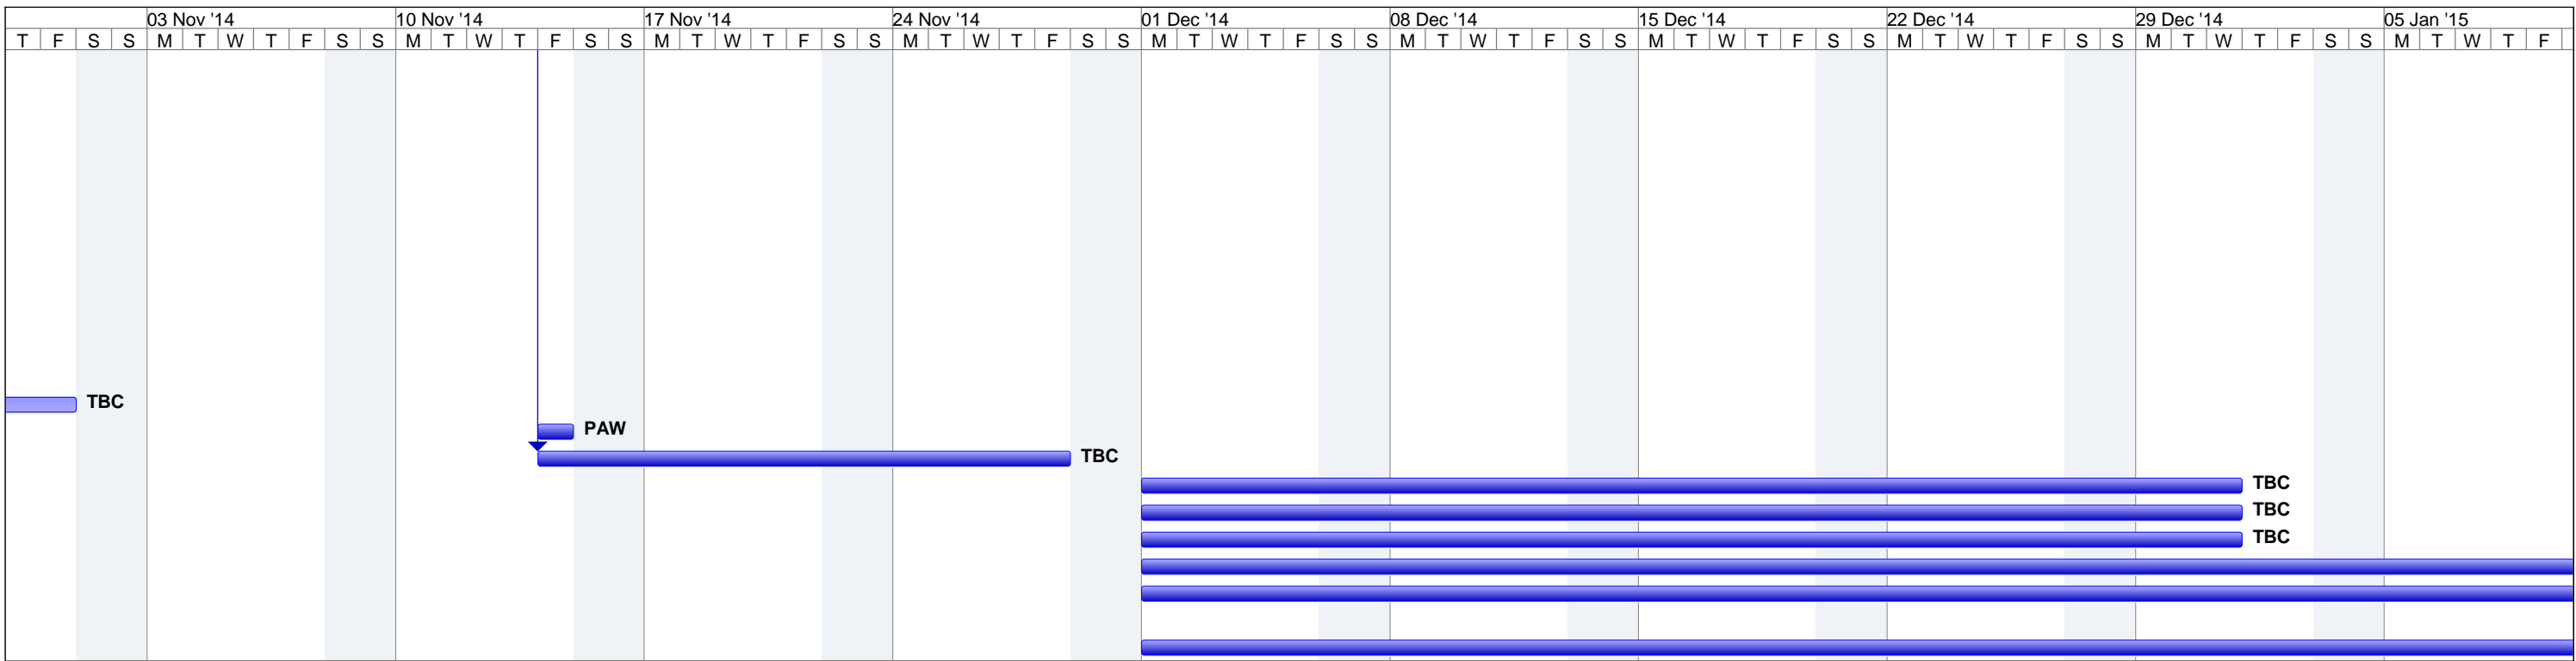


Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

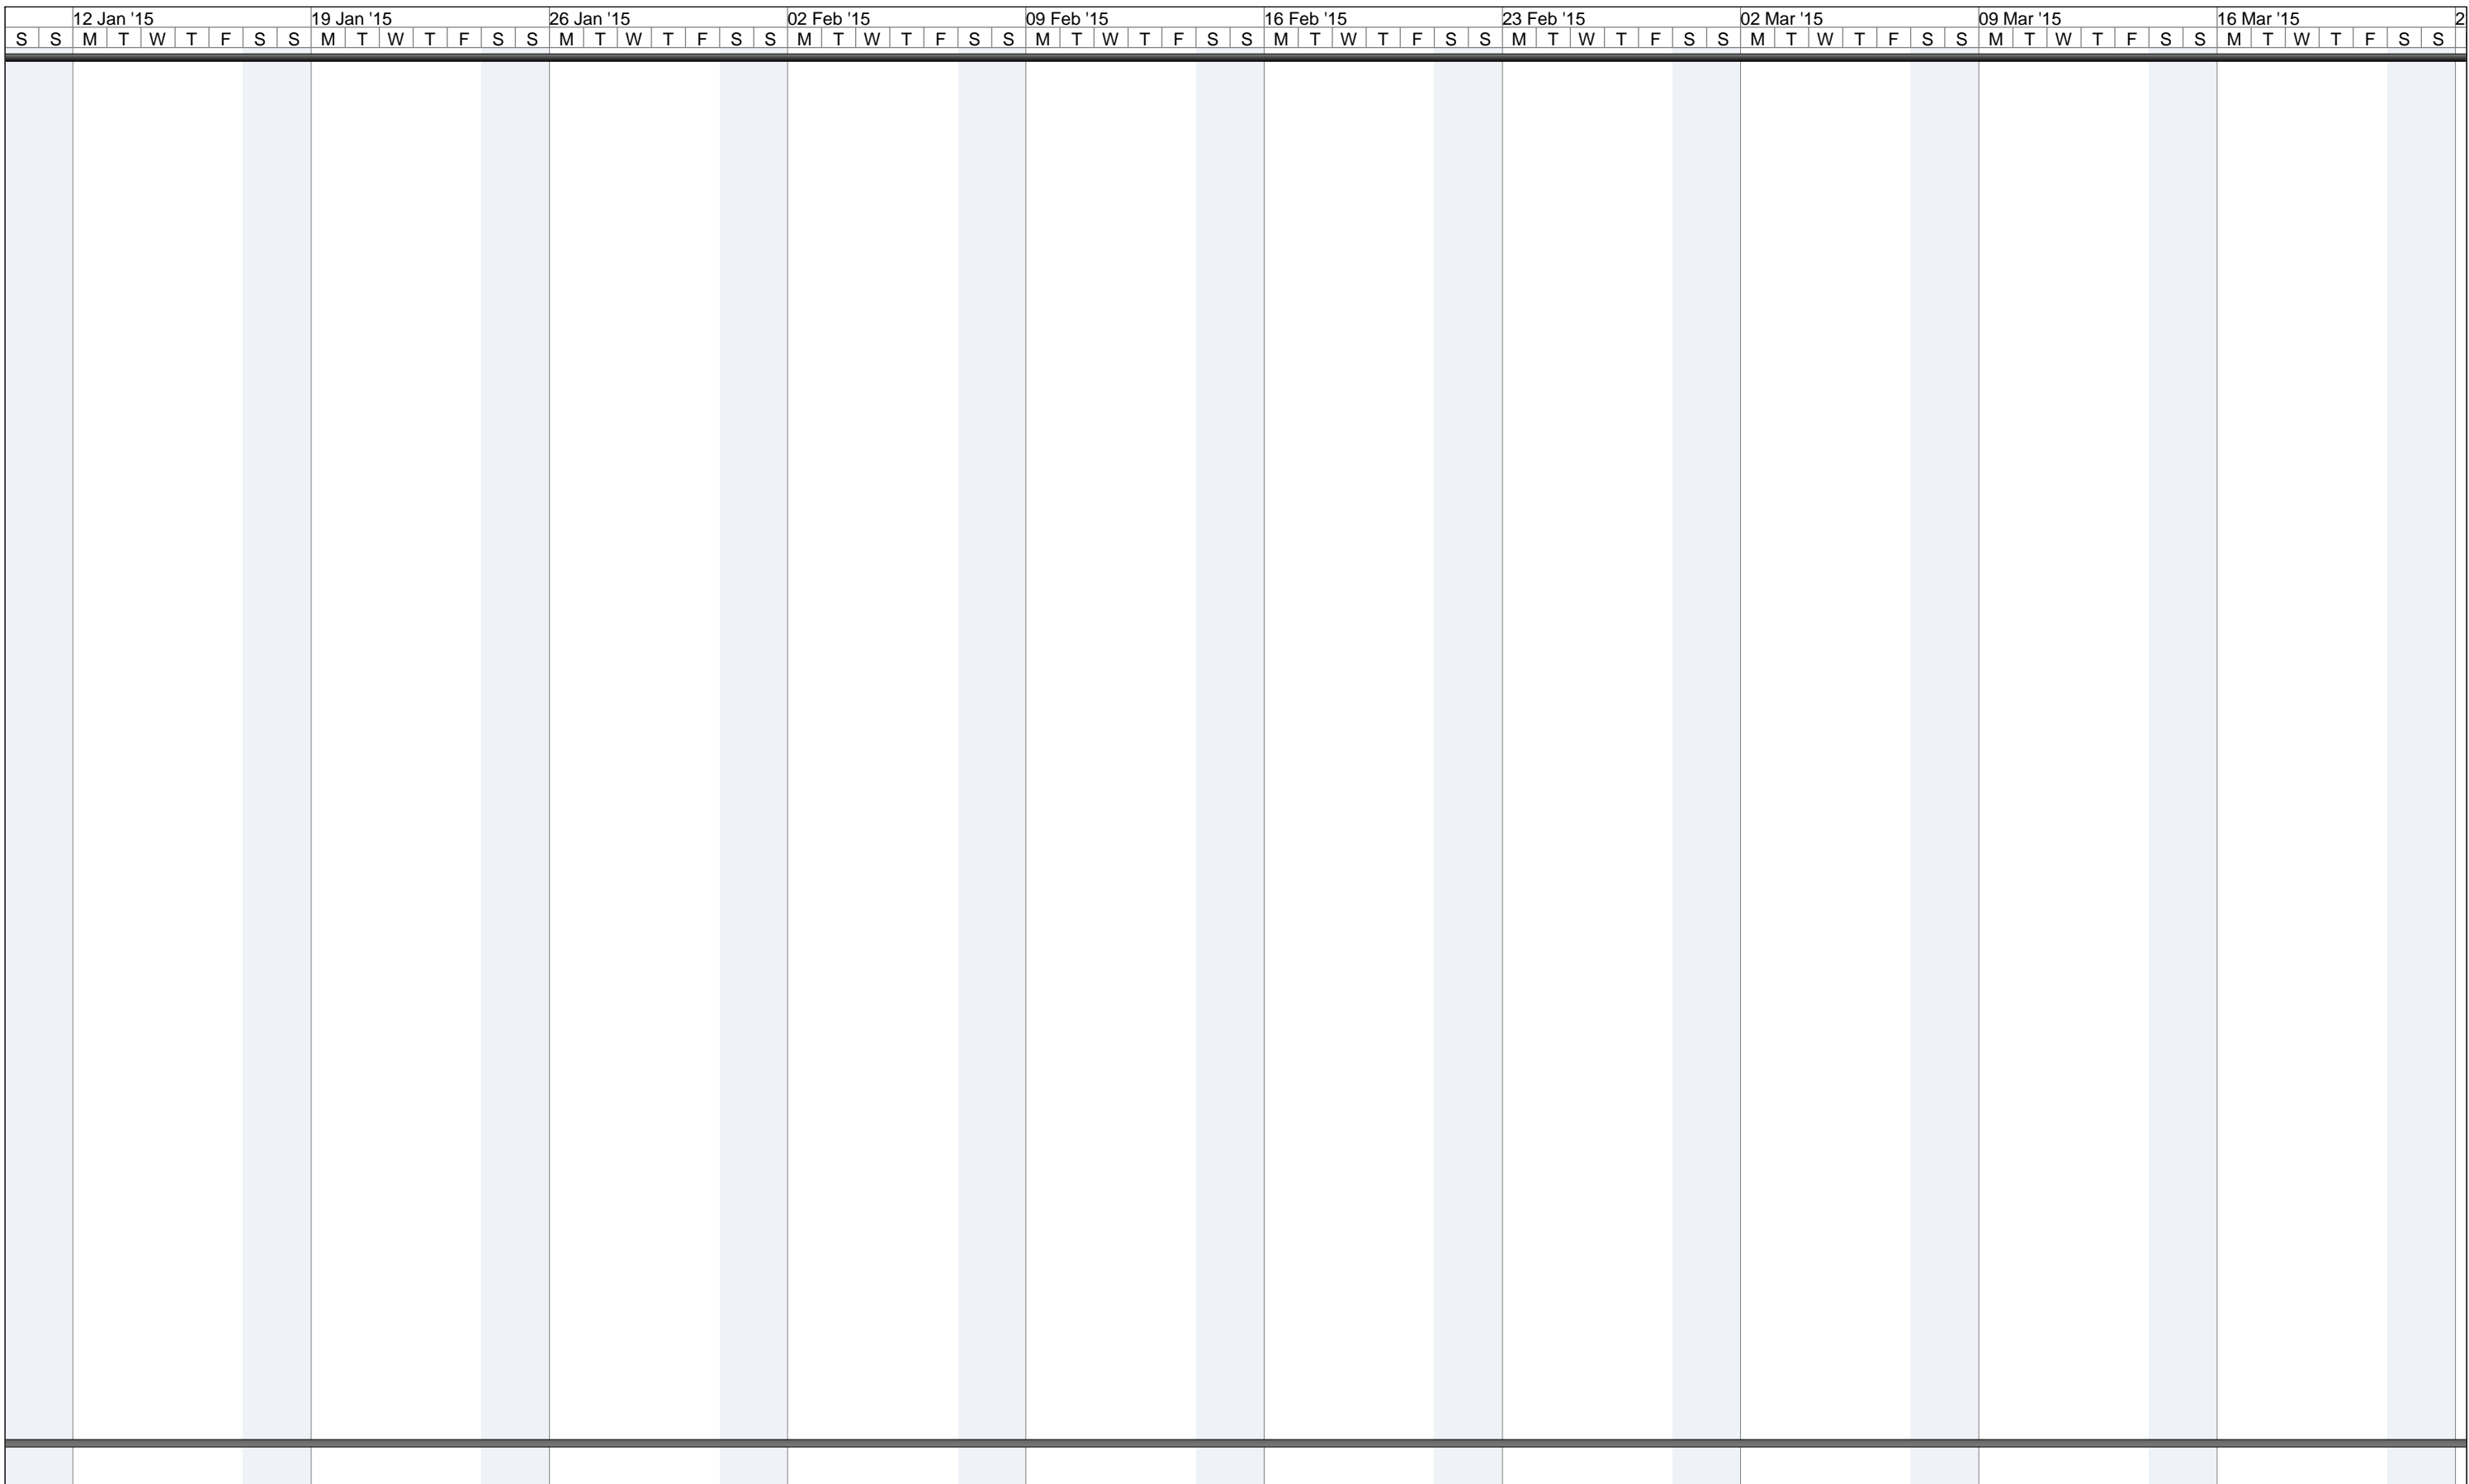

Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

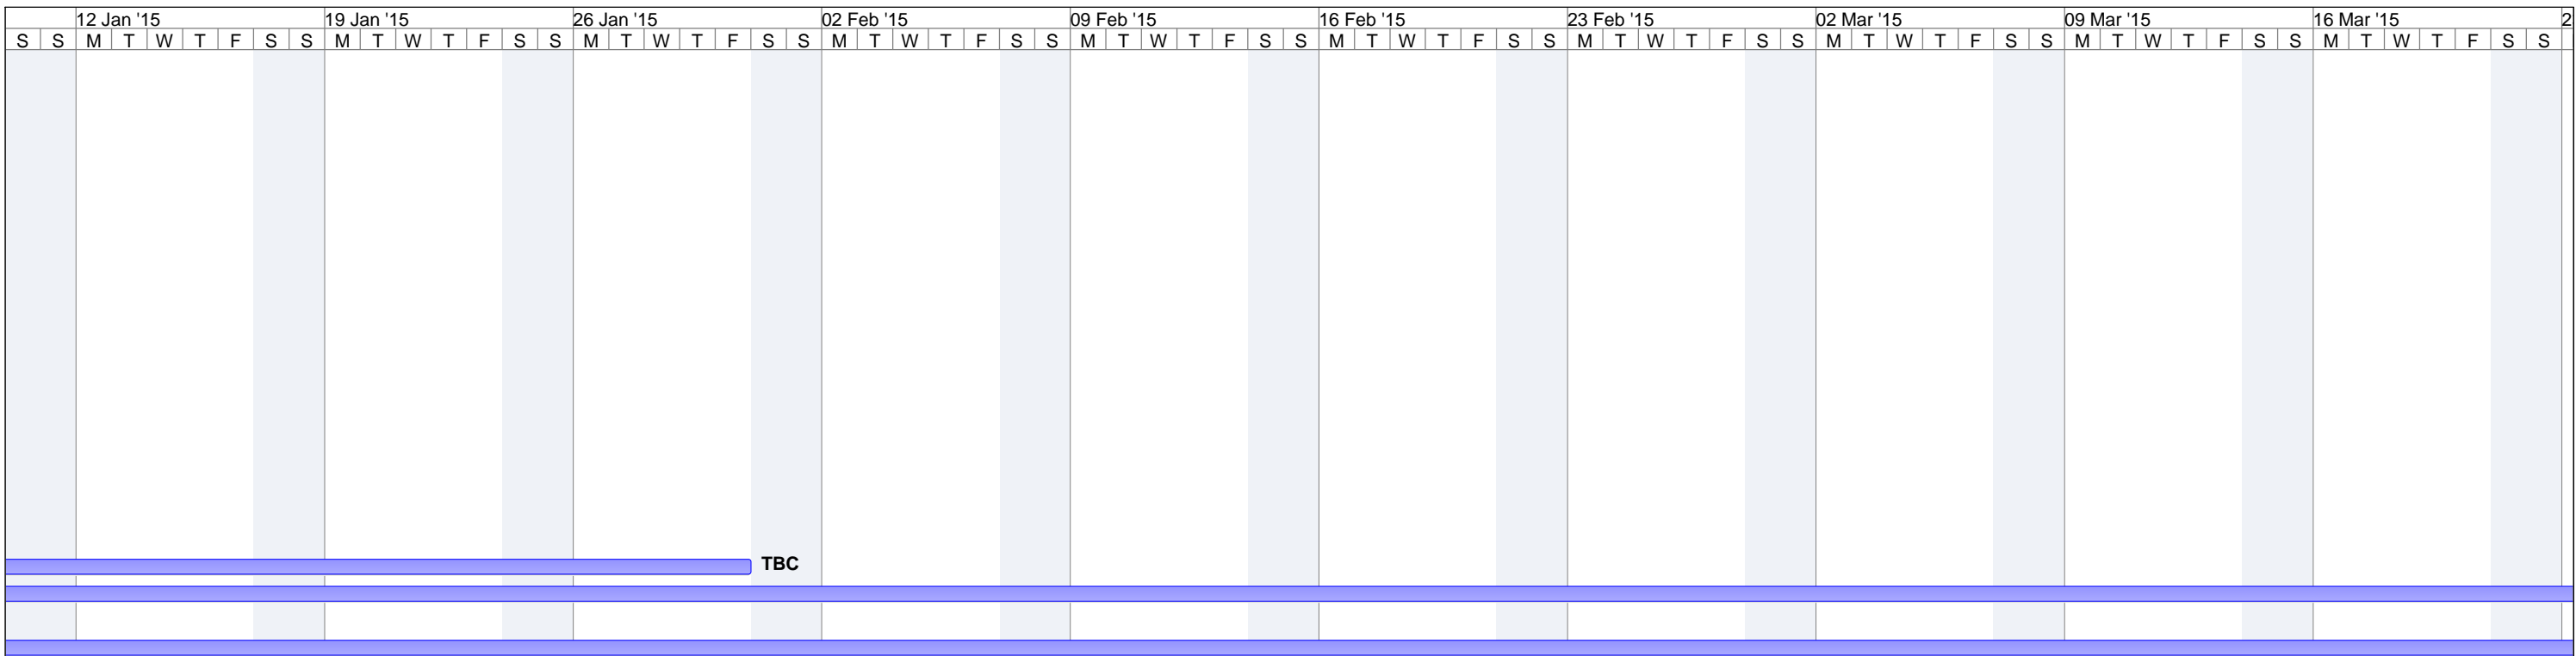


Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			



Project: Performance Assurance Plan  
Date: Mon 09/06/14


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

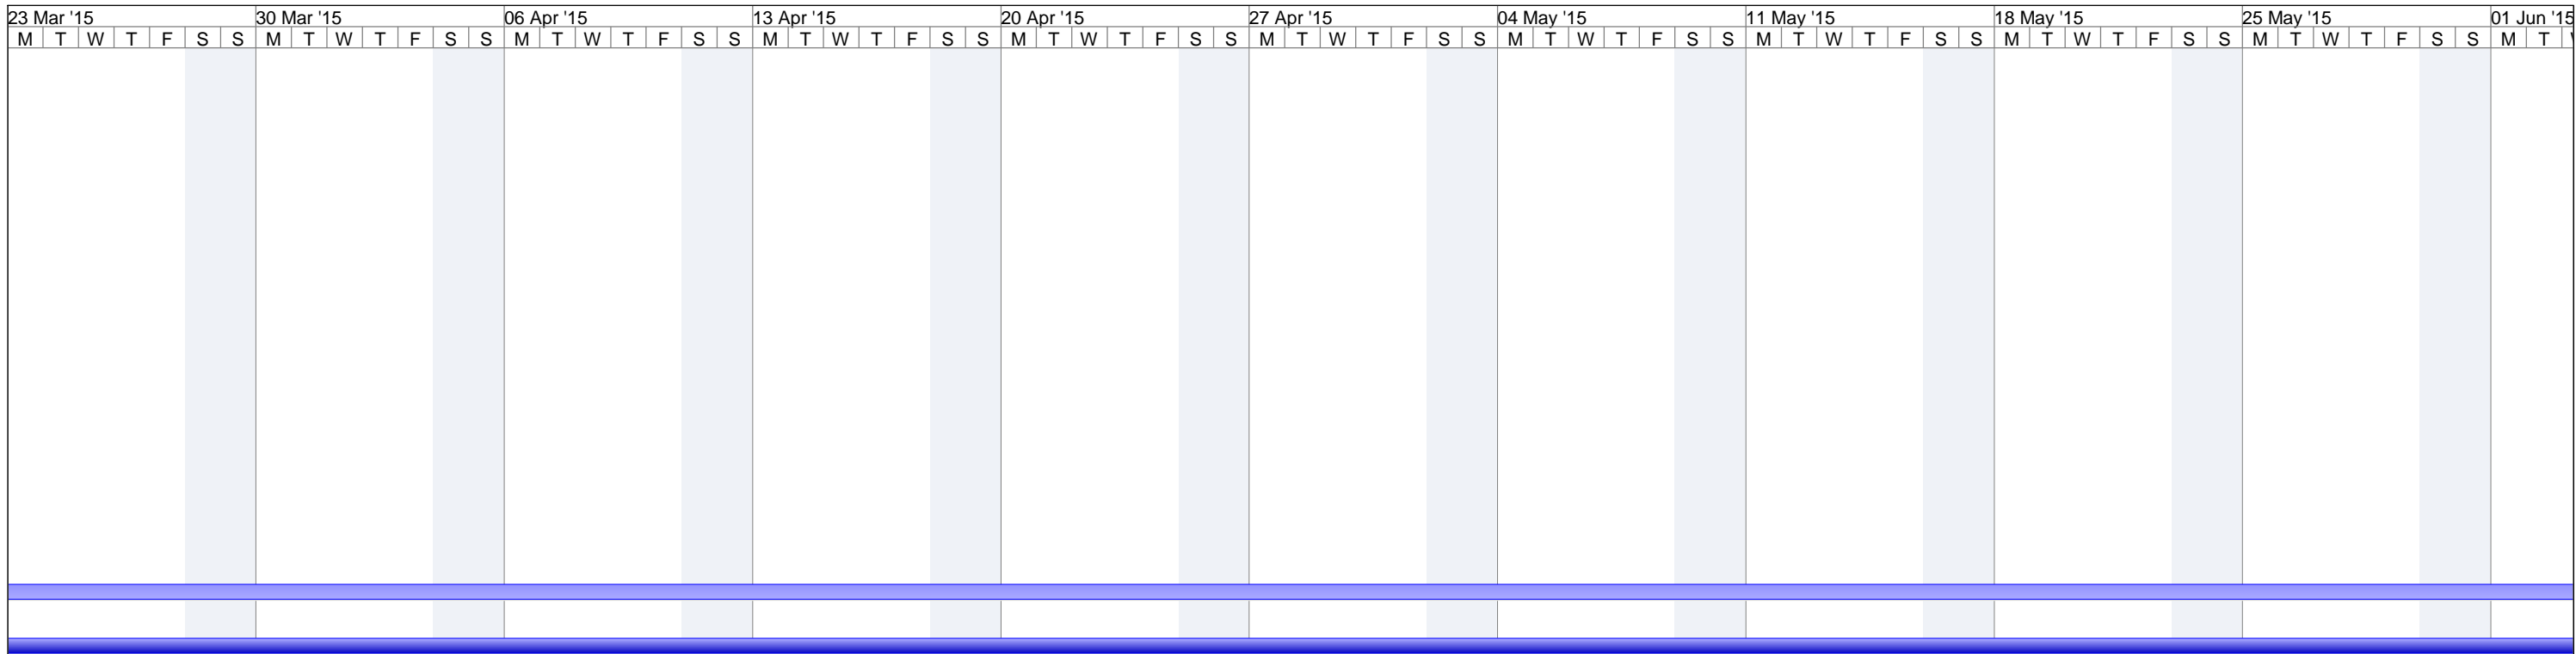

Project: Performance Assurance Plan  
Date: Mon 09/06/14



Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			



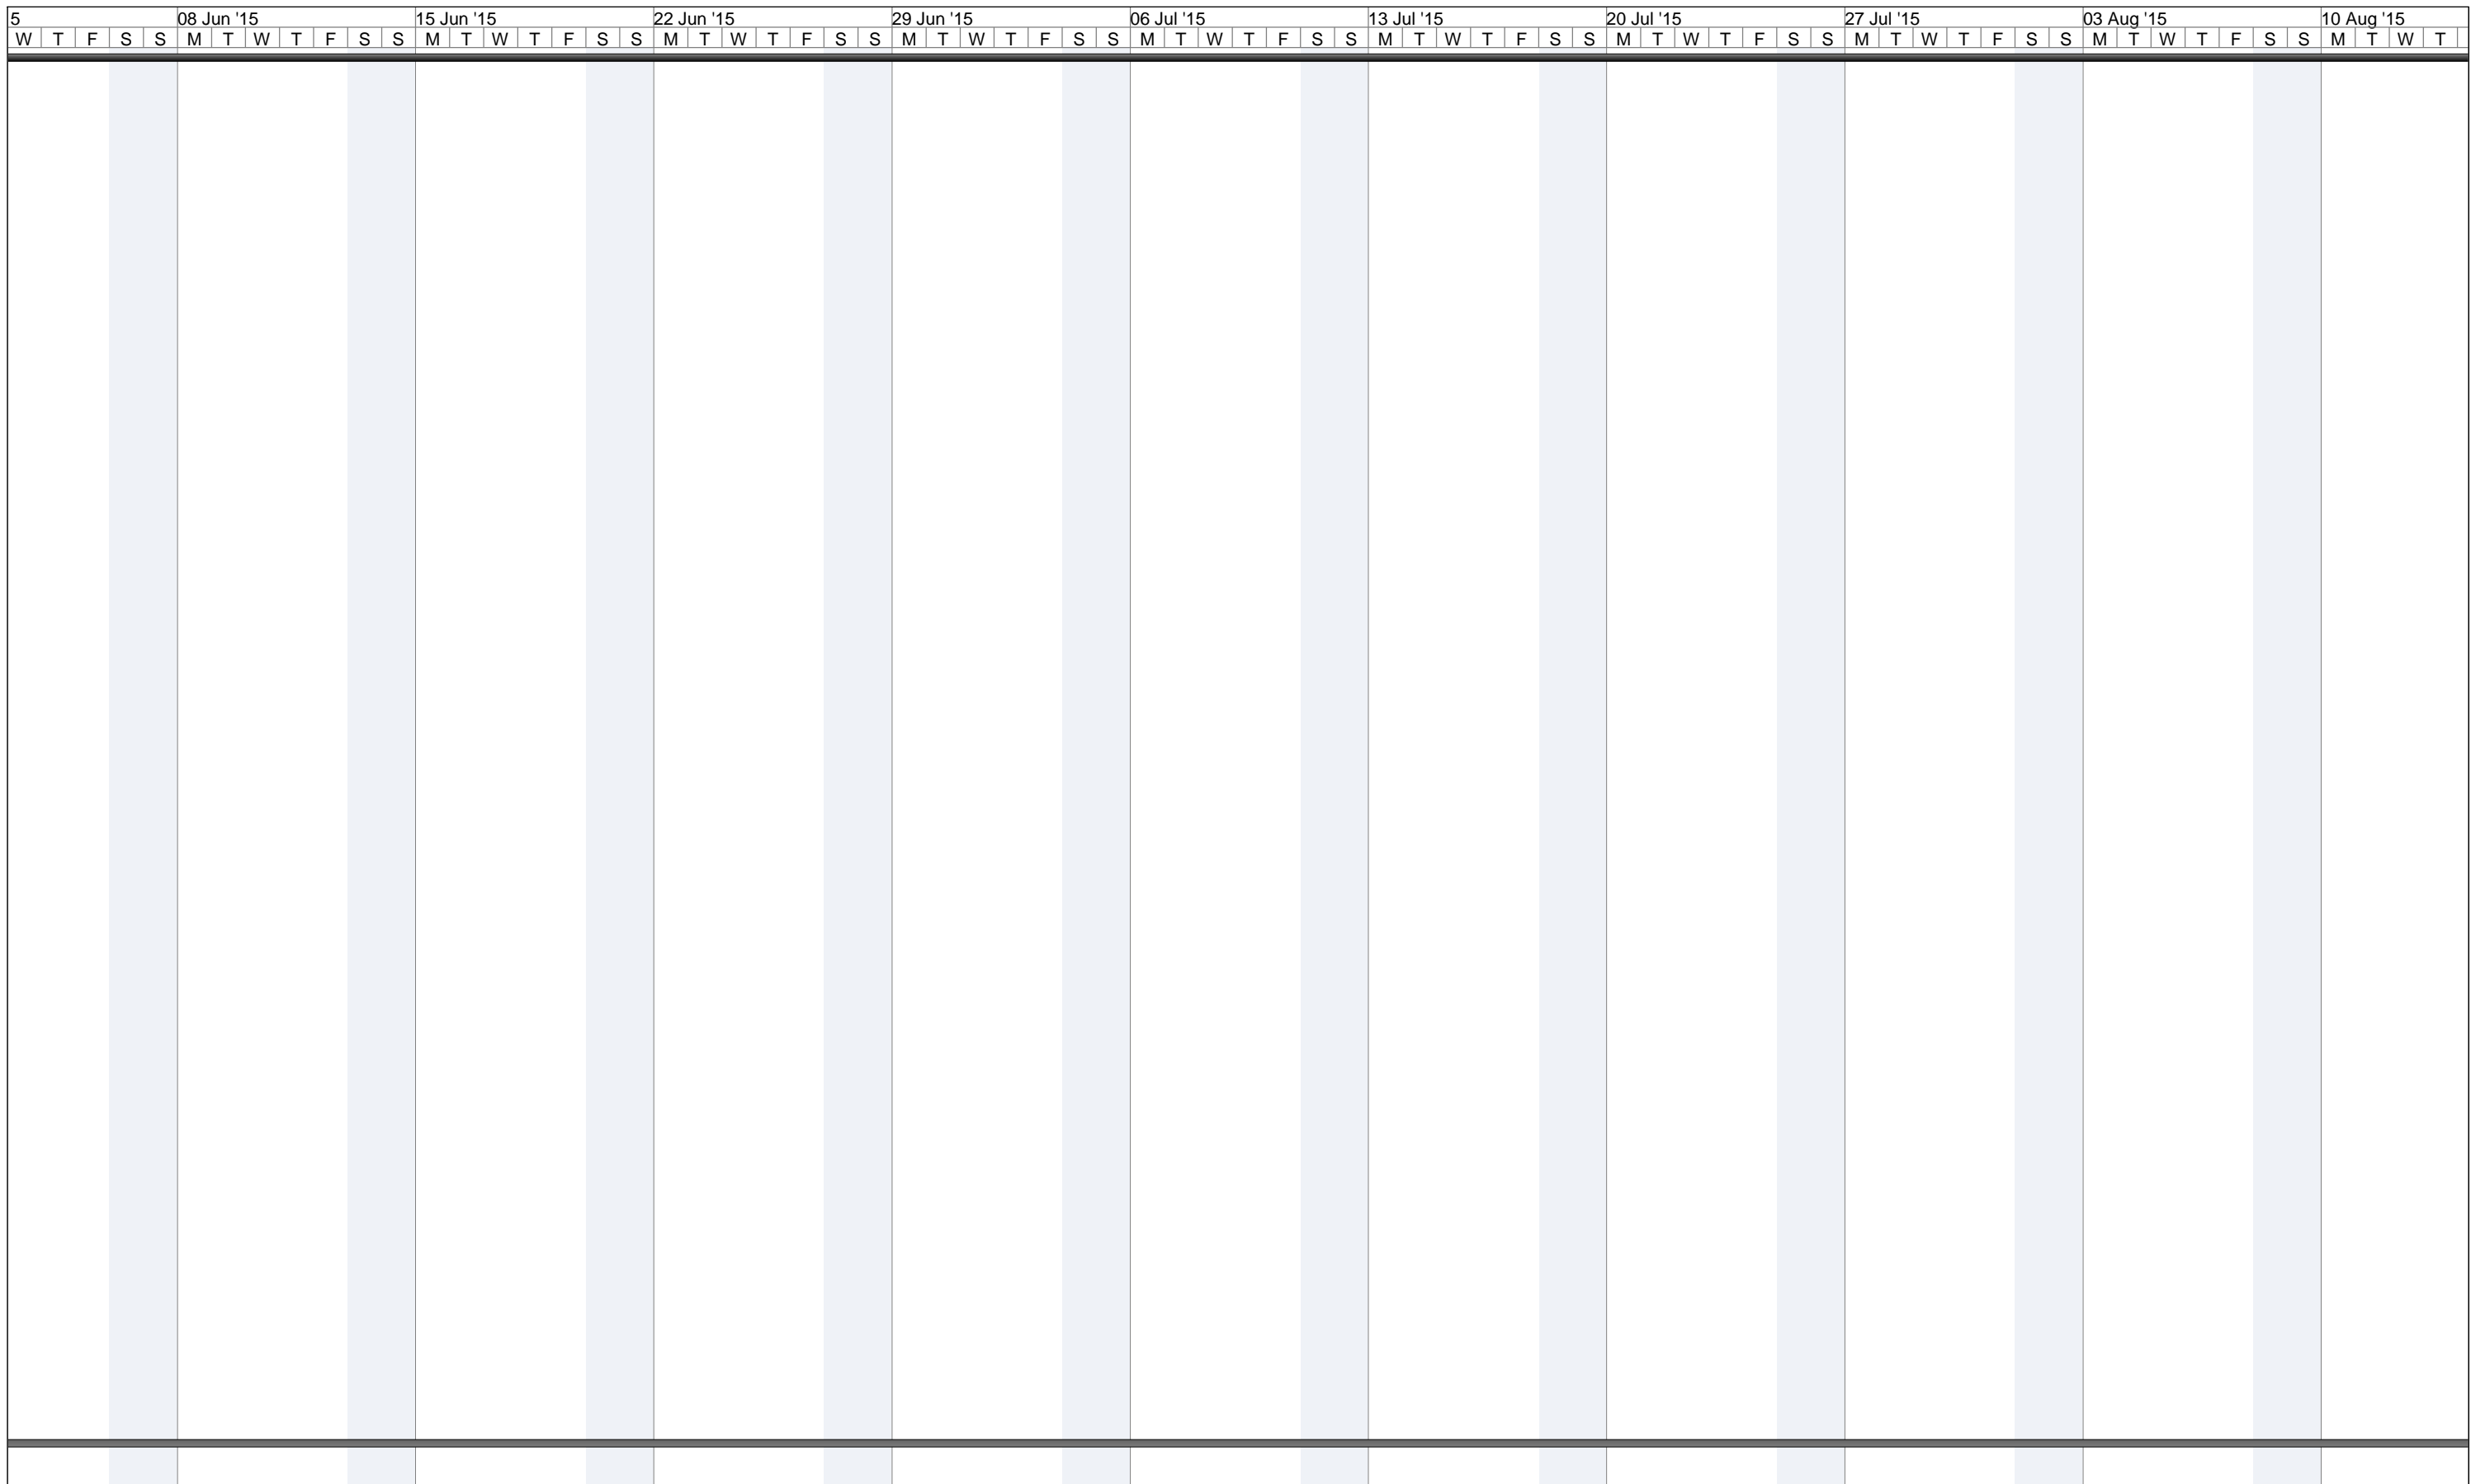

Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

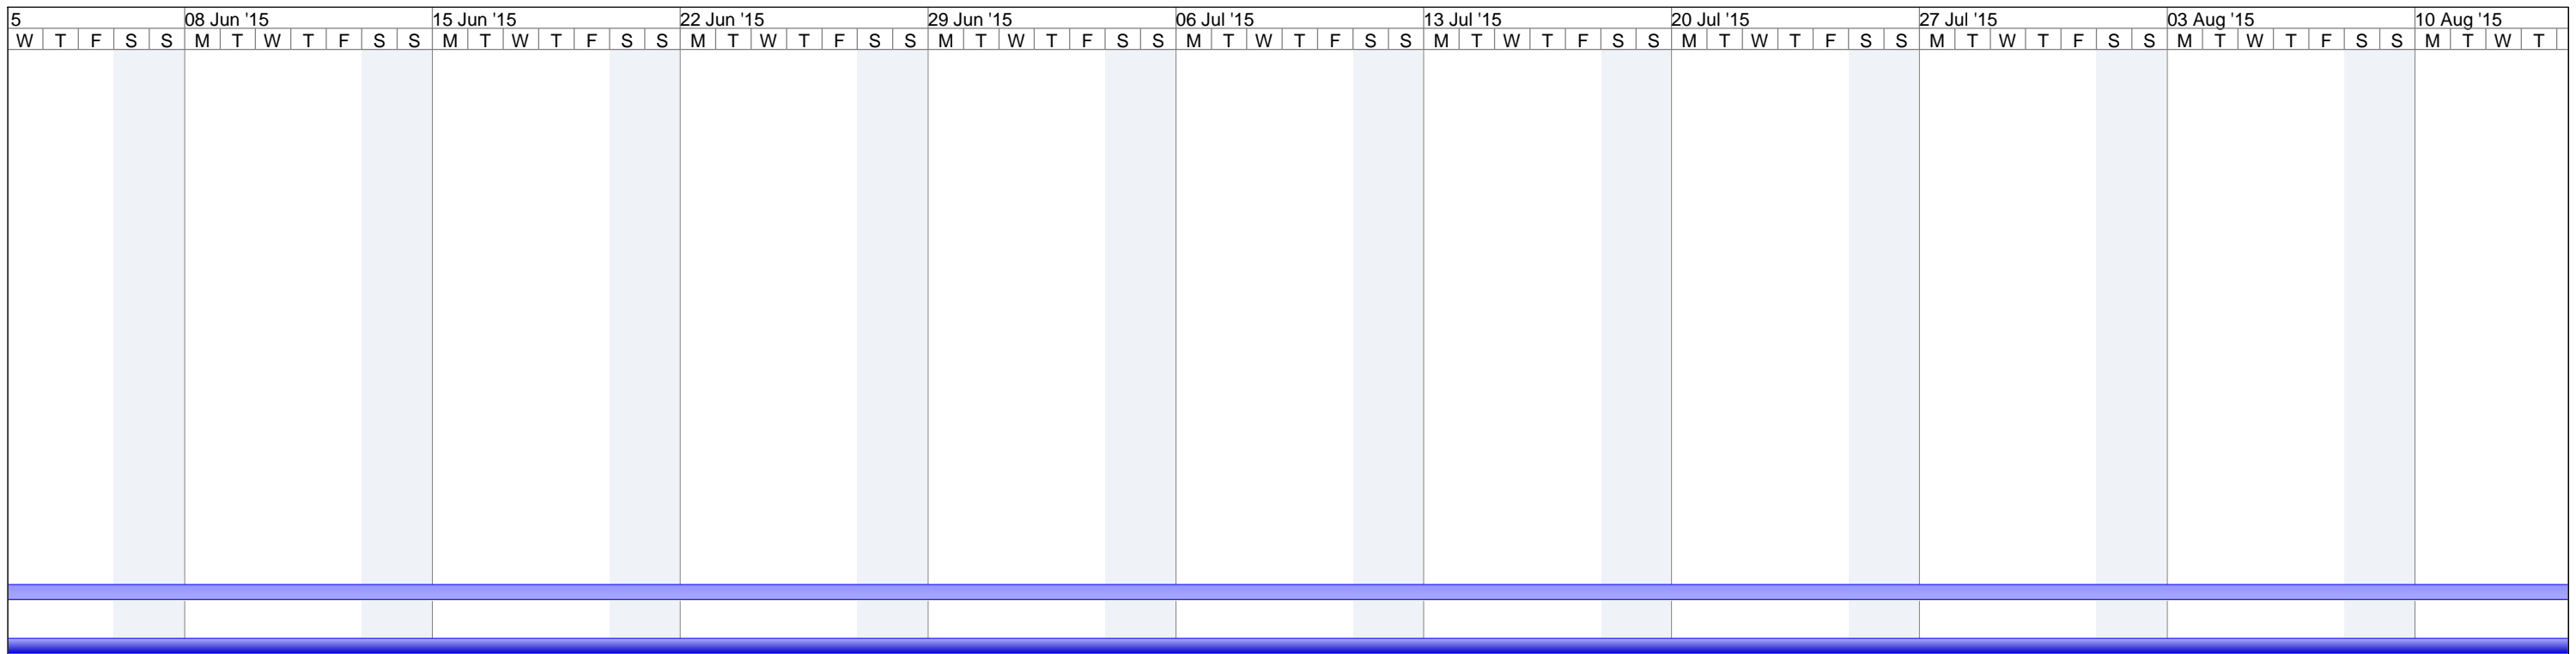


Project: Performance Assurance Plan Date: Mon 09/06/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			




Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

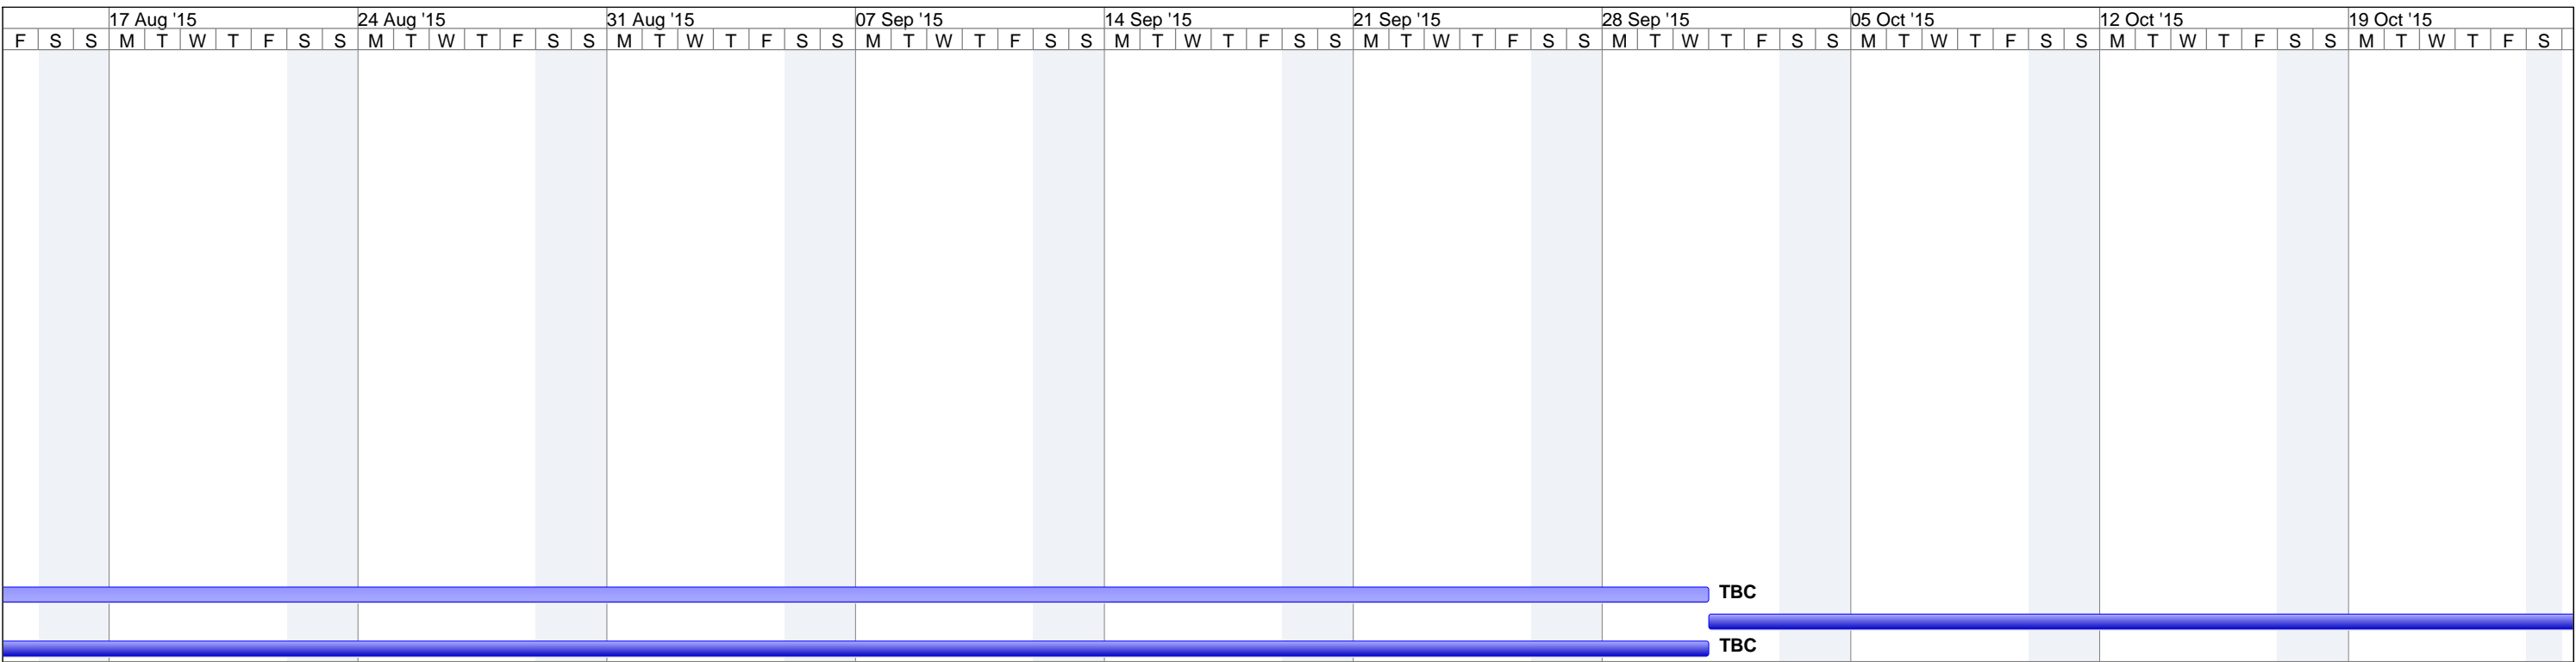


Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

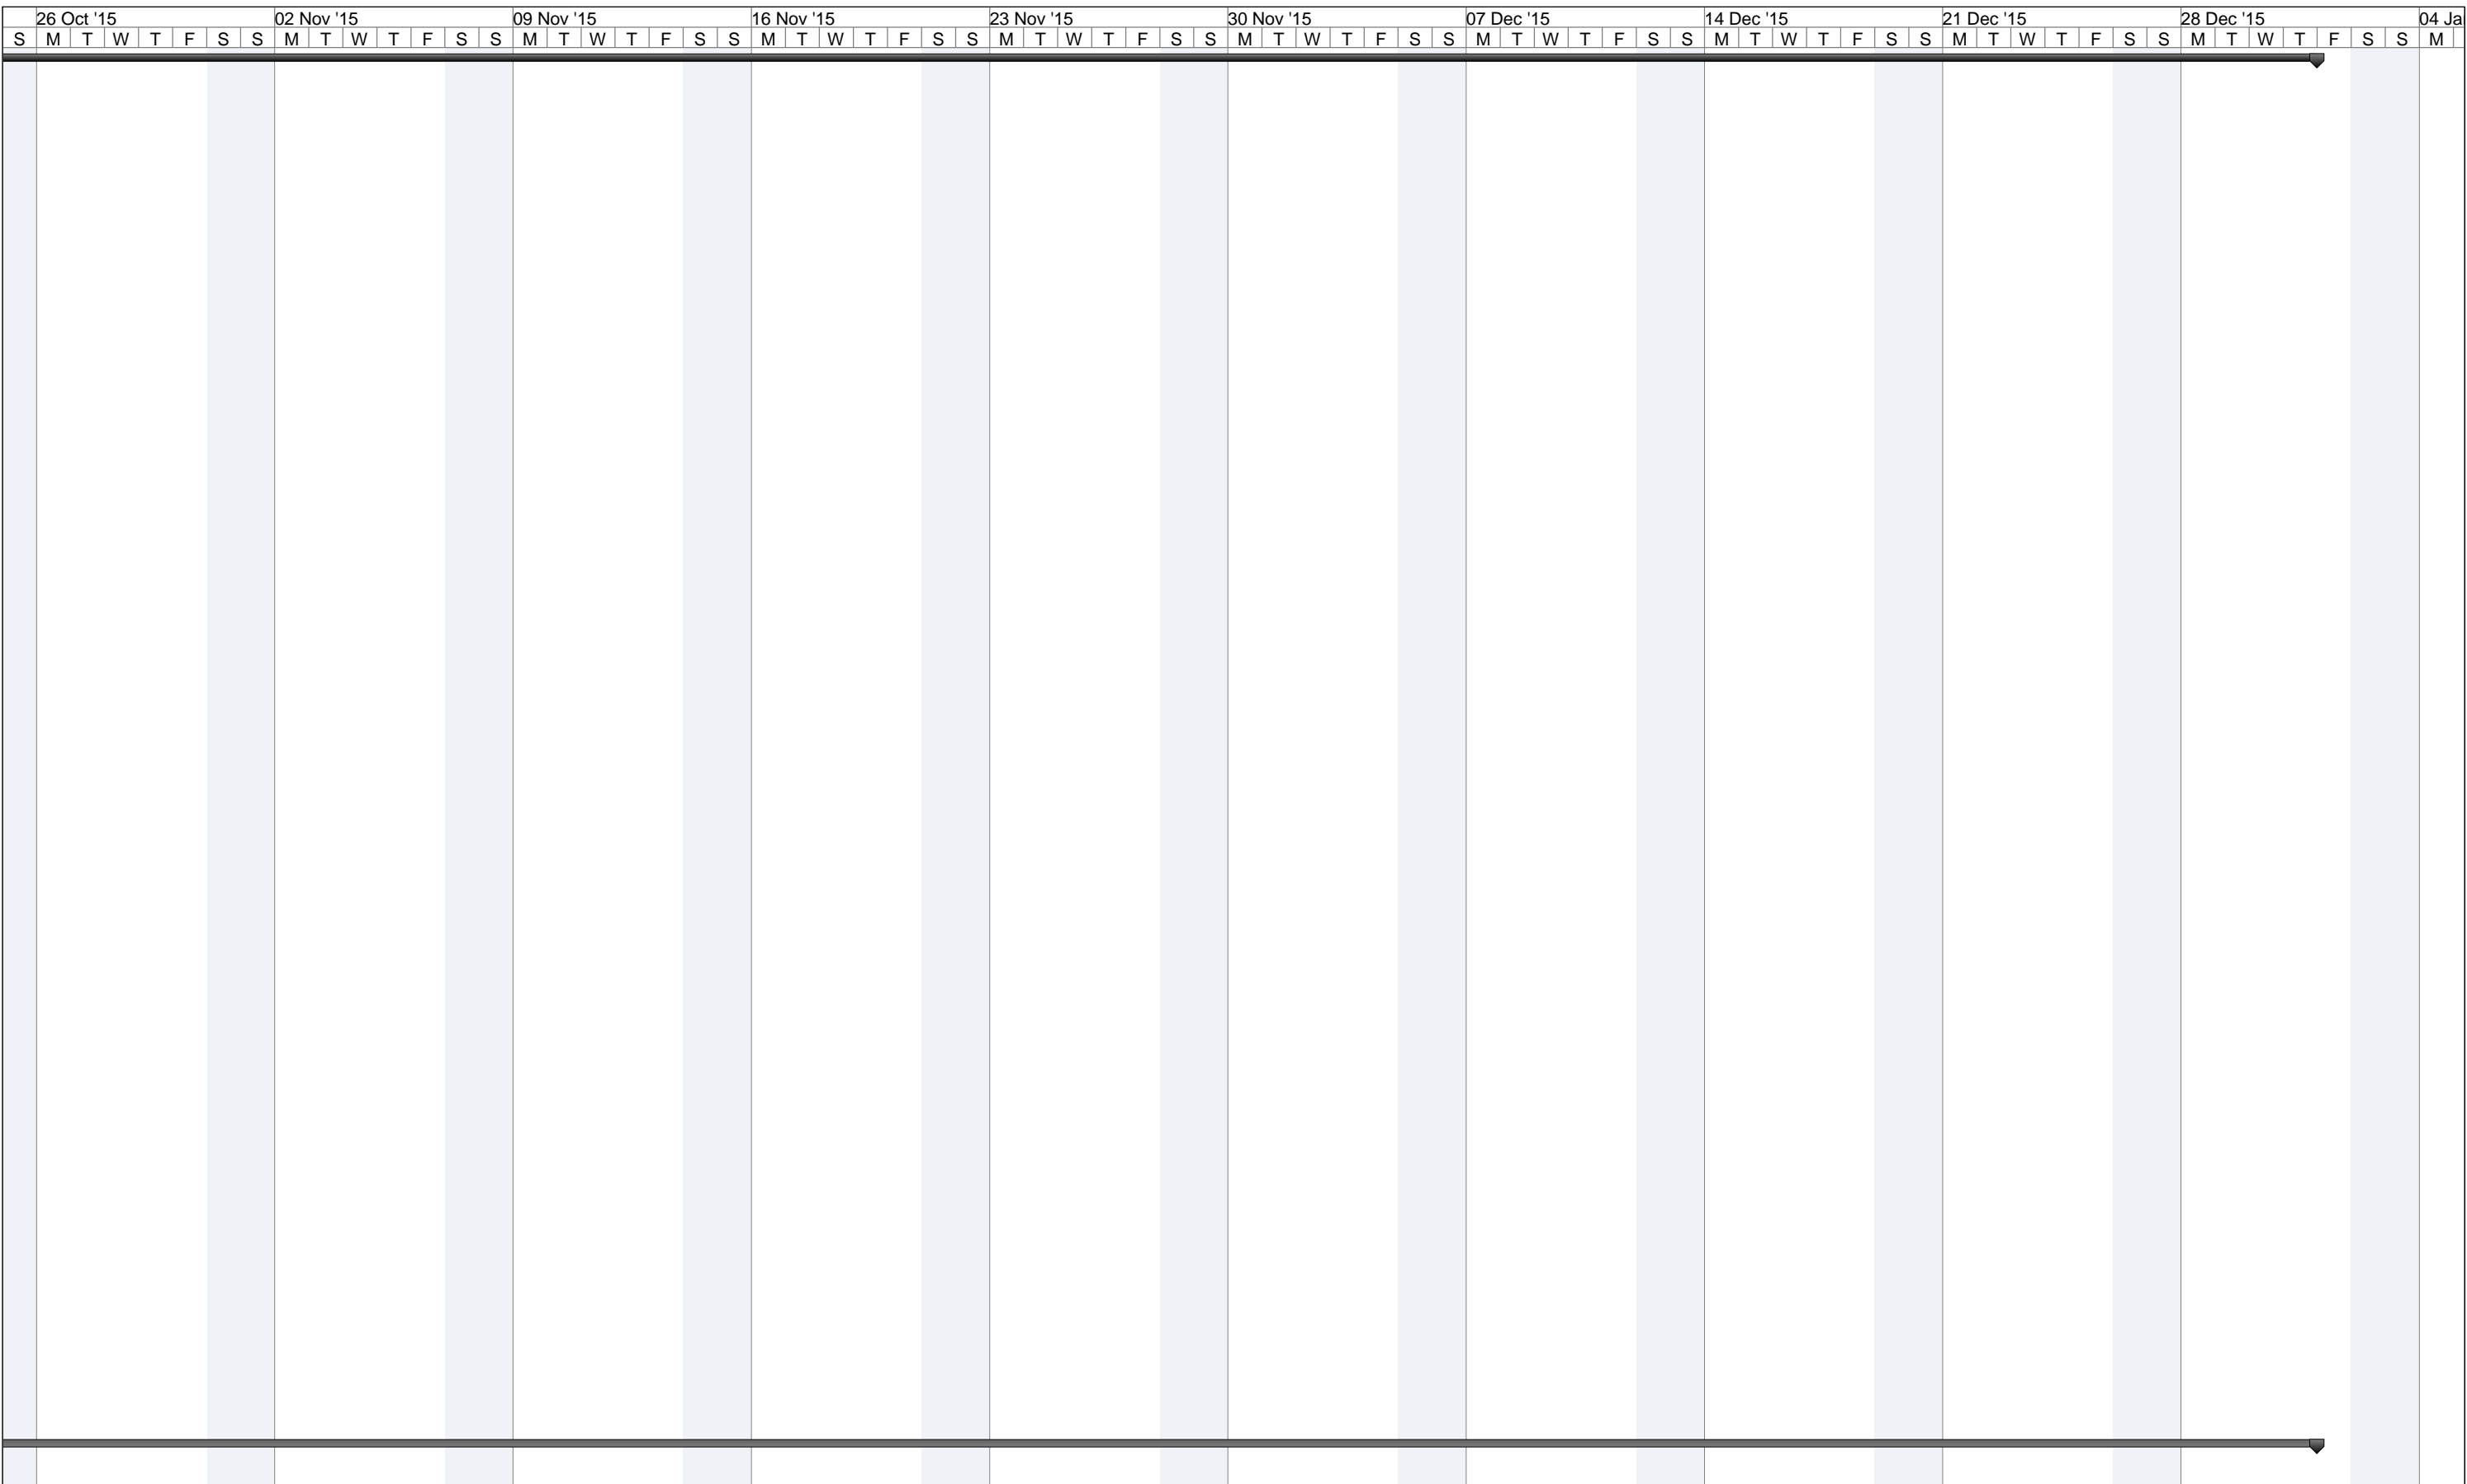

Project: Performance Assurance Plan  
 Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

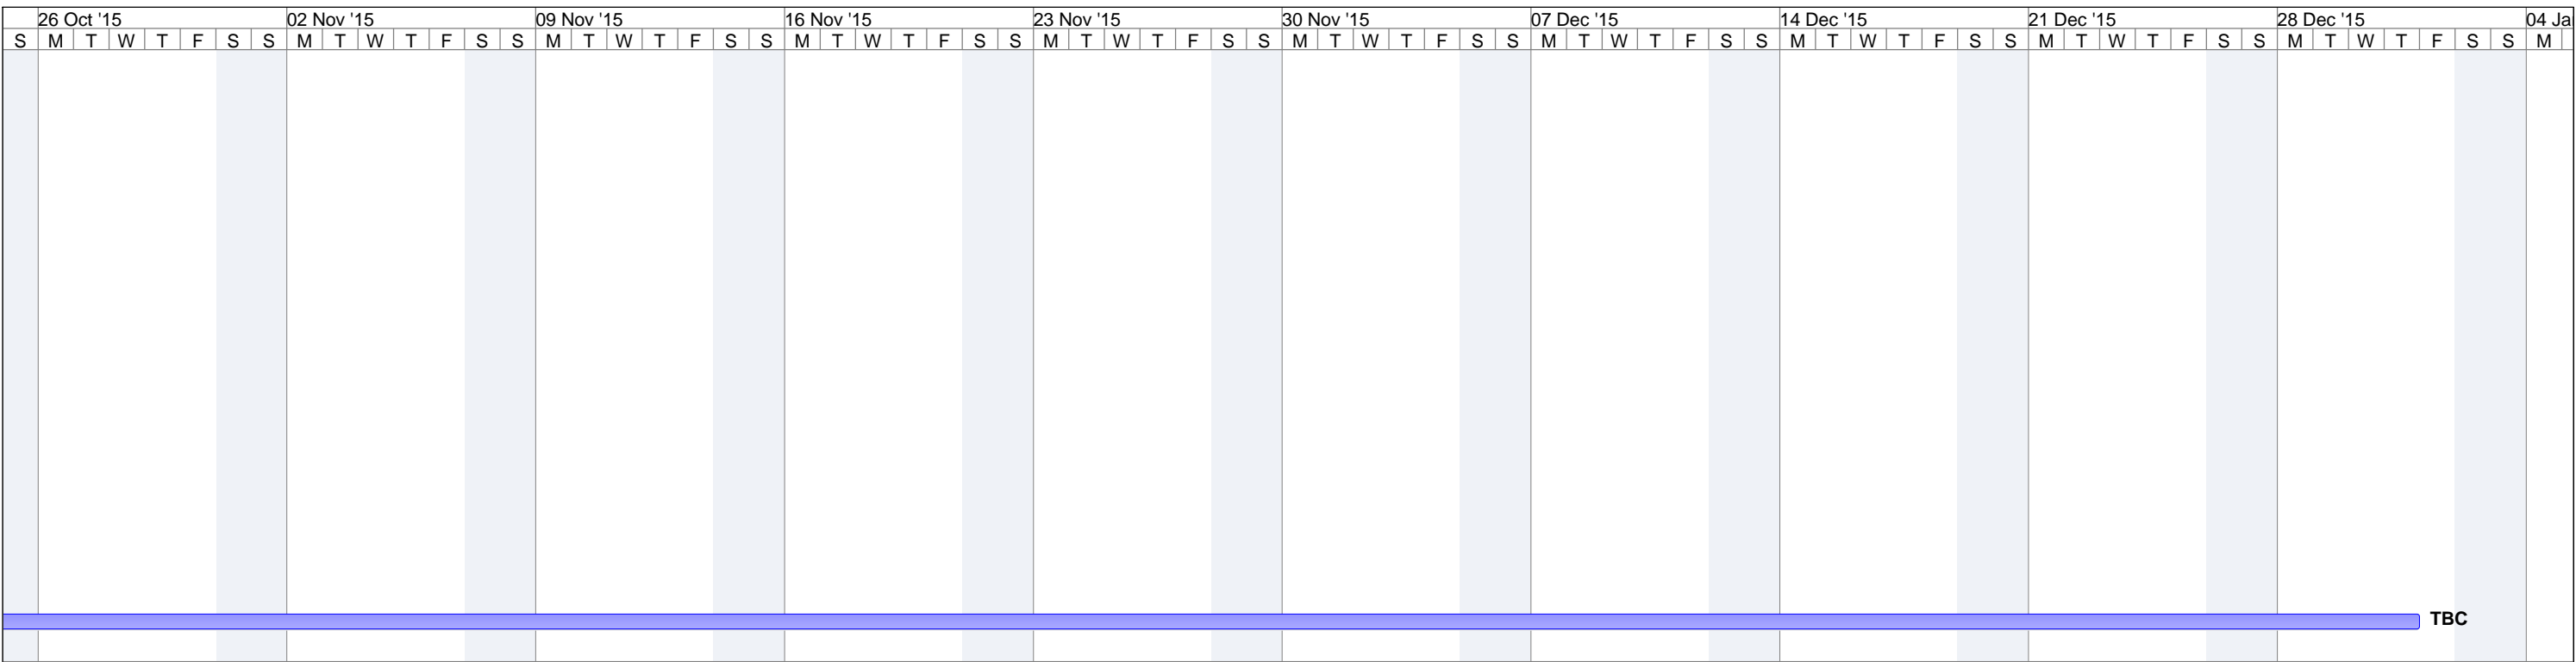

Project: Performance Assurance Plan  
Date: Mon 09/06/14

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
